


PROPOSED CONSTRUCTION ACTIVITIES ASSOCIATED WITH CONSTRUCTION SEQUENCING, PHASE 3

1. PRIOR TO THE COMMENCEMENT OF ANY WORK OR THE PLACEMENT OF EQUIPMENT ON THE ROADWAY THE CONTRACTOR SHALL PROVIDE ADVANCED WARNING SIGNS IN ACCORDANCE WITH THE CONSTRUCTION APPROACH SIGNING PLAN AND THE LATEST VERSION OF THE M.U.T.C.D. AND ITS REVISIONS.
2. INSTALL AND MAINTAIN ANY ADDITIONAL EROSION CONTROL MEASURES IN ACCORDANCE WITH THE EPSC PLANS AND DETAILS AND THE VERMONT D.E.C.'S "LOW RISK SITE HANDBOOK FOR EROSION PREVENTION AND SEDIMENT CONTROL."
3. SHIFT ROUTE 15 TRAFFIC TO PROPOSED ALIGNMENT NORTH OF THE EXISTING ROUNDABOUT. SUPPLY FLAGGERS TO MAINTAIN ONE WAY TRAFFIC THROUGH THE INTERSECTION.
4. INSTALL ALL WARNING SIGNS, REFLECTORIZED DRUMS, TRAFFIC BARRIER, AND ANY OTHER TRAFFIC CONTROL DEVICES PER ACCEPTED TRAFFIC CONTROL PLAN OR AS DIRECTED BY THE ENGINEER.
5. WIDEN NORTHEAST AND NORTHWEST QUADRANTS. BRING GRADE UP TO AND/OR ABOVE EXISTING STREET LIGHT FOUNDATION LEVEL.
6. REMOVE AND RECONSTRUCT SOUTHERN HALF OF ROUNDABOUT TRUCK APRON.

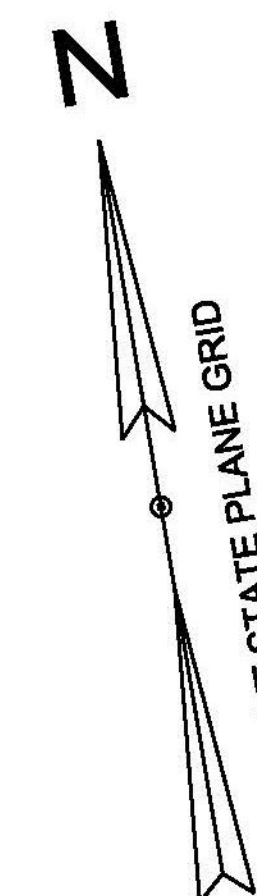

VT ROUTE 100 STA. 41+50.53  
END PROJECT  
HES 030-2(34)

CENTER OF ROUNDABOUT  
VT ROUTE 15 STA. 96+37.69 =  
VT ROUTE 100 STA. 40+00.00 (MM 0.00) =  
TH 5 STA. 63+59.48

VT ROUTE 15 STA. 94+80.66  
BEGIN PROJECT  
HES 030-2(34)

VT ROUTE 15 STA. 97+80.66  
END PROJECT  
HES 030-2(34)

T.H. 5 STA. 62+00.00  
BEGIN PROJECT  
HES 030-2(34)

**LEGEND**

 = WORK AREA



PROJECT NAME: HYDE PARK	PLOT DATE: 11/12/2015
PROJECT NUMBER: HES 030-2(34)	DRAWN BY: M. BOGACZYK
FILE NAME: t14b104+cp.dgn	CHECKED BY: M. LaCROIX
PROJECT LEADER: P. COBURN	SHEET 24 OF 26
DESIGNED BY: M. BOGACZYK	CONSTRUCTION SEQUENCING PLAN SHEET 3

