Route Log and Progress Chart

Please Note: Errors and Omissions May Exist. Contact the VTrans Mapping Section with questions or concerns.

Page Total Mileage: 1.590 mi


DRAFT

DISTRICT TOWN ROUTE MORRISTOWN ALT VT-100

Page Total Mileage: 1.59 mi





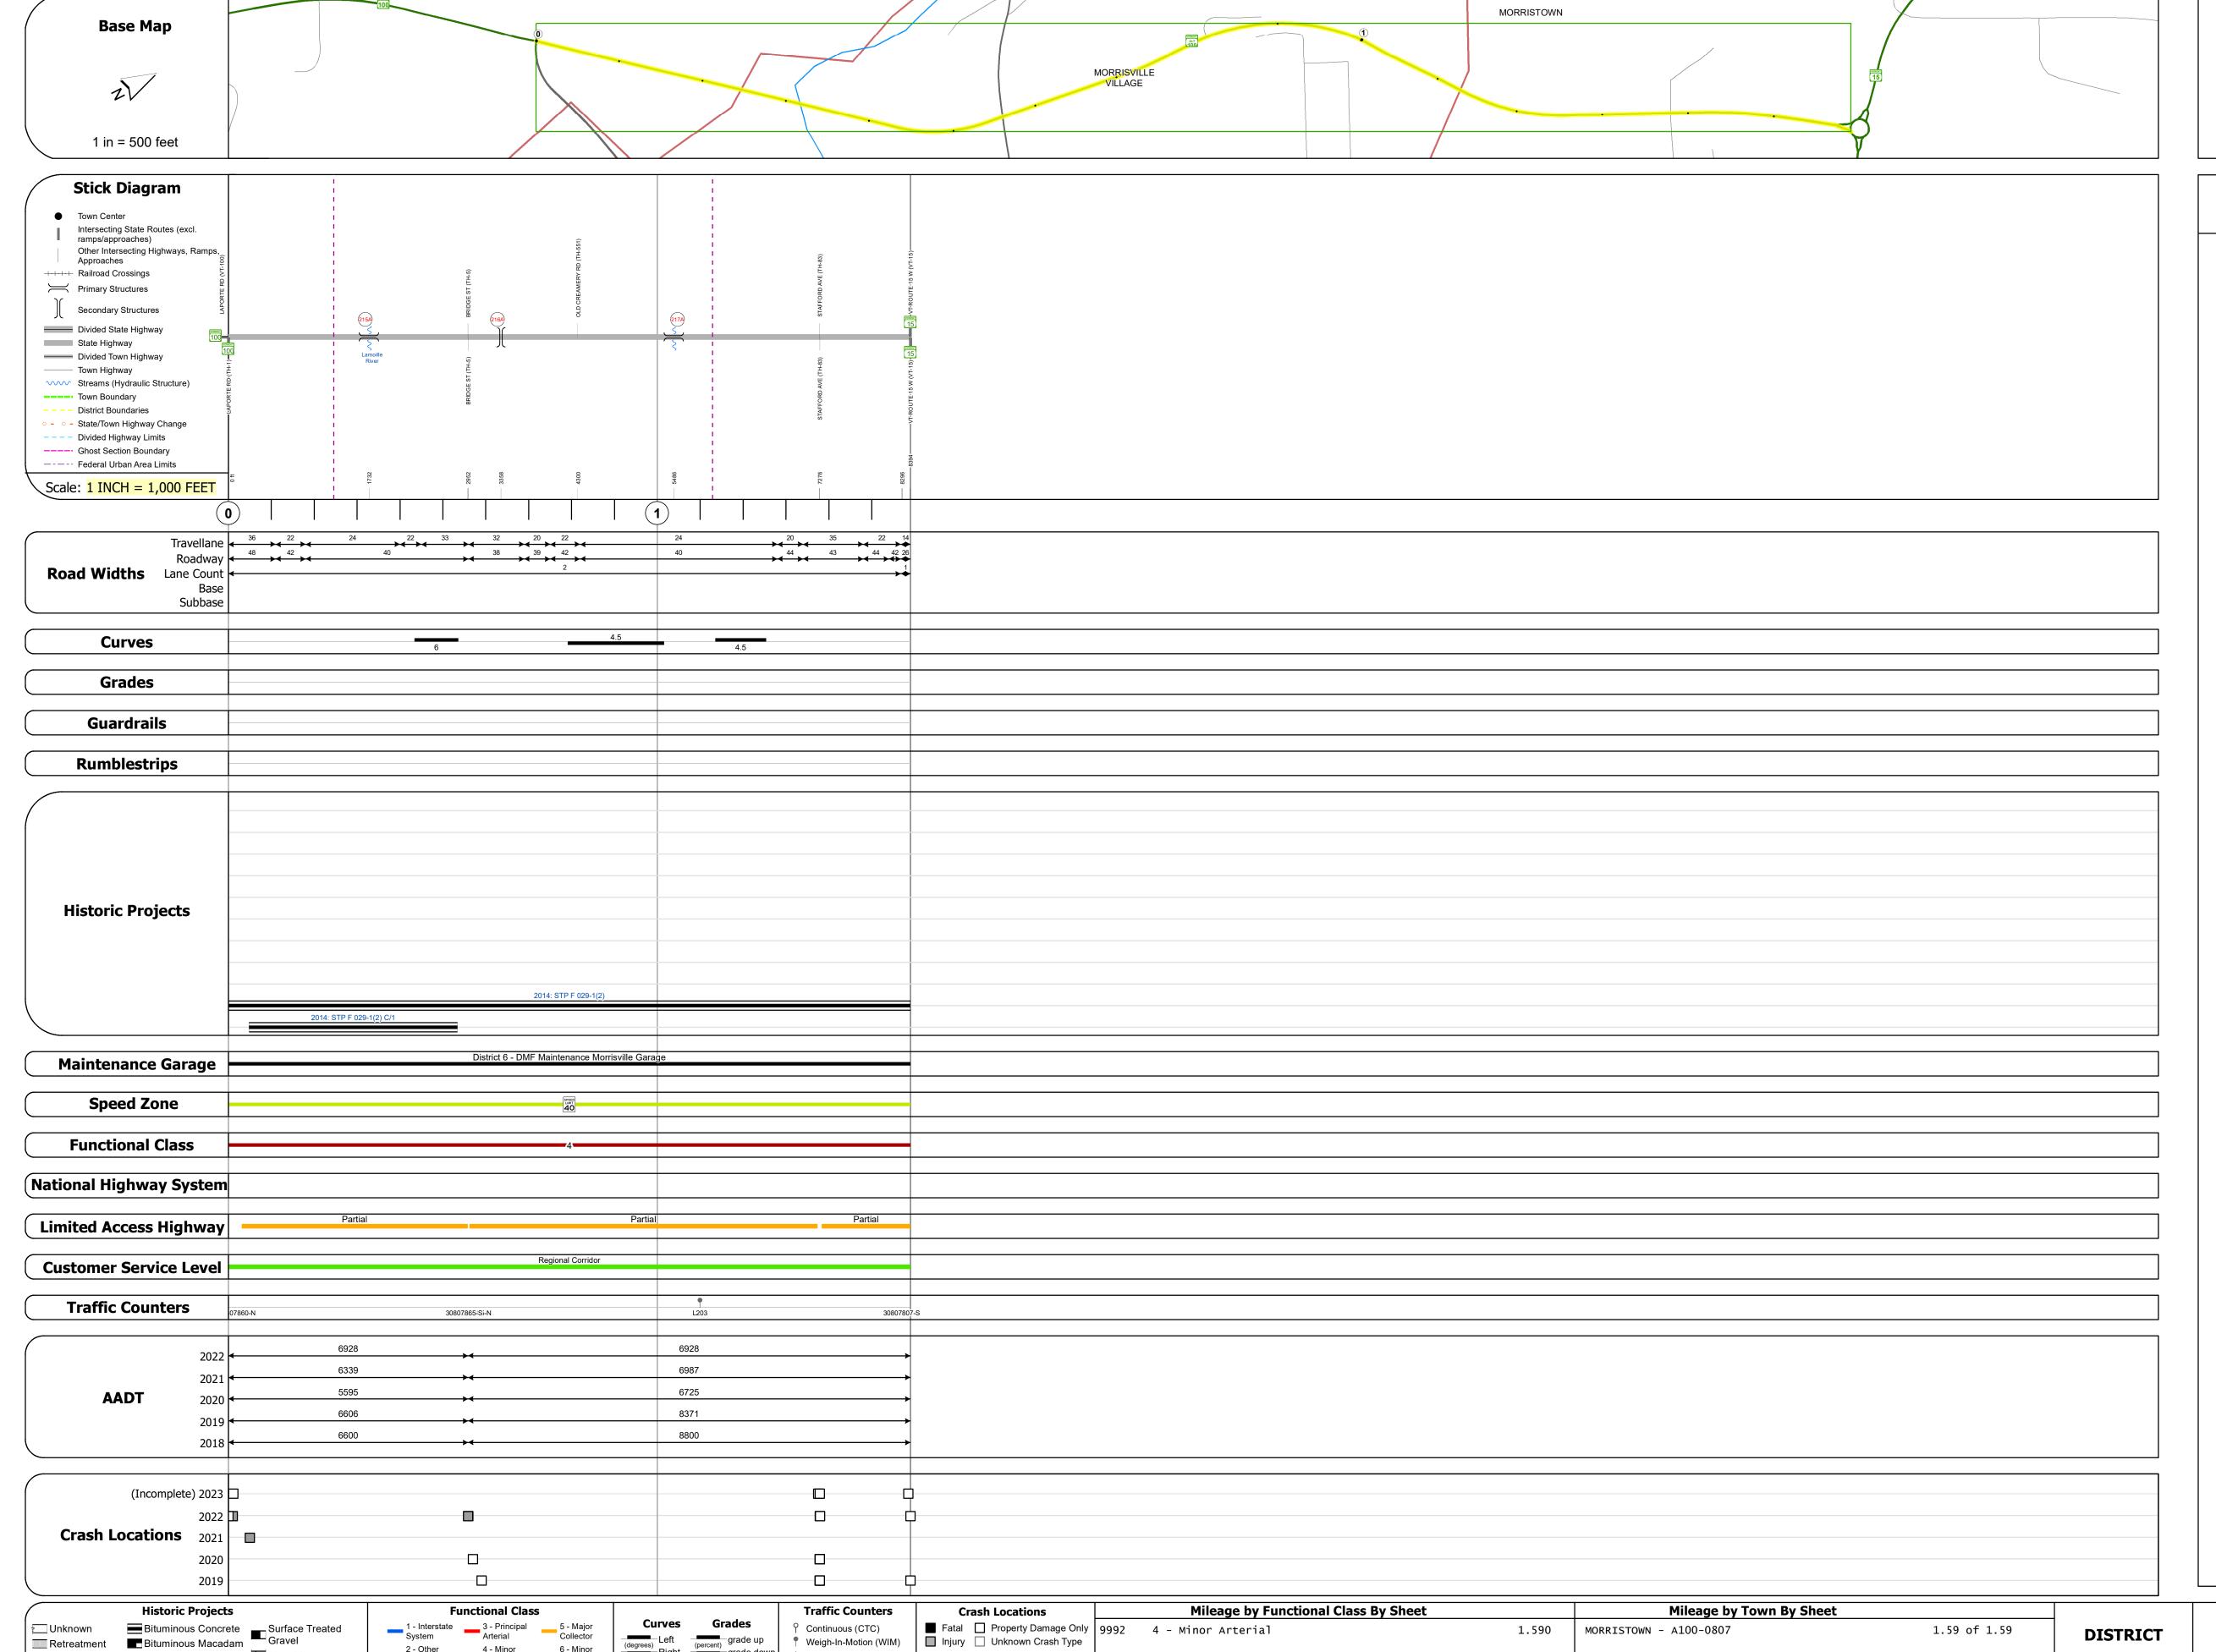

STRUCTURE DESCRIPTIONS

Bridge <mark>215A</mark>: Frame - 2014 Structure No. 200029215A08072 Length: 545' Height: 100.0' Width: 39.0' Weight Limit: 0 Facility Carried: ALT VT 00100 ML Structure Type: STEEL RIGID FRAME Features Intersected: LAMOILLE RIVER Surface: Bituminous Inspection Date: 8/2021 Maintenance/Ownership: State

Bridge 216A: Truss - thru - 2014 Structure No. 200029216A08072 Length: 183' Under Clearance: 1911.0' Weight Limit: 0 Facility Carried: ALT VT 00100 ML Structure Type: GALV PONY TRUSS Features Intersected: VT 100 UNDER PED. BRIDGE

Bridge 217A: Culvert - 2013 Structure No. 300290217A08071 Length: 11' Under Clearance: 7.0' Weight Limit: 0 Facility Carried: ALT VT100 Structure Type: SEGMENTAL RC BOX Features Intersected: BROOK Inspection Date: 11/2022 Maintenance: State

2 - Other 4 - Minor Freeways and Arterial

Cold Plane and
Bituminous Concrete
Bituminous Concrete
Bituminous Concrete
Bituminous Concrete

■ Bituminous Mix

Skinny Mix Concrete

ःः Bituminous Seal **L** Gravel

Left (percent) grade up

High Crash Locations (HCL's)

HCL No. 201 - 300 (21 - 30)

1 - 100 (1 - 10) 301 - 400 (31 - 40)

Sections (& Intersections)

▲ Short-Term, Scheduled

△ Short-Term, Unscheduled
