


Ellen Kennel
 Director of Finance and Administration
 or Duty Authorized Agent

1/18/01
 Date


Scott's Construction Inc. 704 S.C.I. Camp
 Contractor
[Signature]
 Signature
 1/18/01
 Date

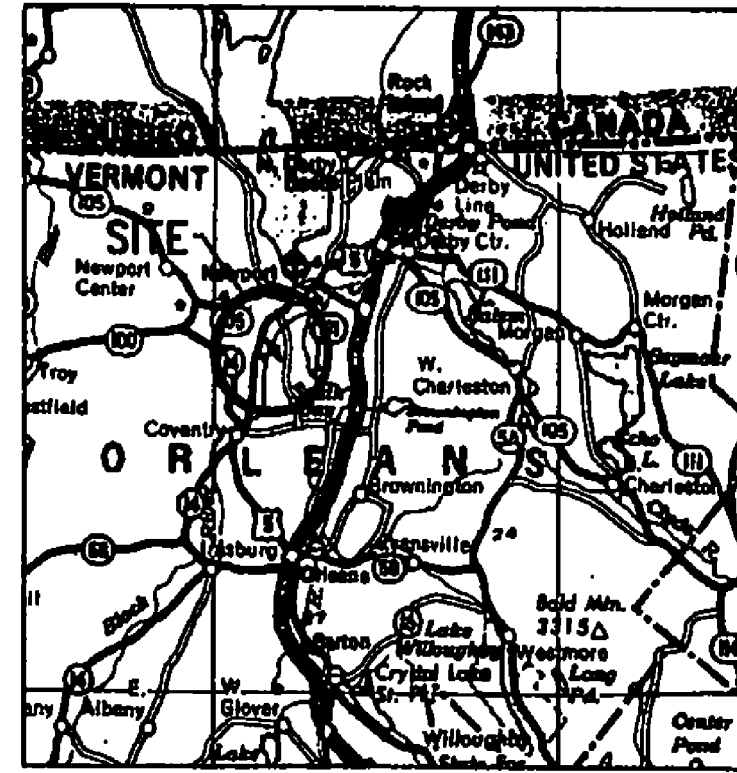

LOCATION MAP
 APPROX. SCALE: 1" = 5 MILES

CONTRACT PLANS
 THESE PLANS DO NOT REFLECT
 CHANGES MADE ON THE PROJECT.

NEWPORT STATE AIRPORT COVENTRY, VERMONT RECONSTRUCTION OF RUNWAY 18-36 , INSTALLATION OF RUNWAY AND TAXIWAY LIGHTS AND INSTALLATION OF AIRFIELD SIGNS

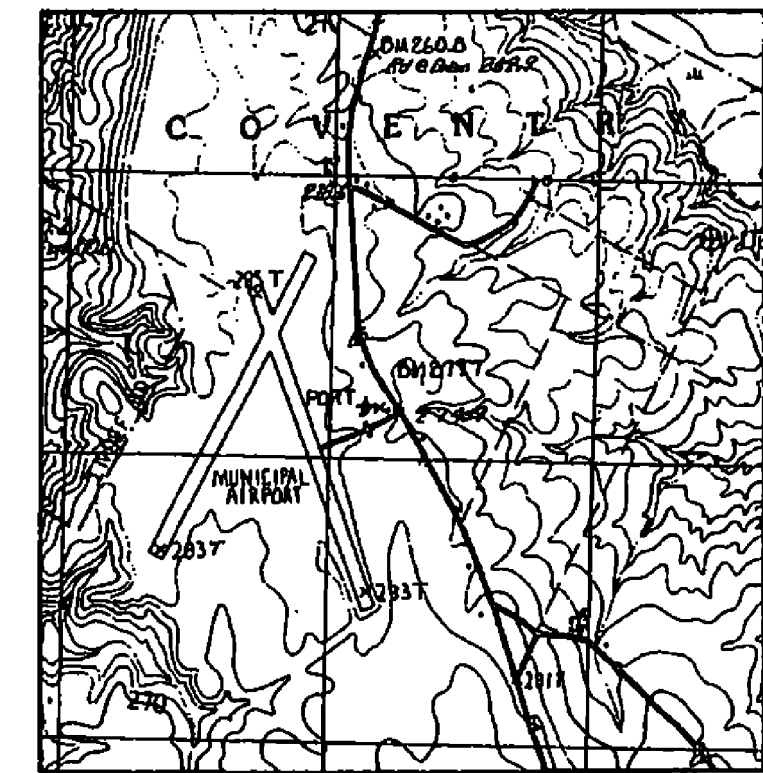

VICINITY MAP
 APPROX. SCALE: 1"=2000'

AIP NO. 3-50-0013-04
 EA NO. 043142

SUMMARY OF AIP QUANTITIES

VAOT ITEM#	DESCRIPTION	UNIT	QUANTITIES	
			EST.	AS BUILT
201.10	CLEARING & GRUBBING (PLUS INDIVIDUAL TREES AND STUMPS)	L.S.	1	
203.15	EXCAVATION	C.Y.	4,200	
204.20	TRENCH EXCAVATION OF EARTH	C.Y.	12,600	
301.35	SUBBASE OF DENSE GRADED CRUSHED STONE(MOD)(P-154)	C.Y.	3,700	
404.45	TAR EMULSION (MOD)(P-603)	GAL	8,900	
406.50	PRICE ADJUSTMENT ASPHALT CEMENT (N.A.B.)	L.S.	1	
601.0805	12" REINFORCED CONCRETE PIPE, TYPE III	LF.	1,750	
601.0815	18" REINFORCED CONCRETE PIPE, TYPE III	LF.	850	
601.0825	24" REINFORCED CONCRETE PIPE, TYPE IV	LF.	2,700	
602.15	CEMENT RUBBLE MASONRY HEADWALL	C.Y.	9	
604.10	CONCRETE CATCH BASIN W/CAST IRON GRATE	EACH	18	
604.11	CONCRETE MANHOLE W/CAST IRON COVER	EACH	2	
604.21	PRECAST REINFORCED CONCRETE MANHOLE WITH CAST IRON COVER (MOD) (D-752)	EACH	1	
604.40	CHANGING ELEVATIONS OF D.I.CB OR MH	EACH	3	
605.10	6" PERFORATED UNDERDRAIN	LF.	10,500	
605.20	6" UNDERDRAIN CARRIER PIPE	LF.	150	
605.90	UNDERDRAIN RISER	EACH	28	
605.95	UNDERDRAIN FLUSHING BASIN	EACH	28	
613.16	RIPRAP LIGHT TYPE	C.Y.	100	
631.10	FIELD OFFICE - ENGINEERS	L.S.	1	
631.16	TESTING EQUIPMENT - CONCRETE	L.S.	1	
631.17	TESTING EQUIPMENT - BITUMINOUS	L.S.	1	
631.25	FIELD OFFICE TELEPHONE (N.A.B.)	L.U.	1	
635.10	MOBILIZATION	L.S.	1	
636.20	UTILITY VAULT (MOD) (L-120)	L.S.	1	

SUMMARY OF AIP QUANTITIES

VAOT ITEM#	DESCRIPTION	UNIT	QUANTITIES	
			EST.	AS BUILT
649.51	COBTEXTILE FOR SILT FENCE	S.Y.	110	
651.15	SEED	LB	500	
651.25	HAY MULCH	TON	25	
651.29	HAY BALES FOR EROSION CONTROL	EACH	400	
651.35	TOPSOIL	C.Y.	1,500	
678.23	WIRED CONDUIT (1") (MOD) (L-110)	LF.	8,850	
678.24	ELECTRICAL WIRING (MOD) (L-108)	LF.	10,500	
854.01	P-802 BITUMINOUS PRIME COAT	GAL	6,800	
854.03	P-825 TAR EMULSION PROTECTIVE SEAL COAT	GAL	2,125	
854.04	P-209 CRUSHED AGGREGATE BASE COURSE	C.Y.	6,400	
854.01	P-208A GOLD MIXED RECYCLED BASE COURSE	C.Y.	4,000	
884.02	P-401 BITUMINOUS CONCRETE PAVEMENT (PG 58-34)	TON	12,575	
884.03	P-620 RUNWAY AND TAXI PAINTING (WHITE)	S.F.	31,000	
884.03	P-620 RUNWAY AND TAXI PAINTING (BLACK)	S.F.	4,500	
884.03	P-620 RUNWAY AND TAXI PAINTING (YELLOW)	S.F.	2,900	
884.04	L-108 CABLE TRENCH (MOD) (SAW CUTTING P-410)	LF.	815	
884.06	L-108 #8 COUNTERPOISE WIRE	LF.	10,500	
884.09	L-110 4-WAY X 4" DIA. U.G. ELECTRICAL DUCT	LF.	32	
884.10	L-125 MEDIUM INTENSITY R/W LTS. BASE MTD. (MOD) (END LIGHTS)	EACH	14	
884.10	L-125 MEDIUM INTENSITY R/W LTS. BASE MTD.	EACH	42	
884.11	L-125 MEDIUM INTENSITY TAXIWAY LTS. BASE MTD.	EACH	17	
884.12	L-125 PRECISION APPROACH PATH INDICATOR	EACH	1	
884.13	L-125 RUNWAY END IDENTIFIER LIGHTS	EACH	2	
884.13	L-125 RUNWAY END IDENTIFIER LIGHTS (MOD) (3 PANEL HOLD SIGN) (RELOCATION)	EACH	1	
884.15	L-125 THRESHOLD LIGHTS(MOD)MARKERS RETROREFLECTIVE	EACH	38	

LIST OF STANDARDS

- AP-1
- AP-2
- AP-3
- AP-4
- AP-9
- AP-10
- AP-11
- AP-12
- D-4
- D-8
- D-11
- D-13
- D-15
- D-16
- T-1
- T-2

THESE PLANS AND SPECIFICATIONS ARE IN ACCORDANCE WITH CRITERIA IN CURRENT FAA ADVISORY CIRCULARS AS OF MAY 1, 1995.

DATE

1 VAOT COMMENTS AND SURVEY ADJUSTMENTS 1/18/01
 NO. REVISIONS DATE

Revised 03/19/01

FEDERAL AVIATION ADMINISTRATION

APPROVED: CHIEF, AIRPORT ENGINEER AND SAFETY BRANCH DATE

VERMONT AGENCY OF TRANSPORTATION

David C. Dine Feb 14, 2001
 APPROVED: DIRECTOR OF MAINTENANCE AND AVIATION DATE

PREPARED BY

DuBOIS AND KING, INC.

P.O. BOX 339.....RANDOLPH, V.T. 05060.....TEL. (802) 728-3378

APPROVED: DATE
