






**REGIONAL TRAFFIC CONTROL NOTES:**

1. TRAFFIC WILL BE MAINTAINED ON A REGIONAL DETOUR AS SHOWN ON THE REGIONAL DETOUR MAP. DETOUR SIGNING IS THE RESPONSIBILITY OF THE CONTRACTOR. PAYMENT FOR ALL TEMPORARY TRAFFIC CONTROL DEVICES FOR IMPLEMENTING THE DETOUR, INCLUDING BUT NOT LIMITED TO SIGNS, AND BARRICADES, WILL BE INCLUDED IN THE UNIT PRICE BID FOR CONTRACT ITEM 641.10 TRAFFIC CONTROL.
2. WHERE PRACTICAL, DETOUR ROUTE MARKERS AND ANY ADDITIONAL PROJECT CONSTRUCTION SIGNS SHALL BE INSTALLED ADJACENT TO EXISTING ROUTE MARKERS. NO CONSTRUCTION SIGNS SHALL BE INSTALLED AS TO BLOCK EXISTING TRAFFIC CONTROL SIGN ASSEMBLIES OR TO INTERFERE WITH STOPPING SIGHT DISTANCE AND CORNER SIGHT DISTANCE FROM DRIVES AND TOWN HIGHWAYS. THE CONTRACTOR SHALL MAINTAIN AT LEAST 200 FEET BETWEEN SIGN ASSEMBLIES WHEREVER POSSIBLE.
3. ANY SIGN THAT CONFLICTS WITH THE ROAD CLOSURE DETOUR SHALL BE COVERED FOR THE DURATION OF THE ROAD CLOSURE. TREES AND SHRUBS WITHIN EXISTING RIGHT OF WAY AND OTHERWISE INTERFERING WITH VISIBILITY OF PROPOSED DETOUR SIGNS SHALL BE TRIMMED ACCORDINGLY. PAYMENT FOR SUCH COVERS AND TRIMMING WILL BE MADE UNDER ITEM 641.10 TRAFFIC CONTROL.
4. THE FIVE PORTABLE CHANGEABLE MESSAGE SIGNS IN SUPPORT OF THE REGIONAL DETOUR SHALL BE PLACED AND FULLY OPERATIONAL A MINIMUM OF TWO WEEKS PRIOR TO THE START OF CONSTRUCTION AND REMAIN THROUGH THE DURATION OF THE ROADWAY CLOSURE PERIOD. PAYMENT FOR THIS WORK SHALL BE MADE UNDER CONTRACT ITEM 641.15 PORTABLE CHANGABLE MESSAGE SIGN.

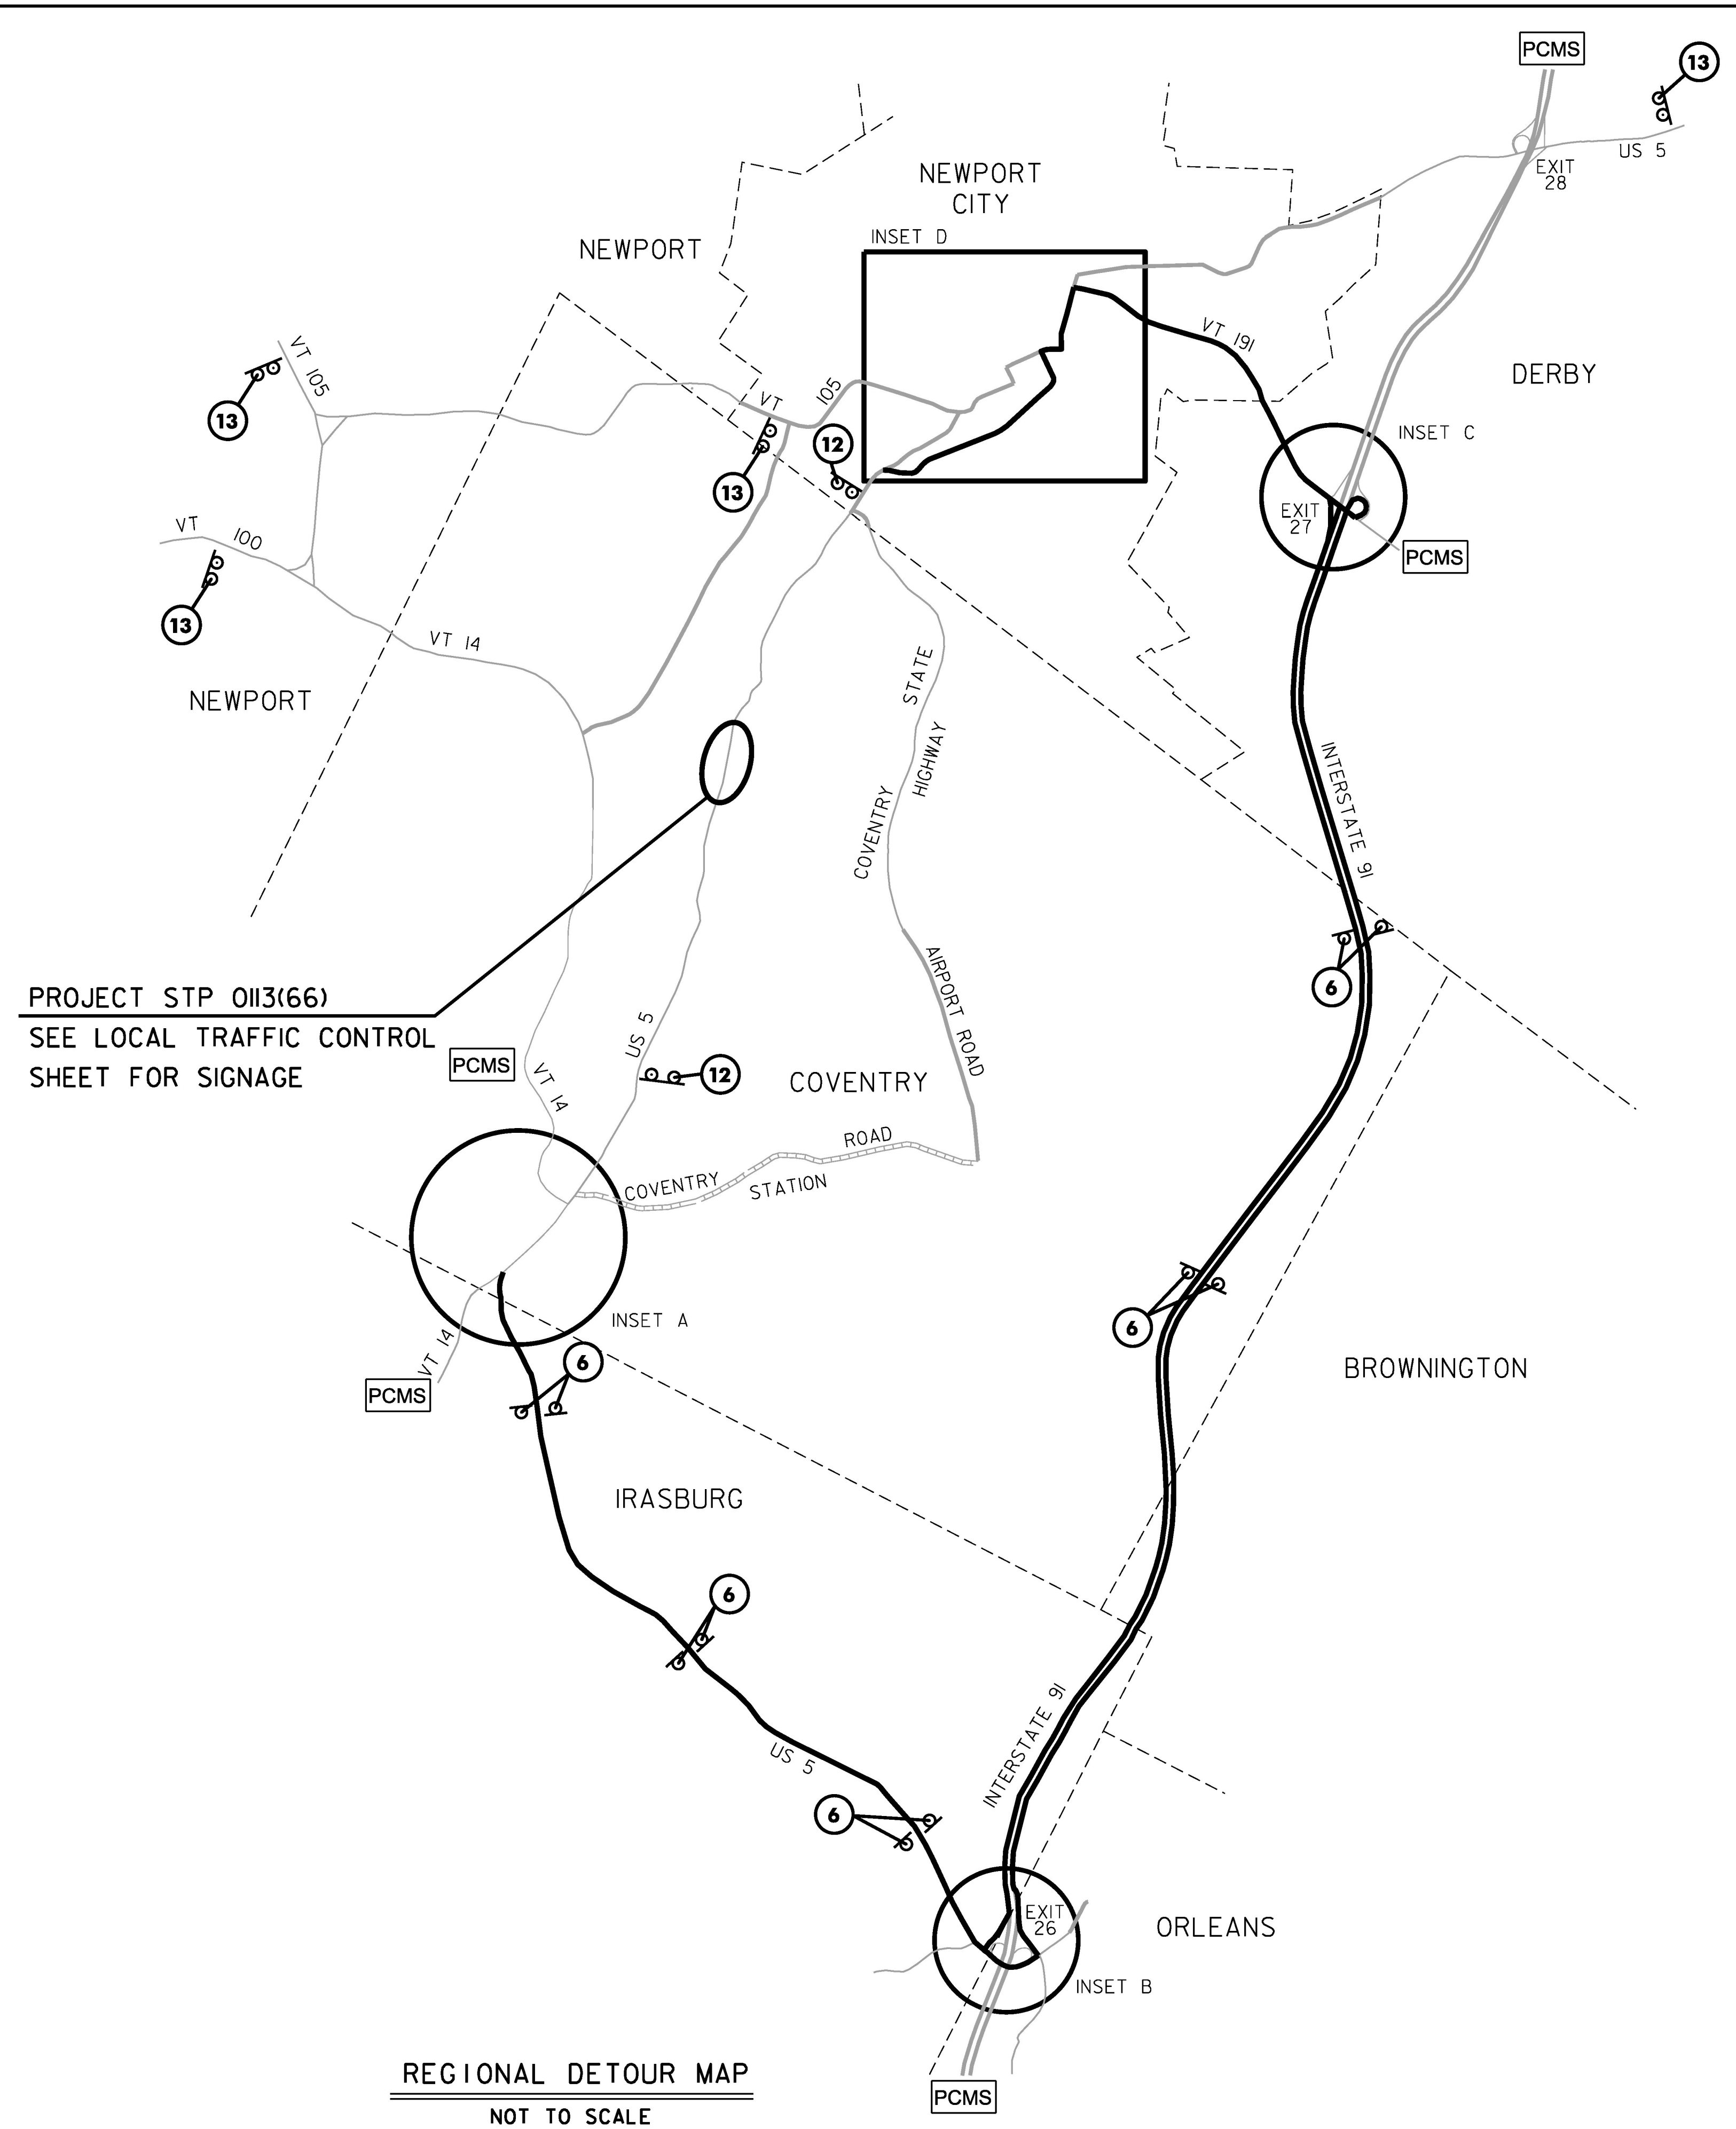

**LEGEND:**

-  SIGN ASSEMBLY
-  SIGN ASSEMBLY INDICATOR
-  PORTABLE CHANGEABLE MESSAGE SIGN
-  DETOUR ROUTE

PROJECT NAME: COVENTRY	
PROJECT NUMBER: STP 0113(66)	
FILE NAME: d:\0c114\detour.dgn	PLOT DATE: 15-FEB-2017
PROJECT LEADER: K. UPMAL	DRAWN BY: S. ZWICK
DESIGNED BY: S. ZWICK	CHECKED BY: C. LEACH
TRAFFIC CONTROL SHEET 1	SHEET 26 OF 29
