
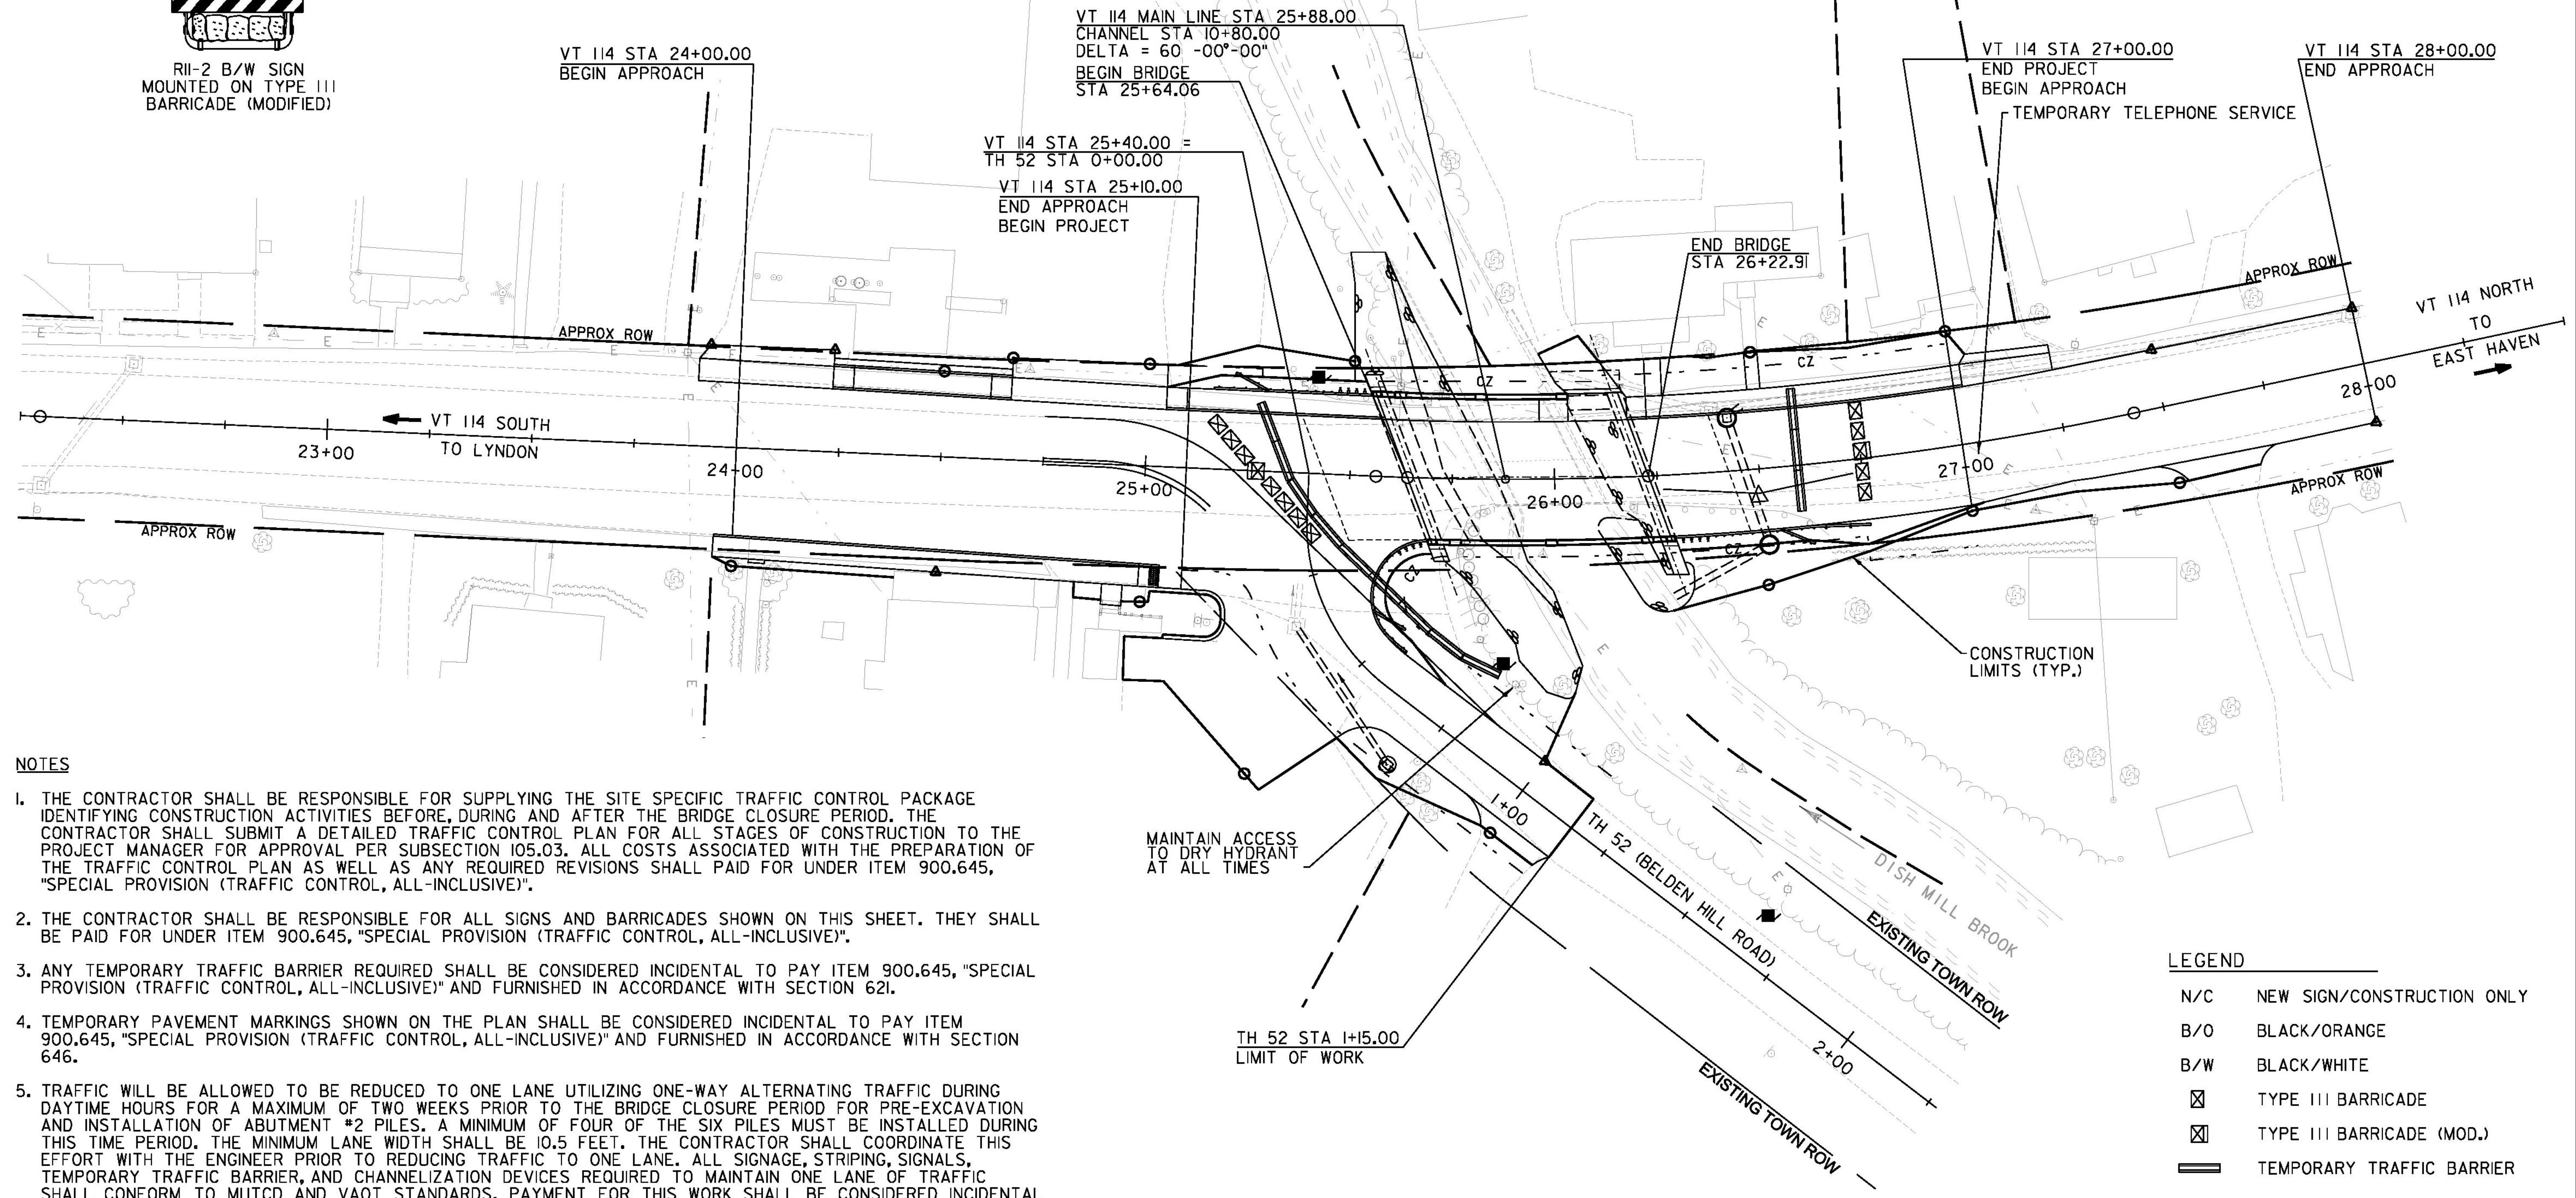


R11-2 B/W SIGN MOUNTED ON TYPE III BARRICADE (MODIFIED)

W20-3 B/O  
N/C



**NOTES**

1. THE CONTRACTOR SHALL BE RESPONSIBLE FOR SUPPLYING THE SITE SPECIFIC TRAFFIC CONTROL PACKAGE IDENTIFYING CONSTRUCTION ACTIVITIES BEFORE, DURING AND AFTER THE BRIDGE CLOSURE PERIOD. THE CONTRACTOR SHALL SUBMIT A DETAILED TRAFFIC CONTROL PLAN FOR ALL STAGES OF CONSTRUCTION TO THE PROJECT MANAGER FOR APPROVAL PER SUBSECTION 105.03. ALL COSTS ASSOCIATED WITH THE PREPARATION OF THE TRAFFIC CONTROL PLAN AS WELL AS ANY REQUIRED REVISIONS SHALL PAID FOR UNDER ITEM 900.645, "SPECIAL PROVISION (TRAFFIC CONTROL, ALL-INCLUSIVE)".
2. THE CONTRACTOR SHALL BE RESPONSIBLE FOR ALL SIGNS AND BARRICADES SHOWN ON THIS SHEET. THEY SHALL BE PAID FOR UNDER ITEM 900.645, "SPECIAL PROVISION (TRAFFIC CONTROL, ALL-INCLUSIVE)".
3. ANY TEMPORARY TRAFFIC BARRIER REQUIRED SHALL BE CONSIDERED INCIDENTAL TO PAY ITEM 900.645, "SPECIAL PROVISION (TRAFFIC CONTROL, ALL-INCLUSIVE)" AND FURNISHED IN ACCORDANCE WITH SECTION 621.
4. TEMPORARY PAVEMENT MARKINGS SHOWN ON THE PLAN SHALL BE CONSIDERED INCIDENTAL TO PAY ITEM 900.645, "SPECIAL PROVISION (TRAFFIC CONTROL, ALL-INCLUSIVE)" AND FURNISHED IN ACCORDANCE WITH SECTION 646.
5. TRAFFIC WILL BE ALLOWED TO BE REDUCED TO ONE LANE UTILIZING ONE-WAY ALTERNATING TRAFFIC DURING DAYTIME HOURS FOR A MAXIMUM OF TWO WEEKS PRIOR TO THE BRIDGE CLOSURE PERIOD FOR PRE-EXCAVATION AND INSTALLATION OF ABUTMENT #2 PILES. A MINIMUM OF FOUR OF THE SIX PILES MUST BE INSTALLED DURING THIS TIME PERIOD. THE MINIMUM LANE WIDTH SHALL BE 10.5 FEET. THE CONTRACTOR SHALL COORDINATE THIS EFFORT WITH THE ENGINEER PRIOR TO REDUCING TRAFFIC TO ONE LANE. ALL SIGNAGE, STRIPING, SIGNALS, TEMPORARY TRAFFIC BARRIER, AND CHANNELIZATION DEVICES REQUIRED TO MAINTAIN ONE LANE OF TRAFFIC SHALL CONFORM TO MUTCD AND VAOT STANDARDS. PAYMENT FOR THIS WORK SHALL BE CONSIDERED INCIDENTAL TO PAY ITEM 900.645, "SPECIAL PROVISION (TRAFFIC CONTROL, ALL-INCLUSIVE)".
6. SEE STANDARD T-10 FOR TYPICAL APPROACH SIGNING AND REGIONAL DETOUR MAP ON SHEET 21 FOR ADDITIONAL INFORMATION.

MAINTAIN ACCESS TO DRY HYDRANT AT ALL TIMES

TH 52 STA 1+15.00  
LIMIT OF WORK

**LEGEND**

- N/C NEW SIGN/CONSTRUCTION ONLY
- B/O BLACK/ORANGE
- B/W BLACK/WHITE
- ☒ TYPE III BARRICADE
- ☒ TYPE III BARRICADE (MOD.)
- ▬ TEMPORARY TRAFFIC BARRIER

PROJECT NAME:	BURKE	PLOT DATE:	11/19/2014
PROJECT NUMBER:	BRF 0269(13)	DRAWN BY:	M. HALEY
FILE NAME:	I0c412/cos/z10c412bdr+tcp.dgn	CHECKED BY:	P. SHEDD
PROJECT LEADER:	J. BYATT	TRAFFIC CONTROL SHEET	SHEET 20 OF 73
DESIGNED BY:	M. HALEY		



MODEL: LOI  
CLD 12-0121
