

STONE FILL, TYPE I  
 MM 3.550 - MM 3.667 RT  
 MM 3.678 - MM 3.850 RT

SPECIAL PROVISION (BOX BEAM  
 GUARDRAIL W/7 FEET POSTS)  
 MM 3.550 - MM 3.667 RT  
 MM 3.678 - MM 3.850 RT  
 MM 3.698 - MM 3.800 LT

REMOVAL AND DISPOSAL OF GUARDRAIL  
 MM 3.678 - MM 3.850 RT  
 MM 3.698 - MM 3.800 LT

DURABLE 4 INCH WHITE LINE (SEE OPTION ITEMS) &  
 TEMPORARY 4 INCH WHITE LINE, PAINT  
 MM 3.550 - MM 3.850 (SOLID LT & RT)  
 (WITH EDGE LINE BREAKS AT TH#10)  
 MM 3.805 LT (EDGE LINES AT TH#10)

DURABLE 4 INCH YELLOW LINE (SEE OPTION ITEMS) &  
 TEMPORARY 4 INCH YELLOW LINE, PAINT  
 MM 3.550 - MM 3.822 (SOLID LT & RT)  
 MM 3.822 - MM 3.850 (SOLID LT, DASHED RT)  
 (WITH CENTERLINE BREAKS AT TH#10)  
 MM 3.805 LT (CENTERLINE AT TH#10)

DURABLE 24 INCH STOP BAR (SEE OPTION ITEMS) &  
 TEMPORARY 24 INCH STOP BAR, PAINT  
 MM 3.802 - MM 3.806 LT


DURABLE LETTER OR SYMBOL (SEE OPTION ITEMS) &  
 TEMPORARY LETTER OR SYMBOL, PAINT  
 MM 3.804 LT (STOP)

GEOTEXTILE FOR SILT FENCE  
 MM 3.550 - MM 3.667 RT  
 MM 3.678 - MM 3.850 RT

REMOVING SIGNS  
 AS SHOWN - 3

ERECTING SALVAGED SIGNS  
 AS SHOWN - 1

SPECIAL PROVISION  
 (DECOMMISSION CURB DROP INLET)  
 MM 3.580 RT  
 MM 3.645 RT  
 MM 3.722 RT  
 MM 3.797 RT

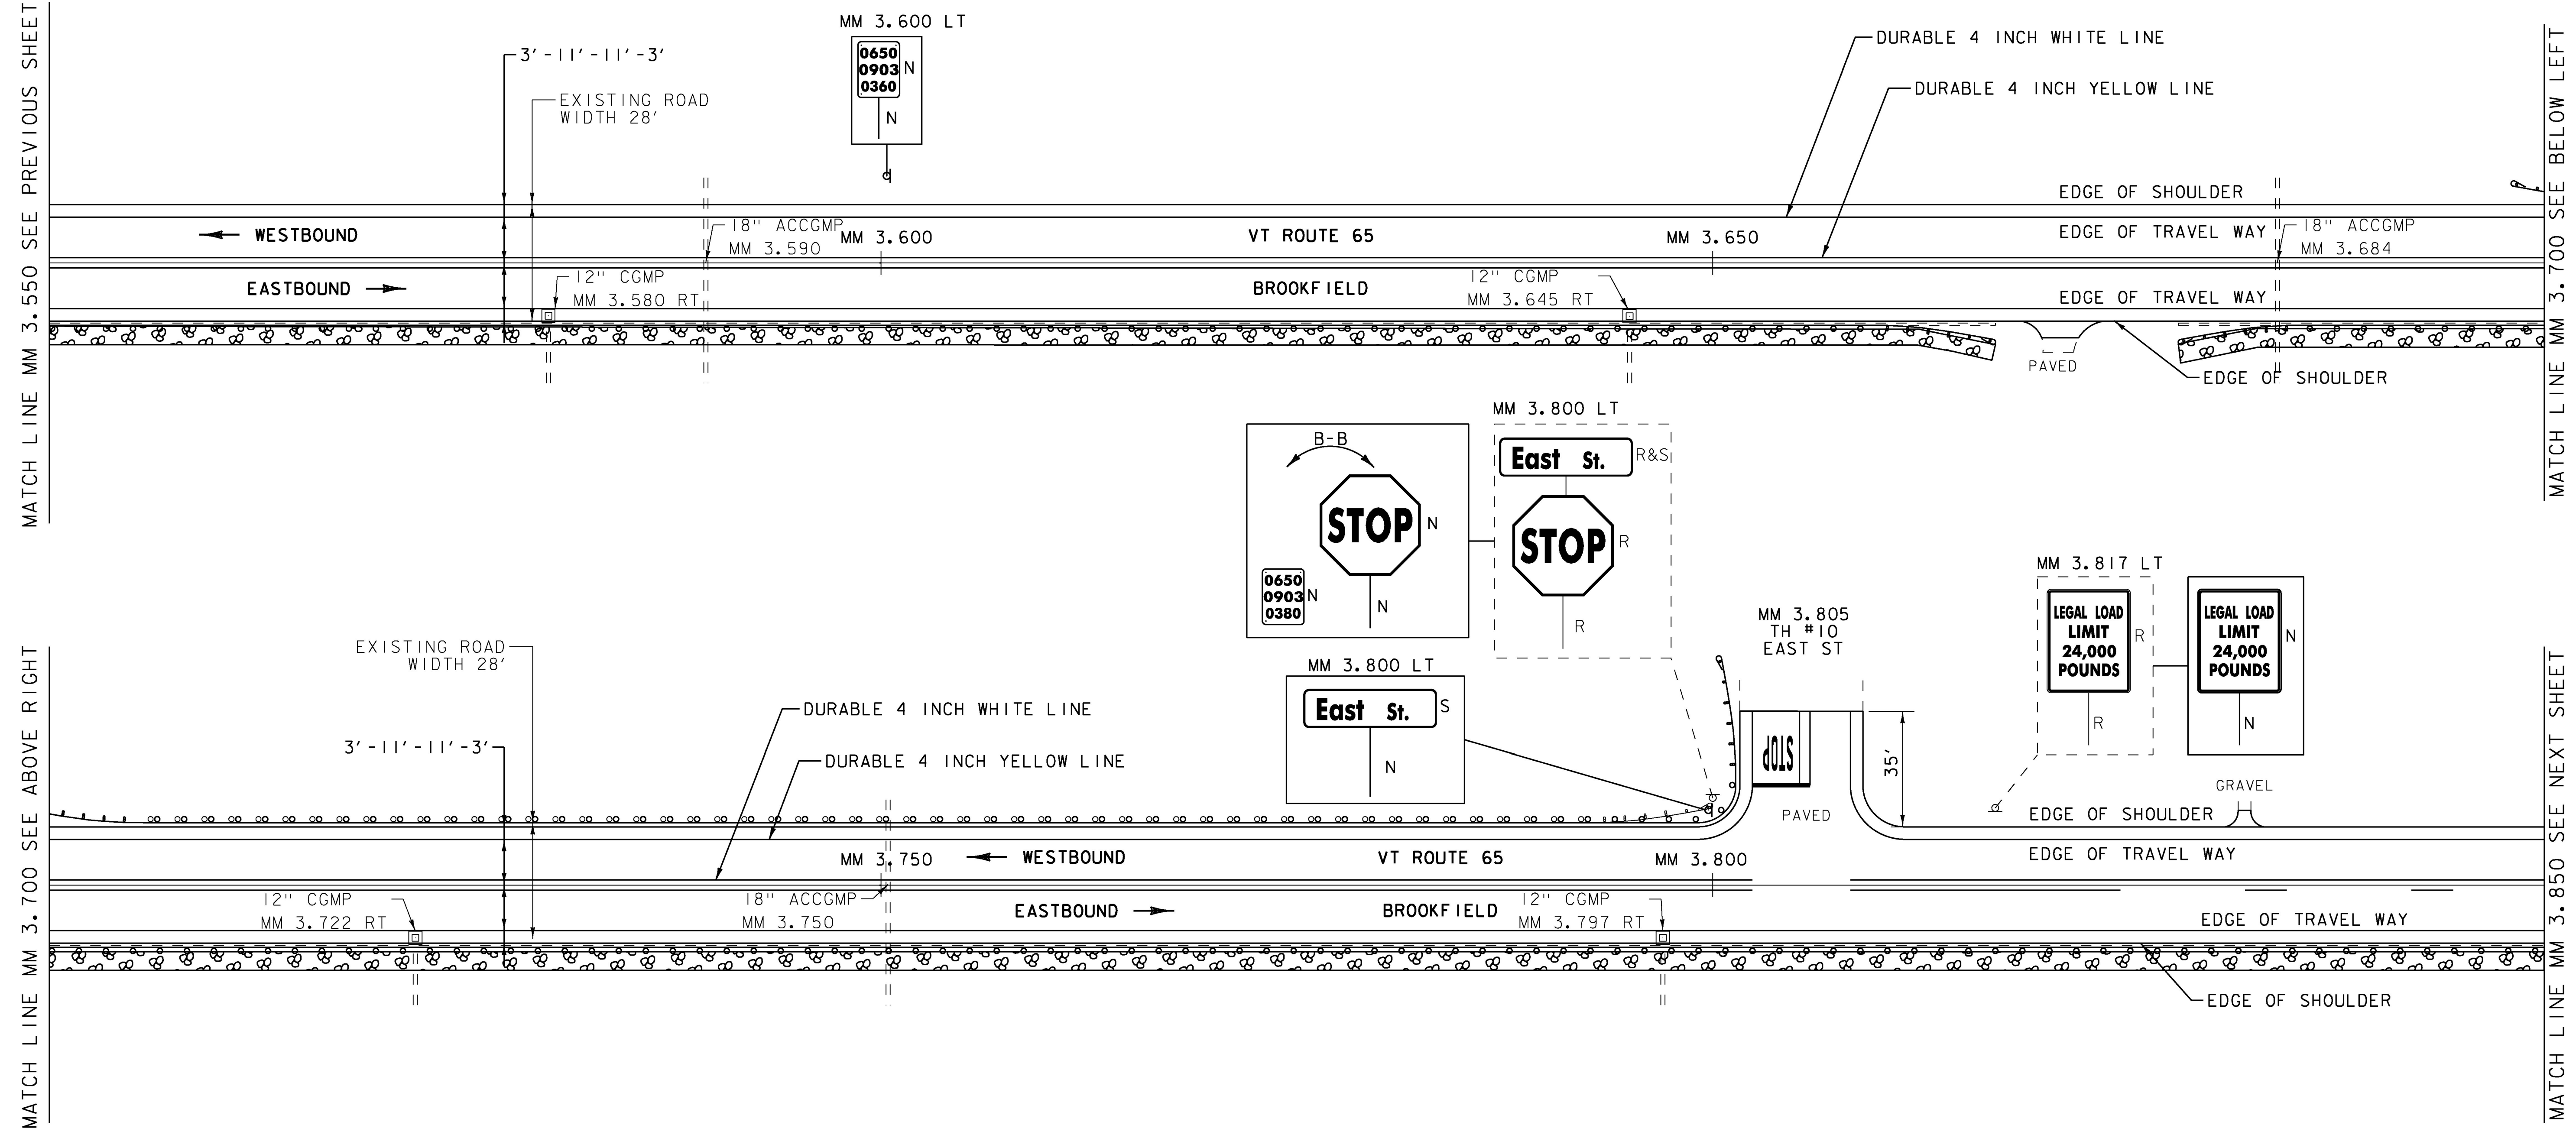

**SIGN LEGEND**  
 R = REMOVE  
 R&S = REMOVE AND SALVAGE  
 RET = RETAIN  
 S = SALVAGE  
 N = NEW  
 B-B = BACK TO BACK  
 - - - = EXISTING  
 — = NEW

PROJECT NAME: BROOKFIELD  
 PROJECT NUMBER: STP 2960(I)  
 FILE NAME: z15v023bdr.dgn  
 PROJECT LEADER: C. LATHROP  
 DESIGNED BY: S. SOLLA  
 PLAN SHEET 4  
 PLOT DATE: 4/26/2016  
 DRAWN BY: O. DALMER  
 CHECKED BY: C. LATHROP  
 SHEET 167 OF 202

NOT TO SCALE
