

File 5.1.2

Contractor:	J.A. McDonald
Job Name:	Lincoln BRF 0188 (8)
Location:	Lincoln, Vt.
Job #	167-15
Date:	6/19/2015



CAMP Precast Concrete Products, Inc.
78 Precast Road, Milton, VT 05468
Phone (802) 893-2401 Fax (802) 893-1542


Product I.D. DI 506 + 14 **Diameter:** 60"
Invert: No **Ladders:** No **Coating:** No **Access Size:** 24" x 48"
Cast Iron / Hatch: Neenah R-3587-4

Rim:	1001.26	Cone:		Riser#1:		Riser#4:	
Inv. Out:	996.58	Cover:	13" (special)	Riser#2:		Riser#5:	
Diff:	4.68	Base:	3'	Riser#3:		Riser#6:	
Sump:	0.50						
Gross V.F.:	5.18	Angle					
C.I. Height:	0.67	Boot:					
Net V.F.:	4.51	Dist. Up:					
Brick Space:	0.43	Pipe Type:					
Actual V.F.	4.08	Pipe Size:					

Quality Control	Prepour	Form Cleaning:		Form Release:	
		Rein. Steel:	Std. Spec.	Form Closure:	
		Block Out:		Rein. Size:	
		Comments:		Q.C. by/date:	
Quality Control	Postpour	Finish:		Bricking:	
		Invert:		Ladders:	
		Coating:		Boots:	
		Comments:		Q.C. by/date:	
Special Info. / Comments:		**VT AOT Specs including 8" thick base**			
Mold #:		YDS ³		Wt.	

PLAN / FLIPPED

COVER

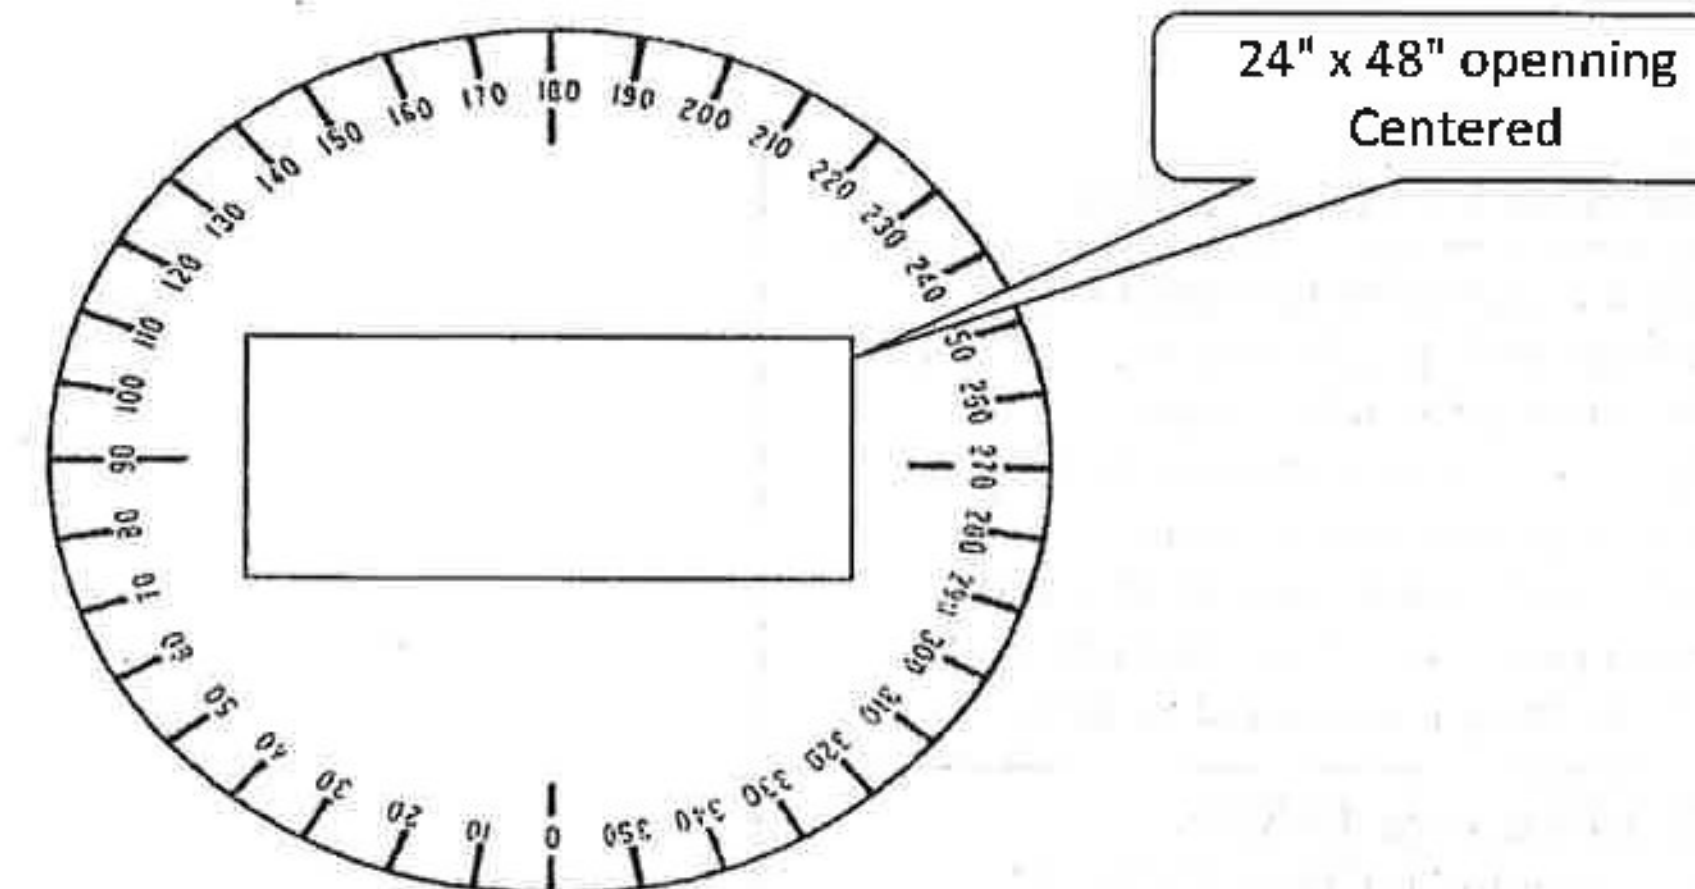

Vermont Agency of Transportation

RECEIVED

ON: June 23, 2015

and Checked for

CONFORMANCE

BY: Todd A. Sumner DATE: 06/24/2015
