


- DRAINAGE NOTES**
- 15 7+00 RT CAP EXIST. DI
 - 16 8+00 LT REMOVE EXIST. DI, HEADWALL AND PIPE
 - 17 6+75 - 9+75 LT NEW 24" X 300' CPEP W/CONC. HEADWALL AT INLET AND OUTLET
 - 18 10+00 LT NEW 18" X 8' RCP CL III, W/CONC. HEADWALL AND RCDI
 - 18A 9+75 - 11+00 LT CONSTRUCT SPECIAL DITCH W/STONE FILL TYPE I
 - 19 8+00 - 10+00 RT NEW 18" X 200' RCP CL III, W/RCDI AT INLET
 - 19A 10+00 - 12+00 RT NEW 18" X 200' RCP CL III, W/RCDI AT INLET

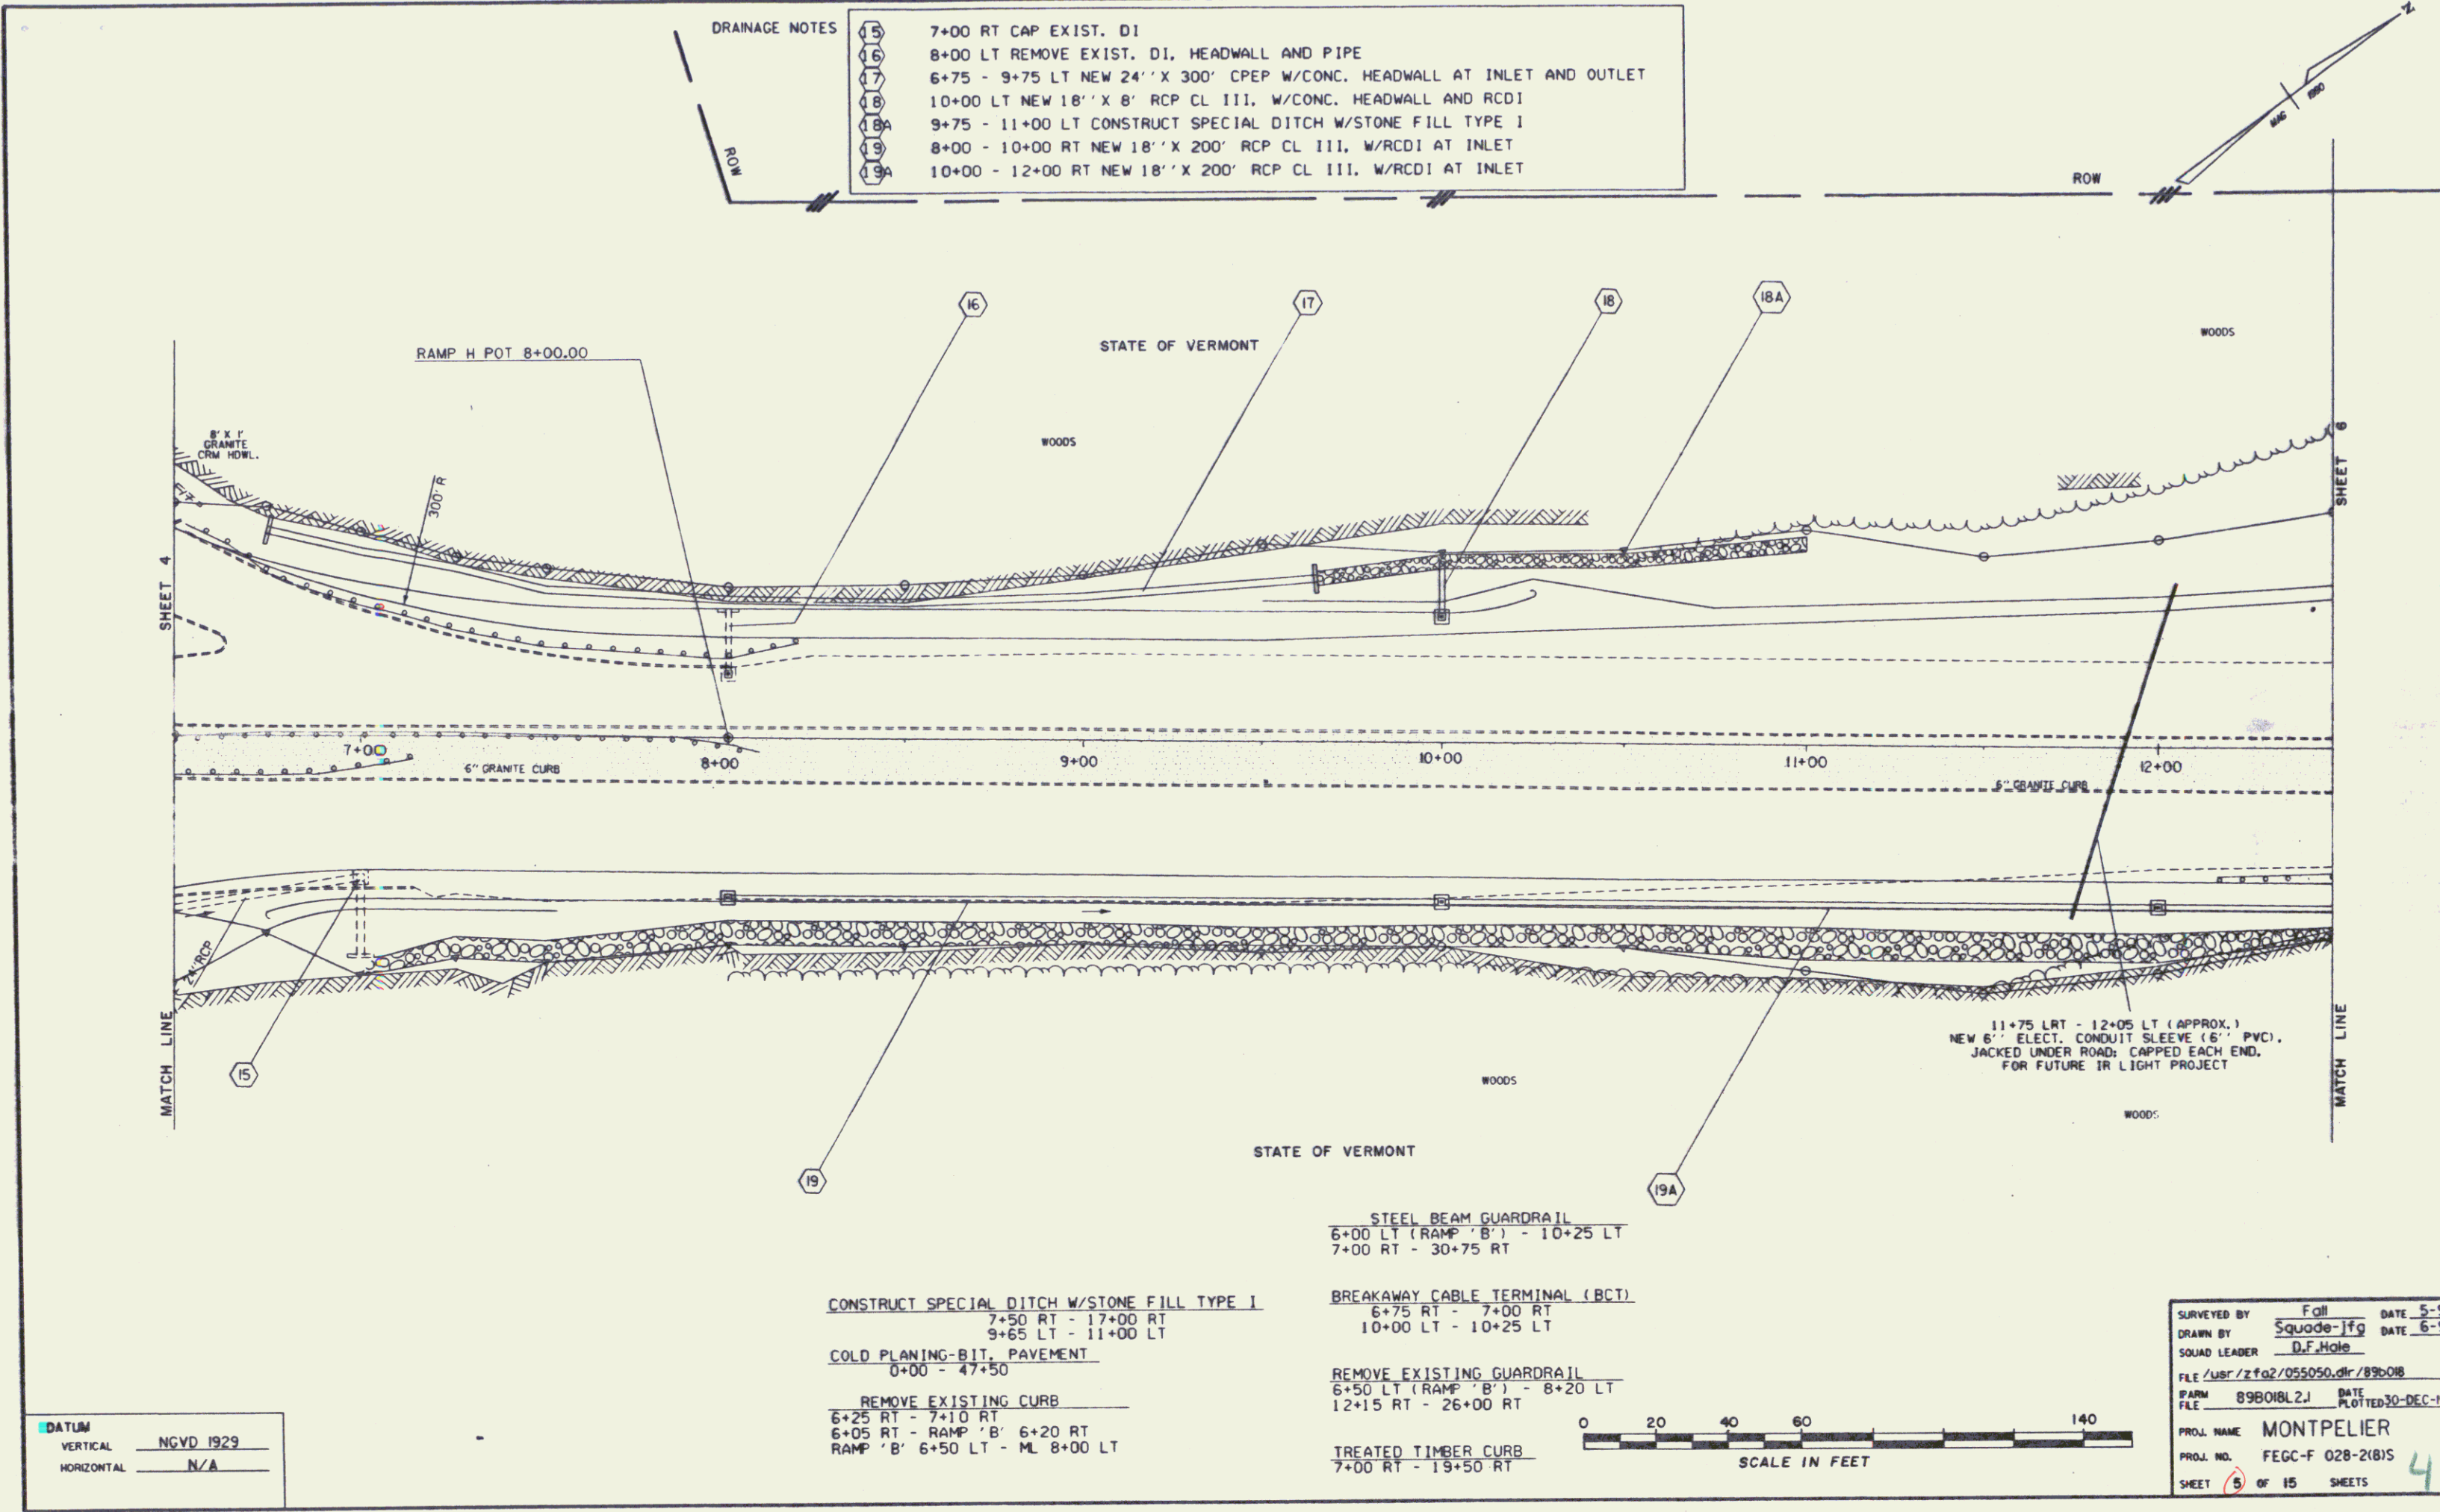

DATUM
 VERTICAL NGVD 1929
 HORIZONTAL N/A

REMOVE EXISTING CURB
 6+25 RT - 7+10 RT
 6+05 RT - RAMP 'B' 6+20 RT
 RAMP 'B' 6+50 LT - ML 8+00 LT

CONSTRUCT SPECIAL DITCH W/STONE FILL TYPE I
 7+50 RT - 17+00 RT
 9+65 LT - 11+00 LT

COLD PLANING-BIT, PAVEMENT
 0+00 - 47+50

STEEL BEAM GUARDRAIL
 6+00 LT (RAMP 'B') - 10+25 LT
 7+00 RT - 30+75 RT

BREAKAWAY CABLE TERMINAL (BCT)
 6+75 RT - 7+00 RT
 10+00 LT - 10+25 LT

REMOVE EXISTING GUARDRAIL
 6+50 LT (RAMP 'B') - 8+20 LT
 12+15 RT - 26+00 RT

TREATED TIMBER CURB
 7+00 RT - 19+50 RT



SURVEYED BY Fall DATE 5-5
 DRAWN BY Squade-jfg DATE 6-5
 SQUAD LEADER D.F.Hole
 FILE /usr/zfg2/055050.dir/89b018
 PARM 89B018.LJ DATE PLOTTED 30-DEC-91
 PROJ. NAME MONTPELIER
 PROJ. NO. FECC-F 028-21815
 SHEET 5 OF 15 SHEETS

FEB 01 1992
