

646.412 DURABLE 4 INCH YELLOW LINE, THERMOPLASTIC
 (ALL LINES WILL INCLUDE C/L BREAKS FOR TOWN HIGHWAYS) S=SOLID, D=DASHED

WOODSTOCK:
 STA. 256+81.92 DOUBLE SOLID LT, TH-3
 STA. 257+45.28 DOUBLE SOLID LT, TH-81

646.442 DURABLE 8 INCH WHITE LINE, THERMOPLASTIC

WOODSTOCK:
 STA. 257+10.00 - STA. 257+45.28 SHOULDER HATCHING LT, TH-81

646.482 DURABLE 24 INCH STOP BAR, THERMOPLASTIC

WOODSTOCK:
 STA. 256+81.92 LT, TH-3
 STA. 257+45.28 LT, TH-81

646.492 DURABLE LETTER OR SYMBOL, THERMOPLASTIC

WOODSTOCK:
 STA. 256+81.92 LT, TH-3 "S,T,O,P" (4 EA)
 STA. 257+45.28 LT, TH-81 "S,T,O,P" (4 EA)

646.612 TEMPORARY 4 INCH YELLOW LINE, PAINT
 (ALL LINES WILL INCLUDE C/L BREAKS FOR TOWN HIGHWAYS) S=SOLID, D=DASHED

WOODSTOCK:
 STA. 256+81.92 DOUBLE SOLID LT, TH-3
 STA. 257+45.28 DOUBLE SOLID LT, TH-81

646.682 TEMPORARY 24 INCH STOP BAR, PAINT

WOODSTOCK:
 STA. 256+81.92 LT, TH-3
 STA. 257+45.28 LT, TH-81

646.692 TEMPORARY LETTER OR SYMBOL, PAINT


WOODSTOCK:
 STA. 256+81.92 LT, TH-3 "S,T,O,P" (8 EA)
 STA. 257+45.28 LT, TH-81 "S,T,O,P" (8 EA)

675.50 REMOVING SIGNS

AS SHOWN - 9

675.60 ERECTING SALVAGED SIGNS

AS SHOWN - 4

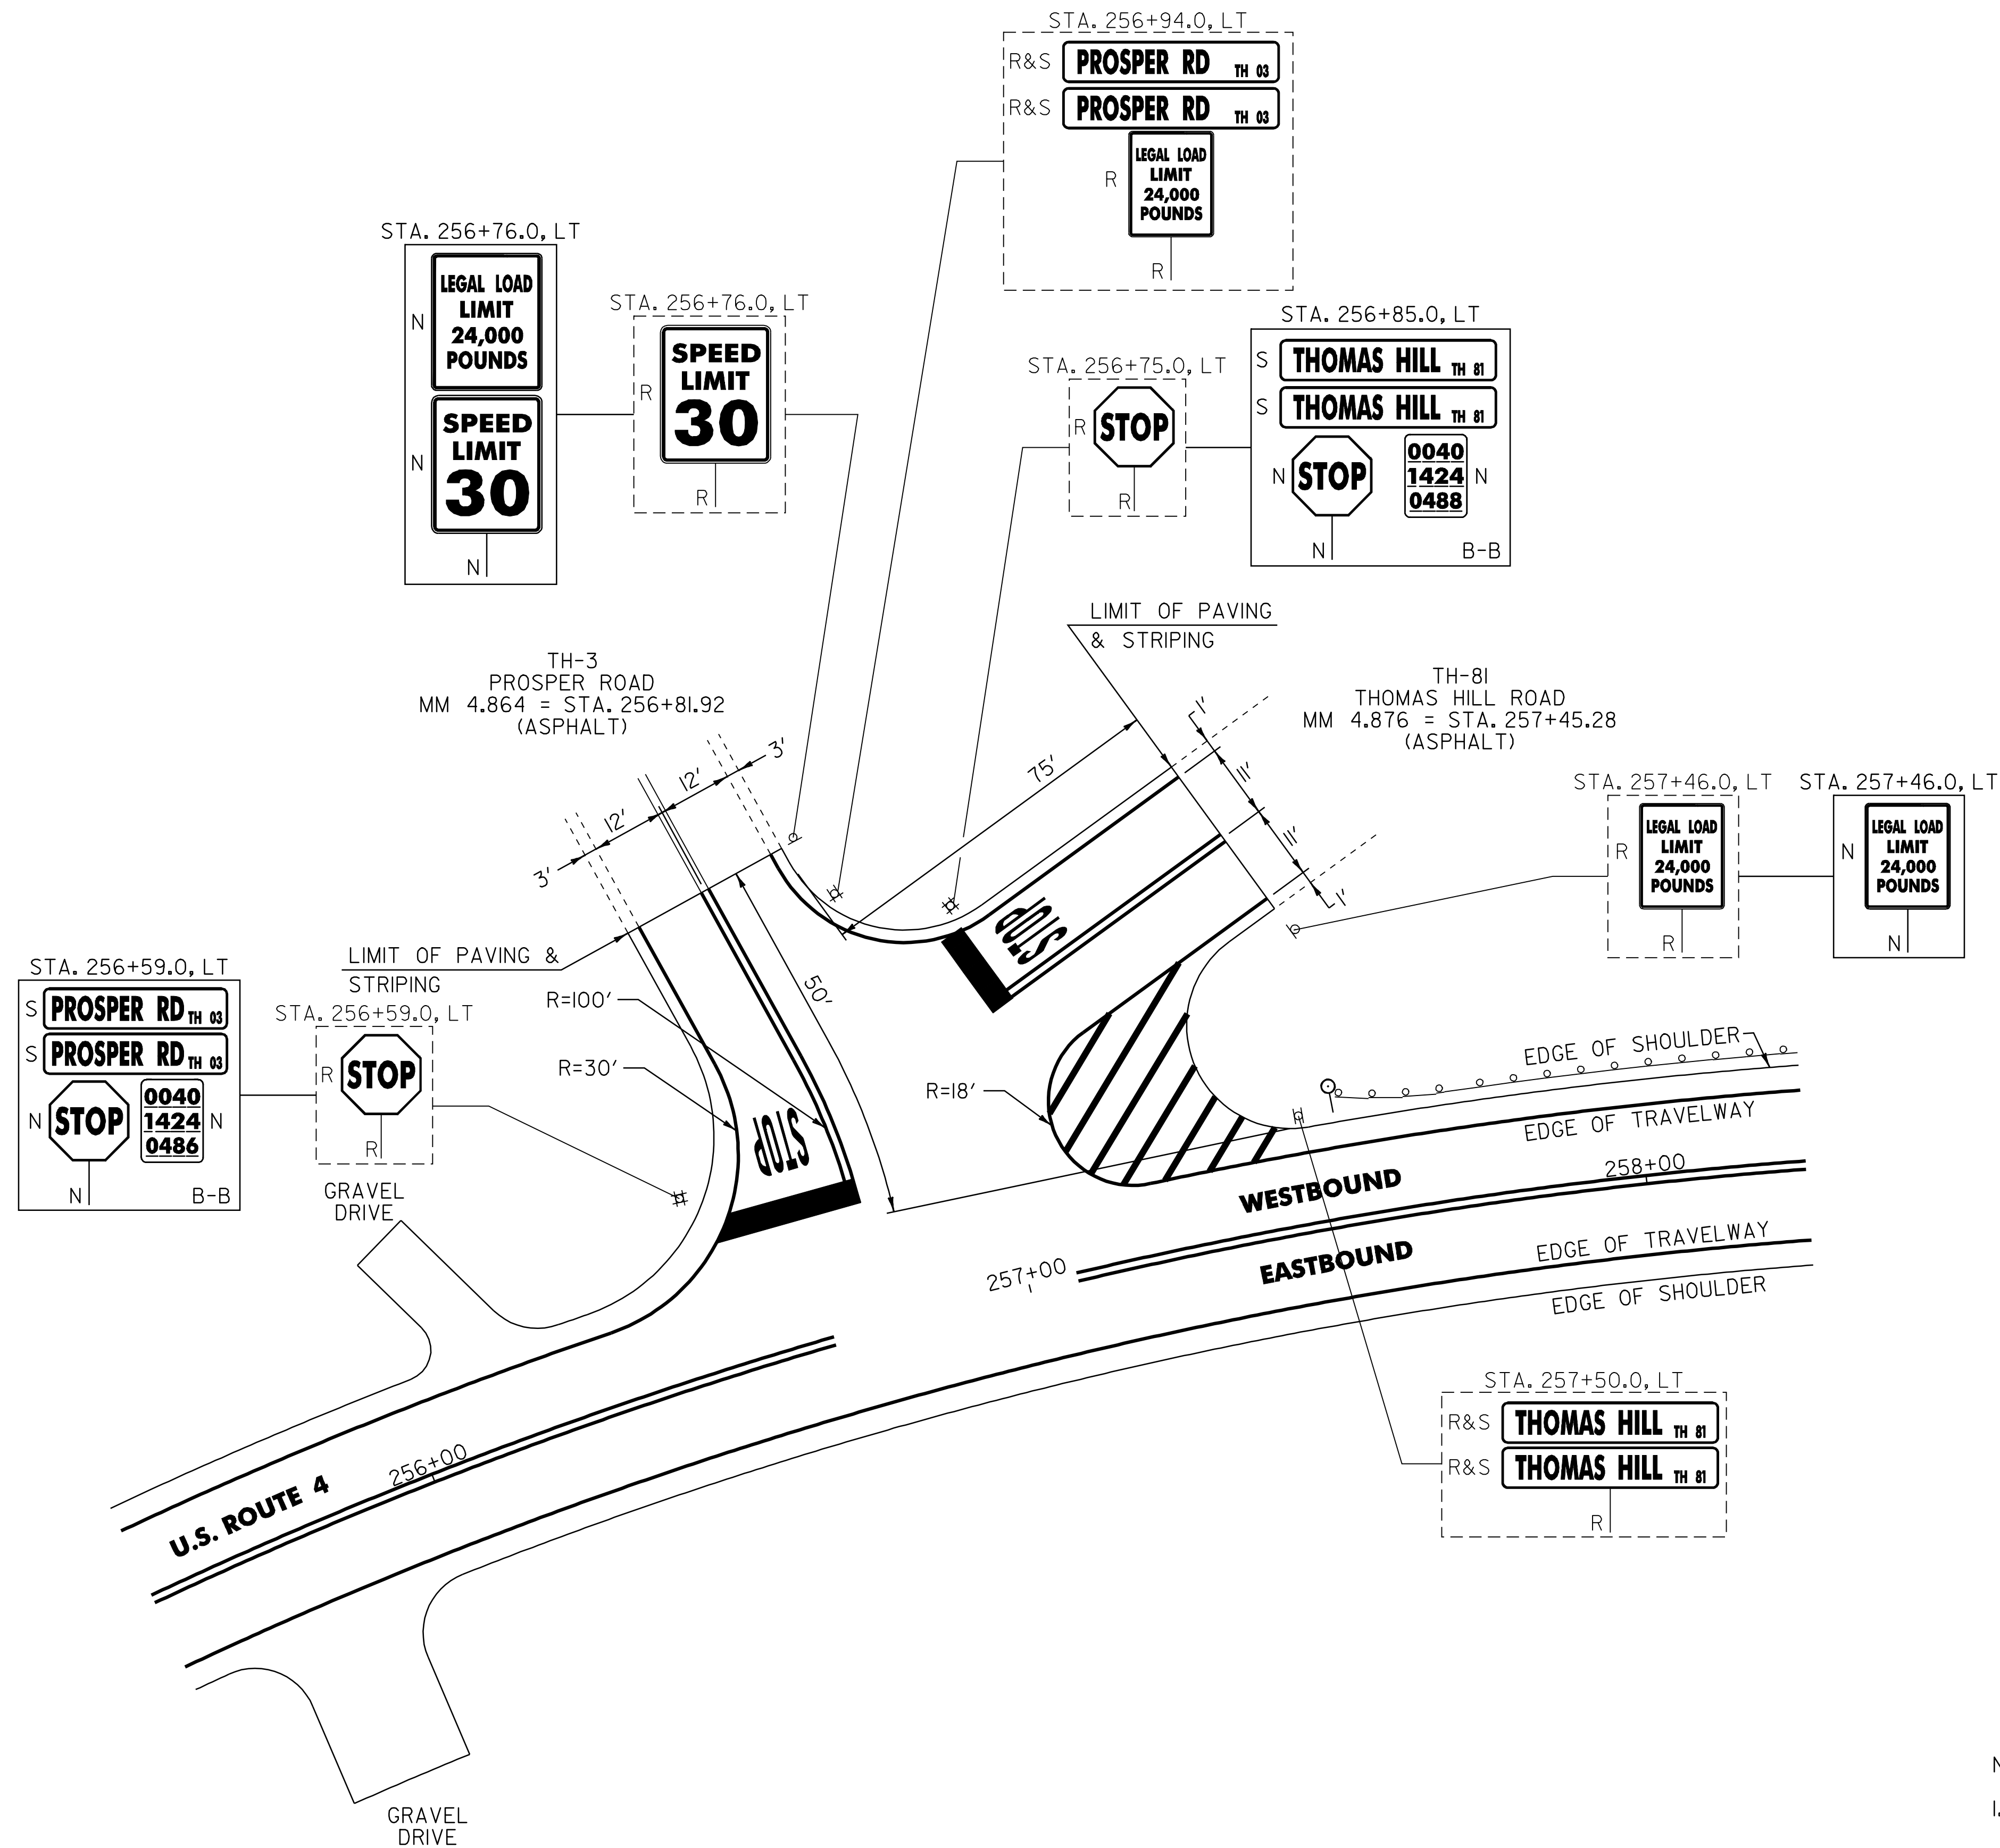

NOTE:
 1. PAVING LIMIT ON ALL TOWN HIGHWAYS SHALL BE MEASURED 25 FT BACK FROM U.S. ROUTE 4 EDGE OF SHOULDER UNLESS DENOTED OTHERWISE ON THE PLANS OR AS DIRECTED BY THE RESIDENT ENGINEER.

SIGN LEGEND
 R = REMOVE
 S = SALVAGE
 N = NEW
 RET = RETAIN
 B-B = BACK TO BACK
 EXISTING = - - - - -
 NEW = _____

NOT TO SCALE
TH-3/TH-81
INTERSECTION
DETAIL
SHEET

PROJECT NAME: BRIDGEWATER - WOODSTOCK
 PROJECT NUMBER: NH_2611(S)
 FILE NAME: p06b160.dgn
 PROJECT LEADER: D.E.G.
 DESIGNED BY: D.W.E.
 IPARM FILE: p06b160n102.i...
 PLOT DATE: 28-MAY-2010
 DRAWN BY: C.A.K.
 CHECKED BY: D.E.G.
 SHEET 38 OF 80
