

646.402 DURABLE 4 INCH WHITE LINE, THERMOPLASTIC
 U.S. ROUTE 7:
 STA 69+00.00 - STA 70+10.00 SOLID LANE LINE LT
 STA 69+00.00 - STA 70+10.00 SOLID LANE LINE C/L
 STA 69+00.00 - STA 73+00.00 DASHED LANE LINE LT
 STA 69+00.00 - STA 73+00.00 DASHED LANE LINE RT
 STA 70+10.00 - STA 71+10.00 DOTTED LANE LINE LT
 STA 70+10.00 - STA 72+10.00 DOTTED LANE LINE LT
 STA 71+10.00 - STA 73+00.00 DOTTED LANE LINE RT
 STA 72+10.00 - STA 73+00.00 DOTTED LANE LINE RT

646.602 TEMPORARY 4 INCH WHITE LINE, PAINT
 U.S. ROUTE 7:
 STA 69+00.00 - STA 70+10.00 SOLID LANE LINE LT
 STA 69+00.00 - STA 70+10.00 SOLID LANE LINE C/L
 STA 69+00.00 - STA 73+00.00 DASHED LANE LINE LT
 STA 69+00.00 - STA 73+00.00 DASHED LANE LINE RT
 STA 70+10.00 - STA 71+10.00 DOTTED LANE LINE LT
 STA 70+10.00 - STA 72+10.00 DOTTED LANE LINE LT
 STA 71+10.00 - STA 73+00.00 DOTTED LANE LINE RT
 STA 72+10.00 - STA 73+00.00 DOTTED LANE LINE RT

646.412 DURABLE 4 INCH YELLOW LINE, THERMOPLASTIC
 (ALL LINES WILL INCLUDE C/L BREAKS FOR TOWN HIGHWAYS)
 U.S. ROUTE 7:
 STA 69+00.00 - STA 70+10.00 DOUBLE SOLID RT
 STA 70+10.00 - STA 73+00.00 DOUBLE SOLID LT/RT
 STA 72+38.88 DOUBLE SOLID RT, NORTON PLACE

646.612 TEMPORARY 4 INCH YELLOW LINE, PAINT
 (ALL LINES WILL INCLUDE C/L BREAKS FOR TOWN HIGHWAYS)
 U.S. ROUTE 7:
 STA 69+00.00 - STA 70+10.00 DOUBLE SOLID RT
 STA 70+10.00 - STA 73+00.00 DOUBLE SOLID LT/RT
 STA 72+38.88 DOUBLE SOLID RT, NORTON PLACE

646.452 DURABLE 8 INCH YELLOW LINE, THERMOPLASTIC
 U.S. ROUTE 7:
 STA 70+10.00 - STA 73+00.00 HATCHED MEDIAN LT/RT


646.481 DURABLE 24 INCH STOP BAR, TYPE ITAPE
 U.S. ROUTE 7:
 STA 72+38.88 RT, NORTON PLACE

646.682 TEMPORARY 24 INCH STOP BAR, PAINT
 U.S. ROUTE 7:
 STA 72+38.88 RT, NORTON PLACE

604.412 REHAB. DROP INLETS, CATCH BASINS, OR MANHOLES, CLASS 1
 U.S. ROUTE 7:
 STA 71+32.0 LT
 STA 71+54.0 RT

604.42 CHANGING ELEVATION OF SEWER MANHOLES
 U.S. ROUTE 7:
 STA 72+42.0 RT

629.20 ADJUST ELEVATION OF VALVE BOX
 U.S. ROUTE 7:
 STA 71+61.0 RT
 STA 72+27.0 RT

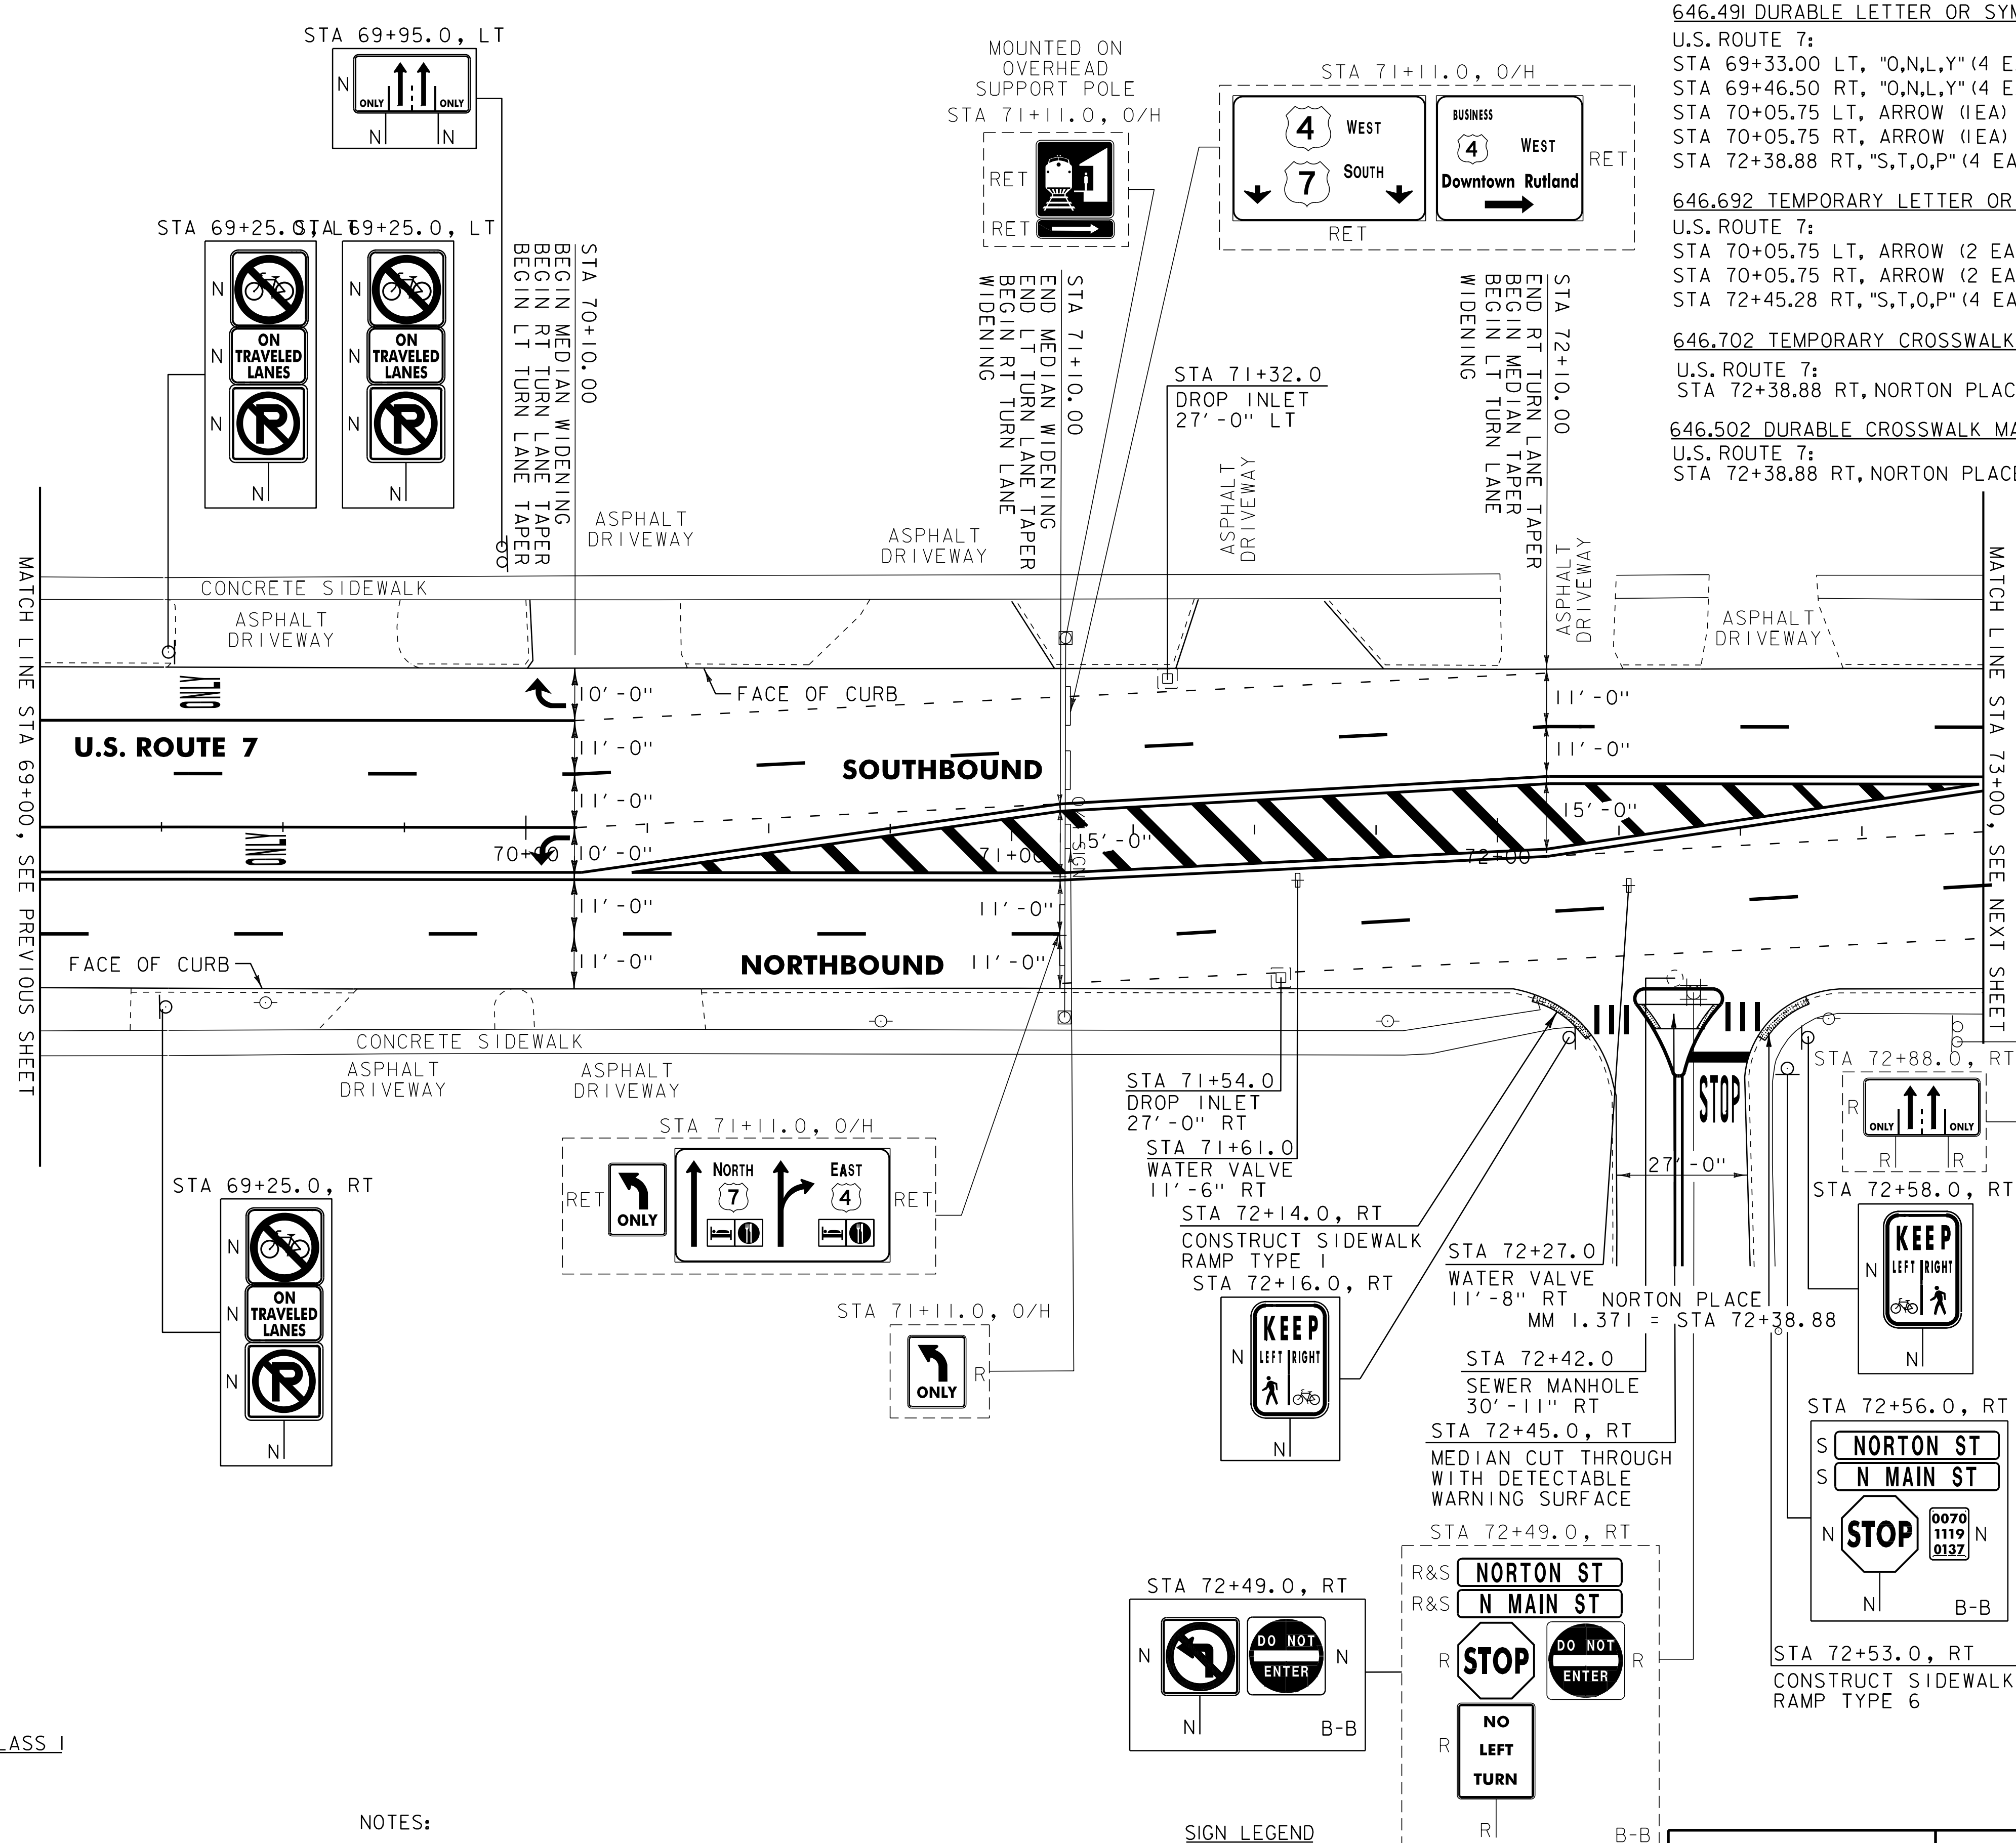

NOTES:
 1. PAVING LIMIT ON ALL TOWN HIGHWAYS SHALL BE MEASURED 25 FT BACK FROM U.S. ROUTE 7 EDGE OF SHOULDER UNLESS DENOTED OTHERWISE ON THE PLANS OR AS DIRECTED BY THE RESIDENT ENGINEER.
 2. SEE SHEET 42 FOR VIDEO DETECTION SYSTEM SHEET.

SIGN LEGEND
 R = REMOVE
 S = SALVAGE
 N = NEW
 RET = RETAIN
 B-B = BACK TO BACK
 EXISTING = - - - - -
 NEW = _____

646.491 DURABLE LETTER OR SYMBOL, TYPE ITAPE
 U.S. ROUTE 7:
 STA 69+33.00 LT, "O,N,L,Y" (4 EA)
 STA 69+46.50 RT, "O,N,L,Y" (4 EA)
 STA 70+05.75 LT, ARROW (1EA)
 STA 70+05.75 RT, ARROW (1EA)
 STA 72+38.88 RT, "S,T,O,P" (4 EA)

646.692 TEMPORARY LETTER OR SYMBOL, PAINT
 U.S. ROUTE 7:
 STA 70+05.75 LT, ARROW (2 EA)
 STA 70+05.75 RT, ARROW (2 EA)
 STA 72+45.28 RT, "S,T,O,P" (4 EA)

646.702 TEMPORARY CROSSWALK MARKING, PAINT
 U.S. ROUTE 7:
 STA 72+38.88 RT, NORTON PLACE

646.502 DURABLE CROSSWALK MARKING, THERMOPLASTIC
 U.S. ROUTE 7:
 STA 72+38.88 RT, NORTON PLACE

675.50 REMOVING SIGNS AS SHOWN - 7
 675.60 ERECTING SALVAGED SIGNS AS SHOWN - 2

PROJECT LAYOUT SHEET #8

PROJECT NAME: RUTLAND CITY
 PROJECT NUMBER: NH 2605(1)S
 FILE NAME: p06d050.dgn
 PROJECT LEADER: DEG
 DESIGNED BY: MJL
 IPARM FILE: p06d050108.1
 PLOT DATE: 03-AUG-2012 12:2
 DRAWN BY: C&K
 CHECKED BY: DWE
 SHEET 20 OF 76
