

TEMPORARY 4 INCH WHITE LINE, PAINT
 DURABLE 4 INCH WHITE LINE, POLYUREA
 402+50 TO 408+50 SOLID LT
 402+50 TO 404+30 SOLID RT
 404+30 TO 404+55 SOLID RT (TH 29)
 404+77 TO 405+07 SOLID RT (TH 29)
 405+07 TO 408+50 SOLID RT

TEMPORARY 4 INCH YELLOW LINE, PAINT
 DURABLE 4 INCH YELLOW LINE, POLYUREA
 402+50 TO 404+50 SOLID LT & RT
 404+66 TO 404+69 DOUBLE SOLID RT (TH 29)
 404+90 TO 408+50 SOLID LT & RT

TEMPORARY 24 INCH STOP BAR, PAINT
 DURABLE 24 INCH STOP BAR (OPTION BID ITEM)
 404+70 TO 404+87 RT (TH 29)

TEMPORARY LETTER OR SYMBOL, PAINT
 DURABLE LETTER OR SYMBOL (OPTION BID ITEM)
 404+75 RT - "STOP" (TH 29)

STEEL BEAM GUARDRAIL, GALVANIZED
 406+50 TO 406+62.5 LT
 406+75.5 TO 406+88 RT

STEEL BEAM GUARDRAIL,
 GALVANIZED W/8 FEET POSTS
 406+62.5 TO 408+50 LT
 406+88 TO 408+50 RT

ANCHOR FOR STEEL BEAM RAIL
 2 (SEE STANDARD G-1d)

REMOVAL AND DISPOSAL OF GUARDRAIL
 406+50 TO 408+50 LT
 406+90 TO 408+50 RT



DELINEATOR WITH STEEL POST
 406+50 LT
 406+75.5 RT

MILLED RUMBLE STRIPS
 402+50 TO 404+50 CL
 404+90 TO 408+50 CL

PROJECT DEMARCATION FENCE
 407+05 TO 408+15 RT

REMOVING SIGNS
 AS SHOWN - 3

CURVE (50)
 DELTA = 0° 18' 44" LT
 D = 0° 34' 23"
 R = 10000.00'
 T = 27.24'
 L = 54.47'
 E = 0.04'
 BANK = NC

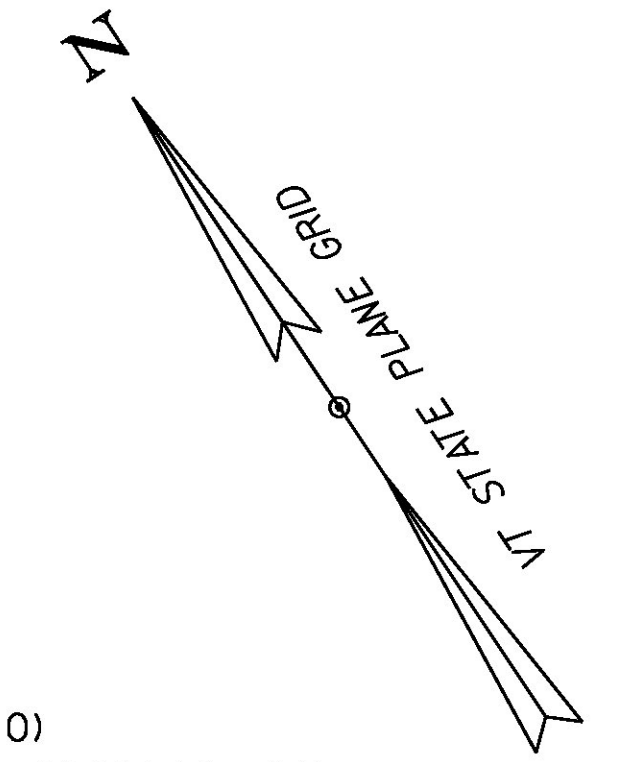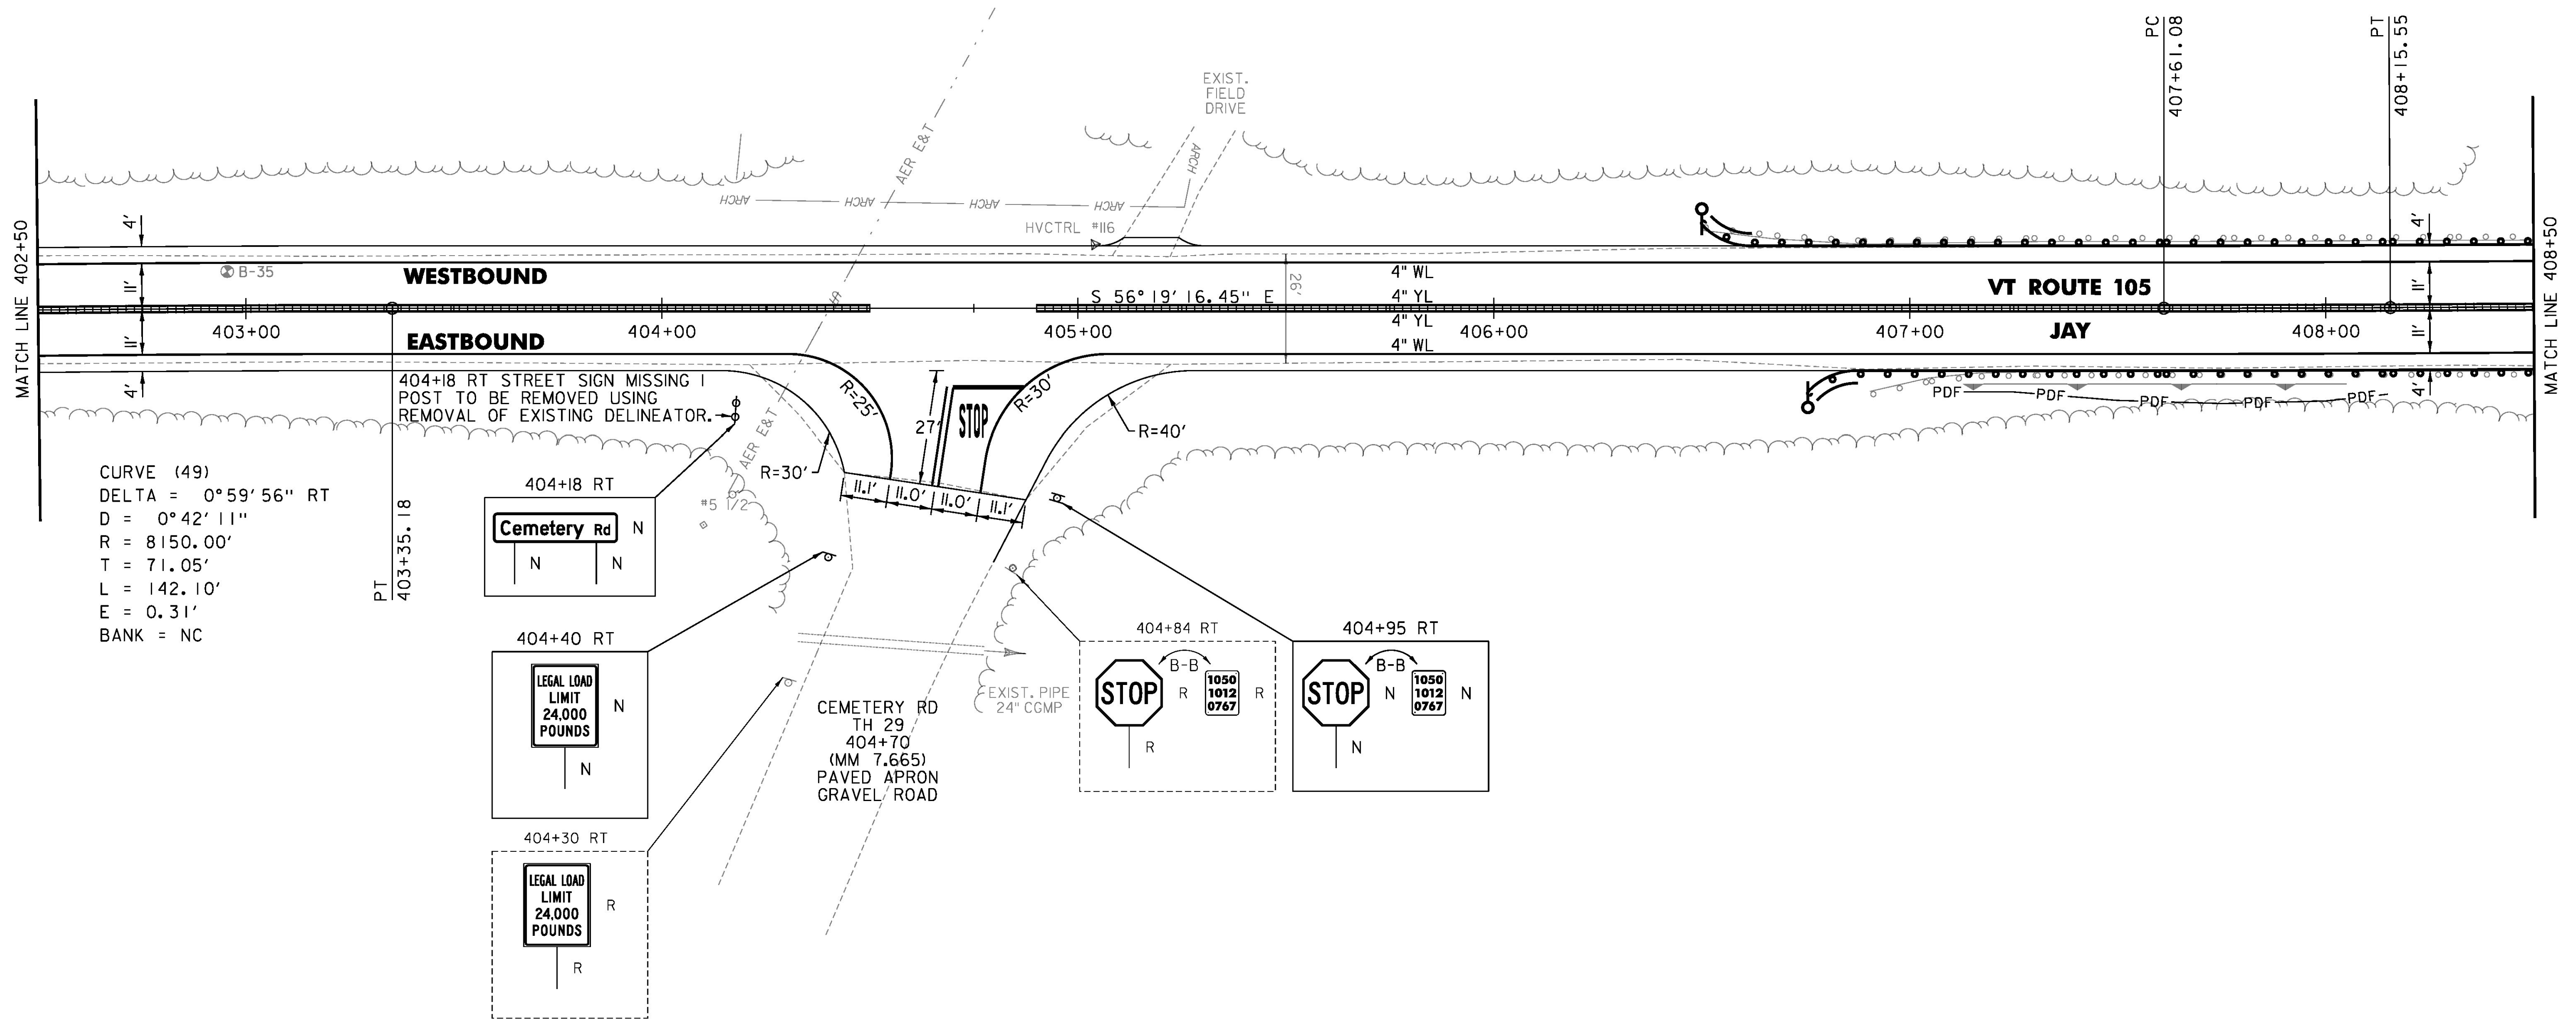

PROJECT NAME:	JAY-TROY
PROJECT NUMBER:	STP 2915(I)
FILE NAME:	z10b232bdr.dgn
PROJECT LEADER:	P. SHEDD
DESIGNED BY:	N. LEMAY
PLAN SHEET	63
PLOT DATE:	5/16/2014
DRAWN BY:	W. GORDON
CHECKED BY:	P. SHEDD
SHEET	96 OF 244
