

TEMPORARY 4 INCH WHITE LINE, PAINT
 DURABLE 4 INCH WHITE LINE (OPTION ITEM)
 N 307+50 TO N 313+50 SOLID LT & RT

TEMPORARY 4 INCH YELLOW LINE, PAINT
 DURABLE 4 INCH YELLOW LINE, EPOXY PAINT OR
 DURABLE 4 INCH YELLOW LINE, POLYUREA (OPTION ITEM)
 N 307+50 TO N 308+35 DASHED LT, SOLID RT
 N 308+35 TO N 313+50 SOLID LT & RT


REHAB. DROP INLETS, CATCH BASINS,
 OR MANHOLES, CLASS I, CLASS II
 N 308+33 LT
 N 309+01 RT

STEEL BEAM GUARDRAIL, GALVANIZED
 N 307+50 TO N 308+20 LT
 N 307+50 TO N 308+86.5 RT
 N 312+14.5 TO N 313+50 LT
 N 312+78.5 TO N 313+50 RT

MILLED RUMBLE STRIPS
 N 307+50 TO N 313+50 CL

REMOVING SIGNS
 AS SHOWN - 6

REMOVAL AND DISPOSAL OF GUARDRAIL
 N 307+50 TO N 308+20 LT
 N 307+50 TO N 308+86.5 RT
 N 312+14.5 TO N 313+50 LT
 N 312+78.5 TO N 313+50 RT

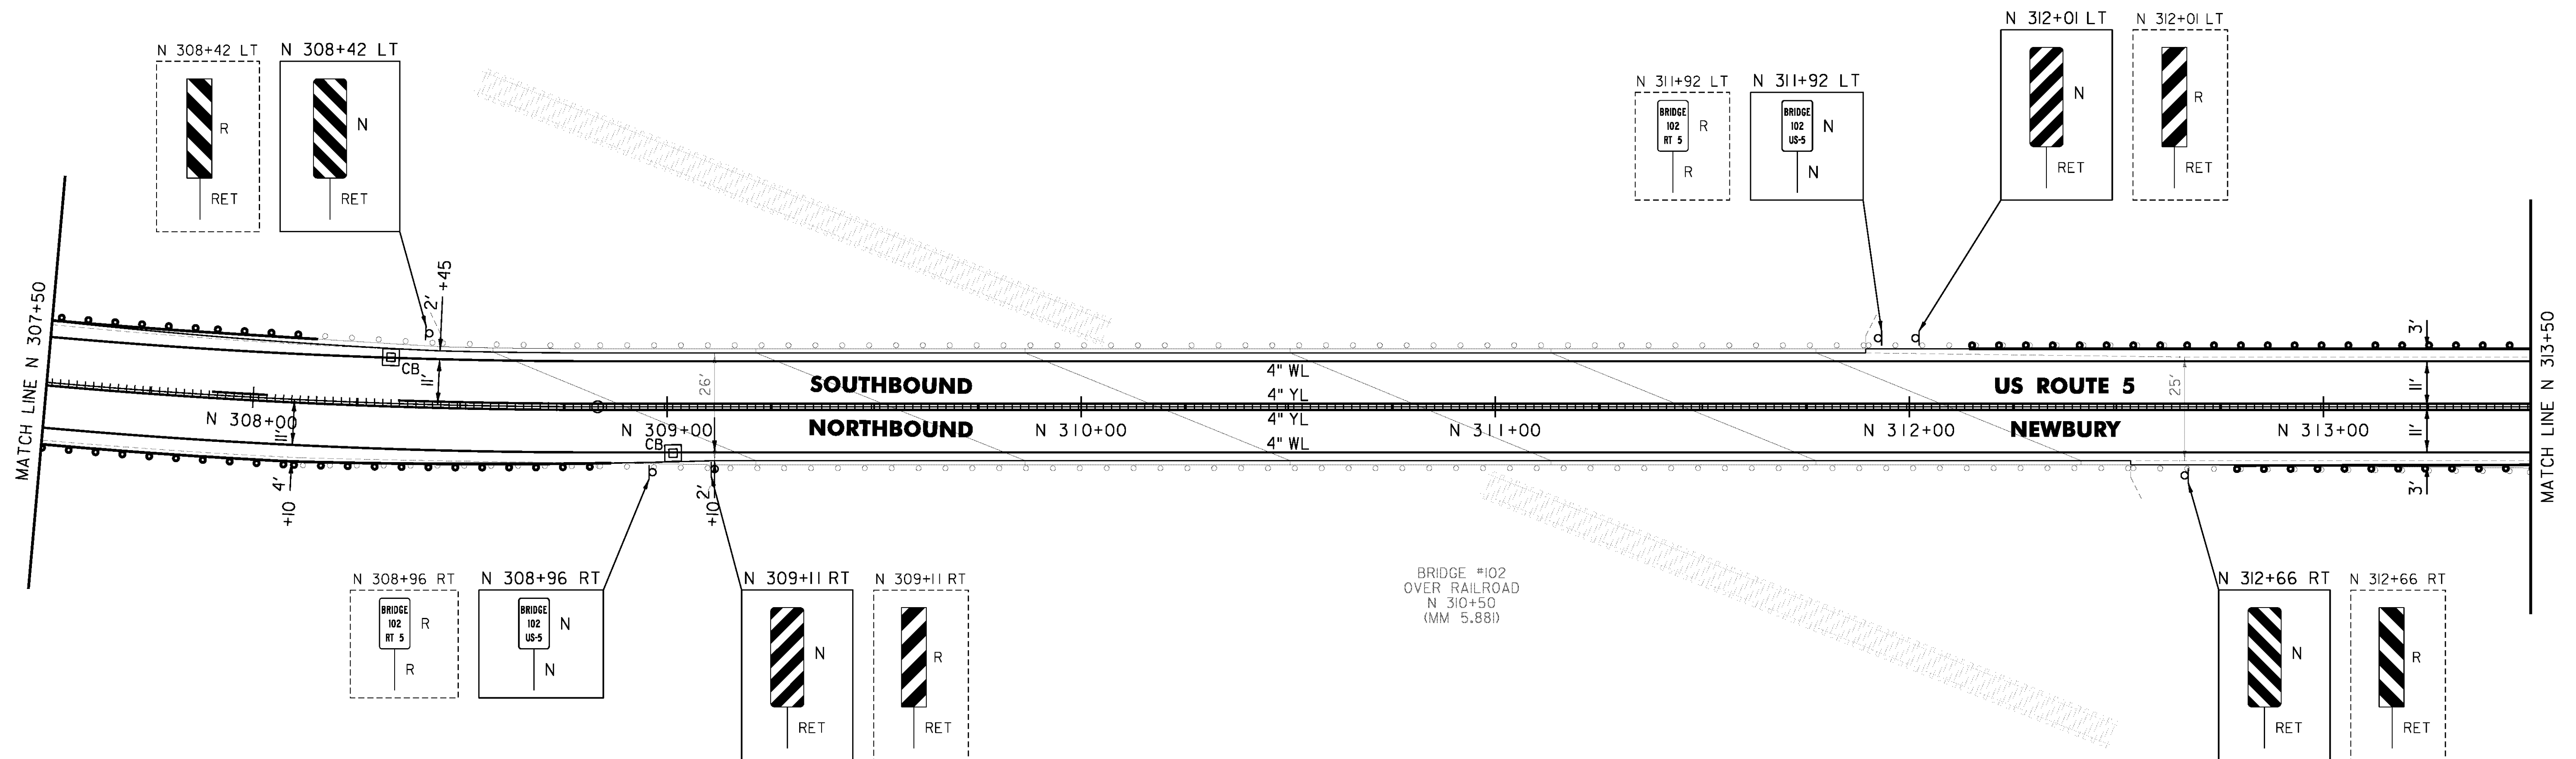

NOT TO SCALE

PROJECT NAME: BRADFORD-RYEGATE	PLOT DATE: 2/4/2016
PROJECT NUMBER: STP 2929(I)	DRAWN BY: W. GORDON
FILE NAME: z10c264bdr.dgn	CHECKED BY: P. SHEDD
PROJECT LEADER: P. SHEDD	SHEET 150 OF 239
DESIGNED BY: N. LEMAY	
US 5 PLAN SHEET 92	
