

MILLED RUMBLE STRIPS (CENTERLINE)
 STA. B 167+00 TO B 172+00, CL

ANCHOR FOR STEEL BEAM RAIL
 STA. B 167+60.0, RT
 STA. B 168+2.5, LT
 STA. B 170+85.0, RT
 STA. B 171+00.0, LT

DURABLE 4 INCH WHITE LINE, (OPTION CC BID ITEMS)
 TEMPORARY 4 INCH WHITE LINE, PAINT
 (ALL LINES WILL INCLUDE EDGE LINE BREAKS
 AND RADII FOR SIDE ROADS)
 STA. B 167+00 TO B 172+00, SOLID LT & RT



DURABLE 4 INCH YELLOW LINE, (OPTION DD BID ITEMS)
 TEMPORARY 4 INCH YELLOW LINE, PAINT
 (ALL LINES WILL INCLUDE C. BREAKS FOR SIDE ROADS)
 STA. B 167+00 TO B 169+49, SOLID LT, DASHED RT
 STA. B 169+49 TO B 172+00, DASHED CL

REMOVING SIGNS
 AS SHOWN - 1

STONE FILL, TYPE J
 SLOPE EROSION PREVENTION WITH GUARDRAIL:
 STA. B 168+13 TO B 171+00, LT
 (SEE SHEET 19)

REMOVAL AND DISPOSAL OF GUARDRAIL
 STA. B 167+21.0 TO B 172+00.0, LT
 STA. B 167+42.0 TO B 171+54.5, RT

STEEL BEAM GUARDRAIL, GALVANIZED
 STA. B 167+60.0 TO B 170+85.0, RT
 STA. B 168+12.5 TO B 171+00.0, LT
 167+76 172+00

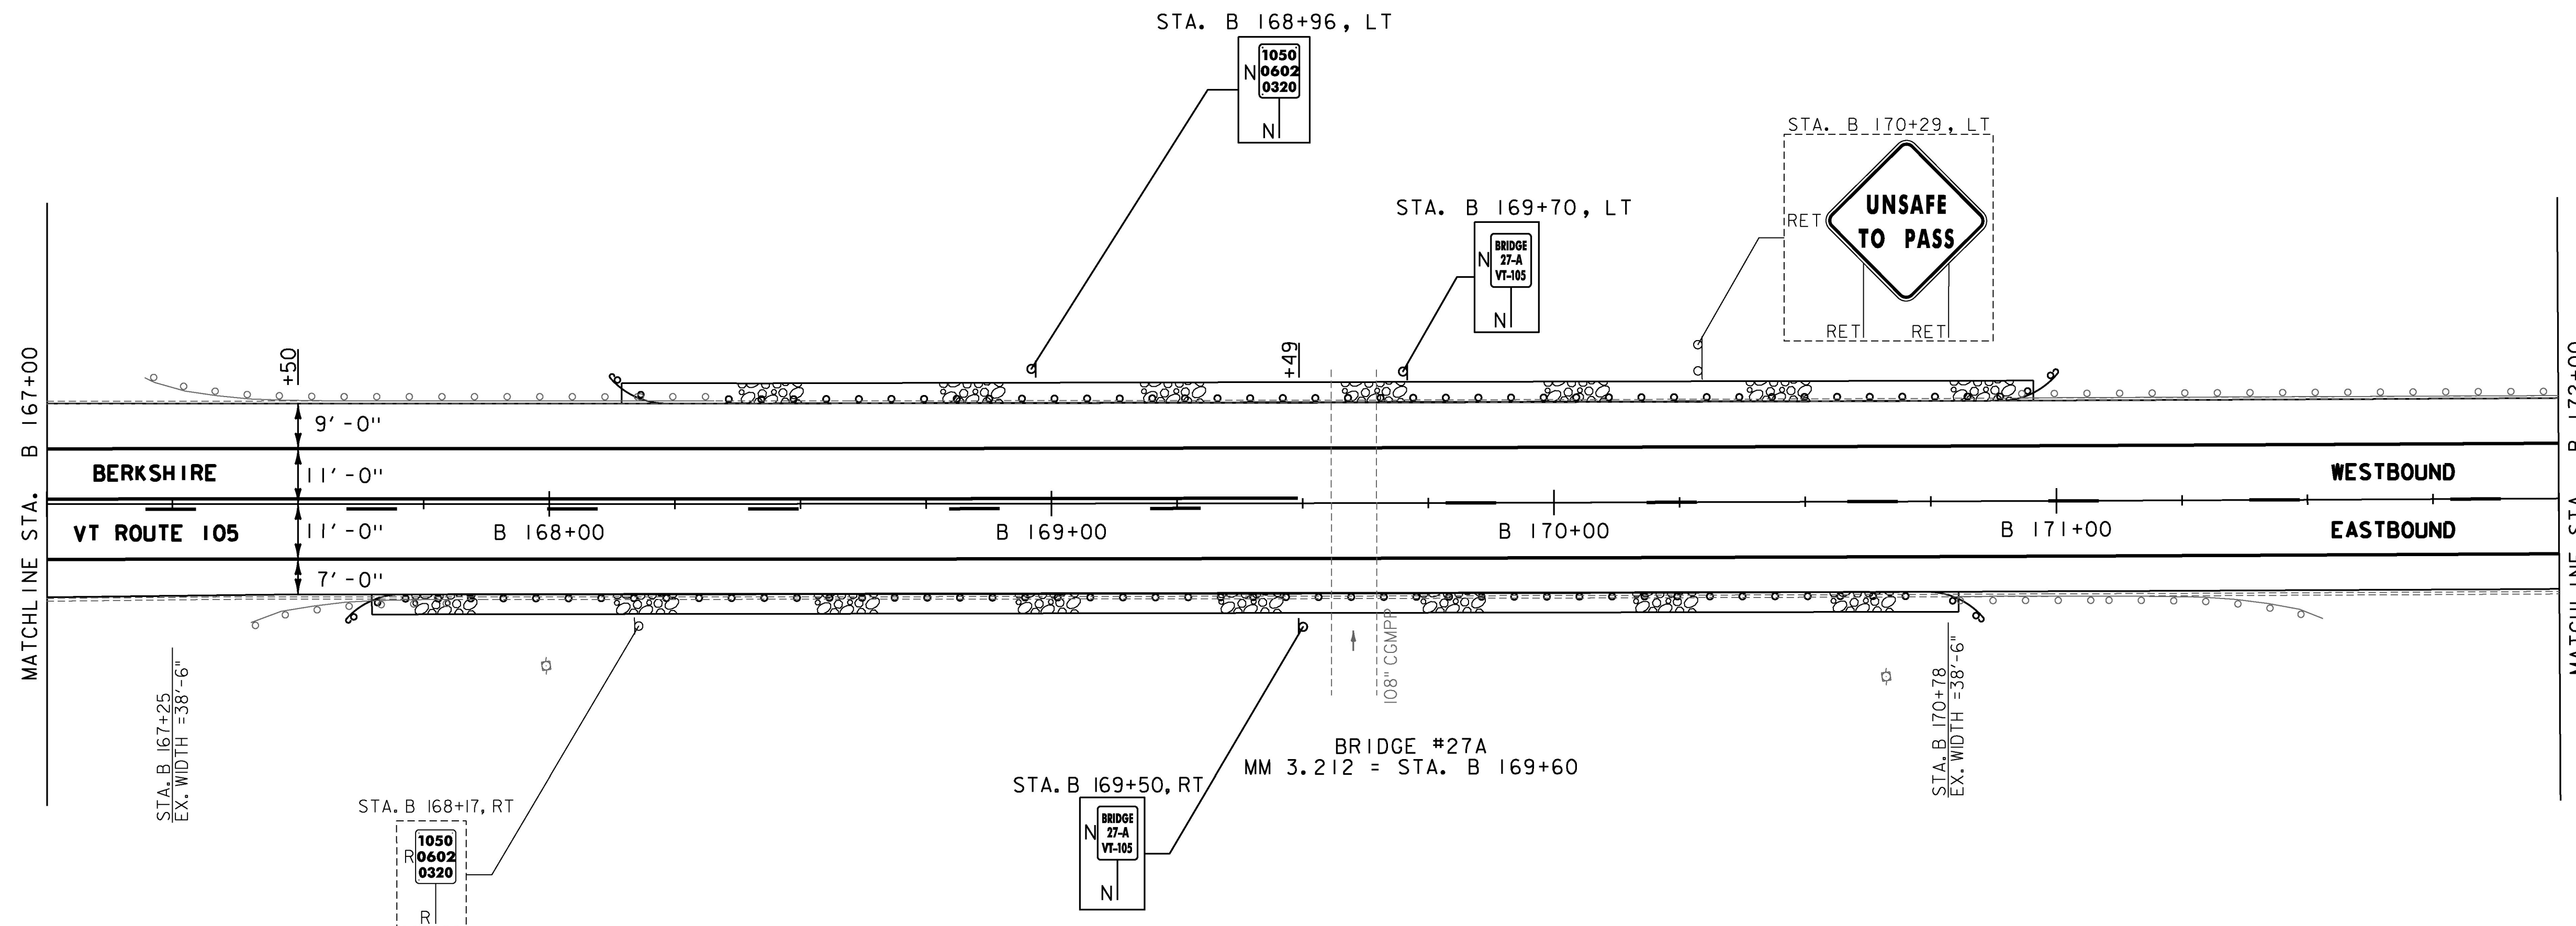

- NOTES:
- FOR LEGENDS, SEE SHEETS 3 & 3I.
 - ALL EXISTING SIGNS NOT SHOWN ON THE PLANS SHALL BE RETAINED.
 - ALL UTILITY LOCATIONS SHOWN ARE APPROXIMATE AND SHOULD BE VERIFIED PRIOR TO ANY WORK COMMENCING.



PROJECT NAME:	ENOSBURGH-RICHFORD
PROJECT NUMBER:	STP 2969(I)
FILE NAME:	z16vi04bdr.dgn
PROJECT LEADER:	G. EDWARDS
DESIGNED BY:	G. BURGMEIER
PLAN SHEET 74	
PLOT DATE:	4/2/2018
DRAWN BY:	G. BURGMEIER
CHECKED BY:	J. LITTLE
SHEET	104 OF 222

