

WORK ORDER

BREAK INTO EXISTING CONDUIT STRUCTURE JOIN NEW DUCTS TO EXISTING DUCTS TO POLE # 3 CAP DUCTS GOING BACK TO MH# 11

existing conduit to Pole#3
2 - 4" PC

SURVEY MARKER
existing sign


Notice: Not for Use/disclosure outside of BELL ATLANTIC without written agreement

BELL ATLANTIC

SAFETY NOTES: ROAD CONSTRUCTION		MOD/REV NO.	DATE	EWO NO.
				PRINT 1 OF
		PREPARED BY: J. BRIAN GRESL		
		C.O. /EXCHANGE NAME: S. ROYALTON		
SIGNATURE DATE 05/01/2000		TYPE AERIAL	RECORD REF: 5	C.O. /EXCHANGE CODE: 4875
PRE CT YES <input type="checkbox"/> NO <input checked="" type="checkbox"/>		UNDERGROUND		MUNICIPALITY: ROYALTON
PRIMARY VOLTAGE TO GROUND 7.2 KV MGN SYSTEM		BLOCK (NYT) CONDUIT	4	
CABLE PRESS.	UNDER PRESS. YES <input type="checkbox"/> NO <input checked="" type="checkbox"/>	BUFFER YES <input type="checkbox"/> NO <input checked="" type="checkbox"/>	MANHOLE LOCATION MH# NA	
TRANSMISSION	28GA LIMIT YES <input type="checkbox"/> NO <input checked="" type="checkbox"/>	AMT. BRIDGE TAP INPUT	KF	

PROJECT - 131154

SEE PLAN # 2

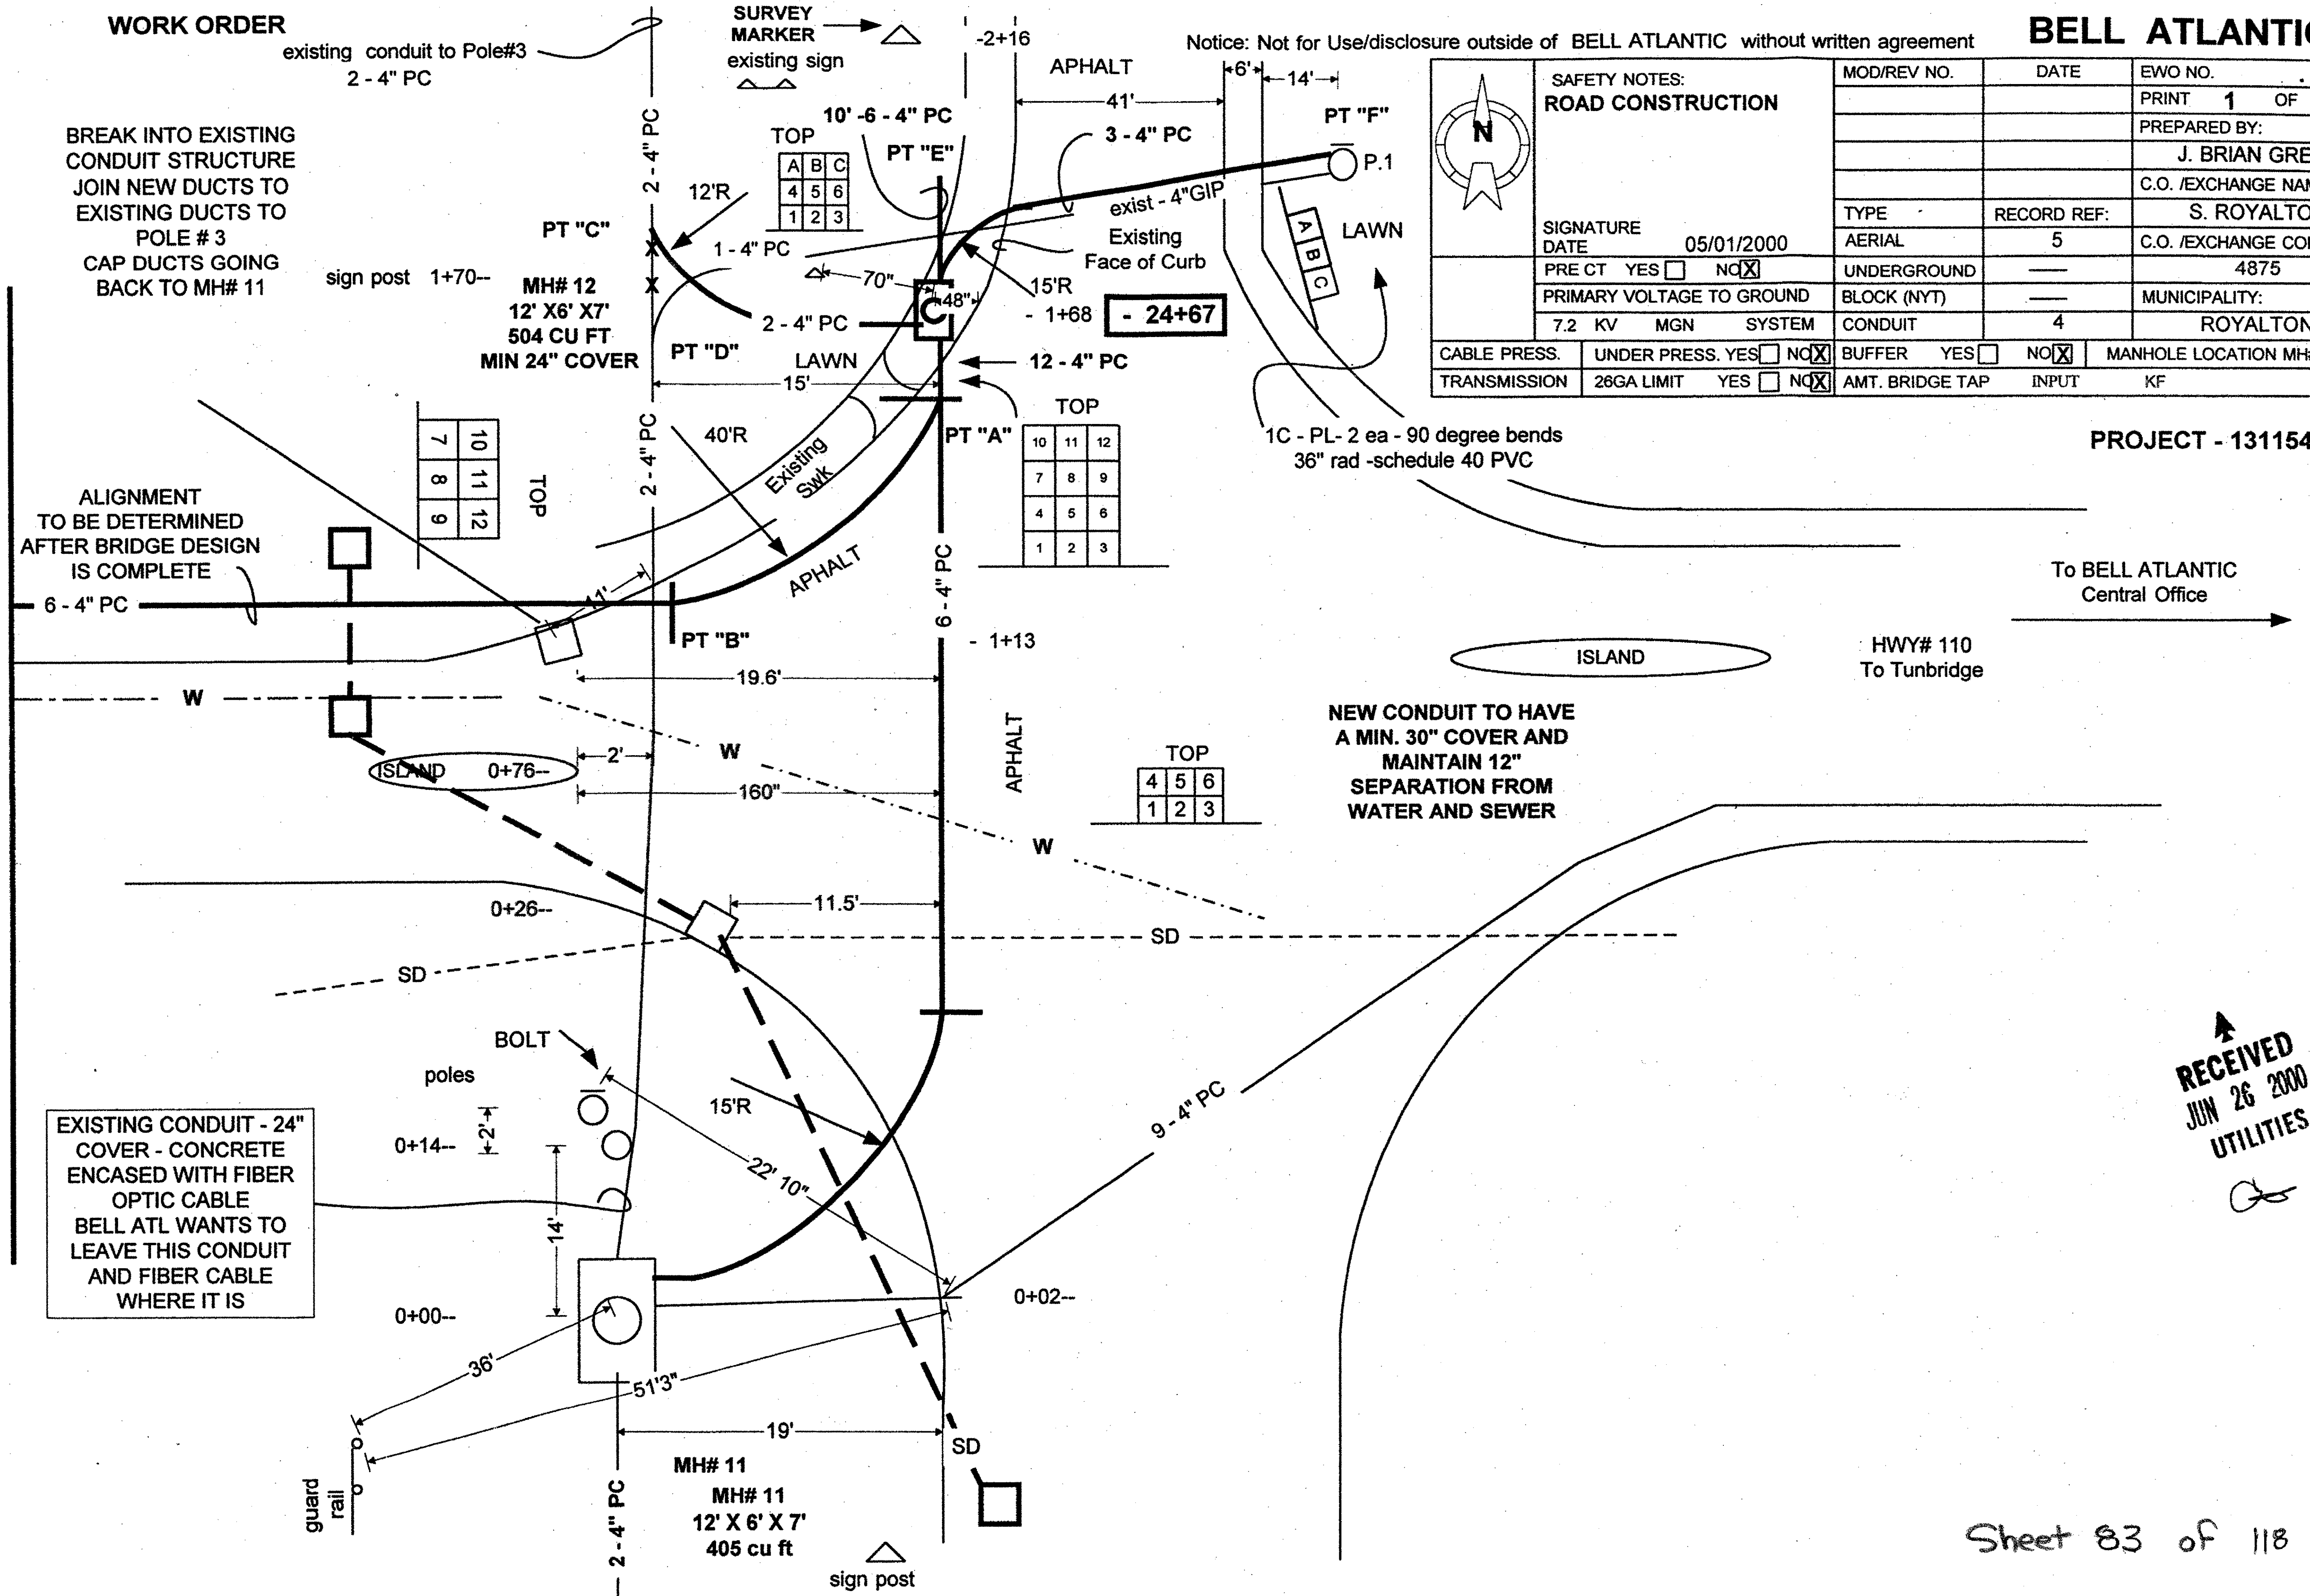

To BELL ATLANTIC
Central Office

HWY# 110
To Tunbridge

NEW CONDUIT TO HAVE
A MIN. 30" COVER AND
MAINTAIN 12"
SEPARATION FROM
WATER AND SEWER

EXISTING CONDUIT - 24"
COVER - CONCRETE
ENCASED WITH FIBER
OPTIC CABLE
BELL ATL WANTS TO
LEAVE THIS CONDUIT
AND FIBER CABLE
WHERE IT IS

RECEIVED
JUN 26 2000
UTILITIES

6/23/00
