

CHANGING ELEVATION OF DROP INLETS,
CATCH BASINS, OR MANHOLES

BENNINGTON:
MM 5.762 RT
MM 5.769 LT
MM 5.788 LT
MM 5.788 RT
MM 5.811 LT
MM 5.811 RT
MM 5.842 RT

CHANGING ELEVATION OF SEWER MANHOLES
(ELEVATION ADJUSTMENT BY OTHERS)

BENNINGTON:
MM 5.763 CL
MM 5.814 CL
MM 5.868 CL

TEMPORARY 4 INCH WHITE LINE, PAINT &
DURABLE 4 INCH WHITE LINE (OPTION BID ITEM)
(ALL LINES WILL INCLUDE EDGE LINE BREAKS AND
RADIUS FOR TOWN HIGHWAYS)

BENNINGTON:
MM 5.752 - 5.765 SOLID LT
MM 5.752 - 5.871 SOLID RT
MM 5.752 - 5.779 SOLID RT (LANE LINE)
MM 5.779 - 5.786 DOTTED RT TO LT
MM 5.791 - 5.799 DOTTED LT TO RT
MM 5.802 - 5.829 SOLID LT
MM 5.826 - 5.844 DOTTED RT
MM 5.837 - 5.858 DOTTED LT
MM 5.844 - 5.869 SOLID RT (LANE LINE)
MM 5.858 - 5.871 SOLID LT

TEMPORARY 4 INCH YELLOW LINE, PAINT &
DURABLE 4 INCH YELLOW LINE (OPTION BID ITEM)
(ALL LINES WILL INCLUDE C/L BREAKS FOR
TOWN HIGHWAYS)

BENNINGTON:
MM 5.752 - 5.779 DOUBLE SOLID C/L
MM 5.811 - 5.869 DOUBLE SOLID LT & RT

TEMPORARY 6 INCH WHITE LINE, PAINT &
DURABLE 6 INCH WHITE LINE, POLYUREA

BENNINGTON:
MM 5.762 - 5.763 SOLID LT
MM 5.787 - 5.791 SOLID LT
MM 5.800 - 5.802 SOLID LT
MM 5.827 - 5.869 SOLID LT

TEMPORARY 6 INCH YELLOW LINE, PAINT &
DURABLE 6 INCH YELLOW LINE, POLYUREA

BENNINGTON:
MM 5.763 - 5.769 SOLID LT
MM 5.793 - 5.794 SOLID LT
MM 5.798 - 5.801 SOLID LT
MM 5.835 - 5.837 SOLID LT

TEMPORARY 8 INCH WHITE LINE, PAINT &
DURABLE 8 INCH WHITE LINE (OPTION BID ITEM)

BENNINGTON:
MM 5.763 - 5.768 SOLID LT (GORE)
MM 5.786 - 5.791 SOLID LT (GORE)
MM 5.800 - 5.802 SOLID LT (GORE)
MM 5.828 - 5.837 SOLID LT (DIAGONALS MEDIAN)(106 FT)

TEMPORARY 8 INCH YELLOW LINE, PAINT &
DURABLE 8 INCH YELLOW LINE (OPTION BID ITEM)

BENNINGTON:
MM 5.793 - 5.798 SOLID LT
MM 5.811 - 5.868 (GORE W/DIAGONALS)(328 FT)

TEMPORARY 24 INCH STOP BAR, PAINT &
DURABLE 24 INCH STOP BAR (OPTION BID ITEM)

BENNINGTON:
MM 5.779 RT
MM 5.791 LT
MM 5.811 LT

TEMPORARY LETTER OR SYMBOL, PAINT &
DURABLE LETTER OR SYMBOL (OPTION BID ITEM)

BENNINGTON:
MM 5.753 RT - "ONLY" (4 EACH)

MM 5.763 RT - "↑" (1 EACH)

MM 5.763 RT - "↓" (1 EACH)

MM 5.764 LT - "ONLY" (4 EACH)

MM 5.771 RT - "▼▼▼▼" (4 EACH)

MM 5.778 RT - "↑" (1 EACH)


MM 5.778 RT - "↓" (1 EACH)

MM 5.846 RT - "↔" (2 EACH)

MM 5.863 RT - "↔" (2 EACH)

TEMPORARY CROSSWALK MARKING, PAINT &
DURABLE CROSSWALK MARKING (OPTION BID ITEM)

BENNINGTON:
MM 5.873 RT (HARVARD ST.)

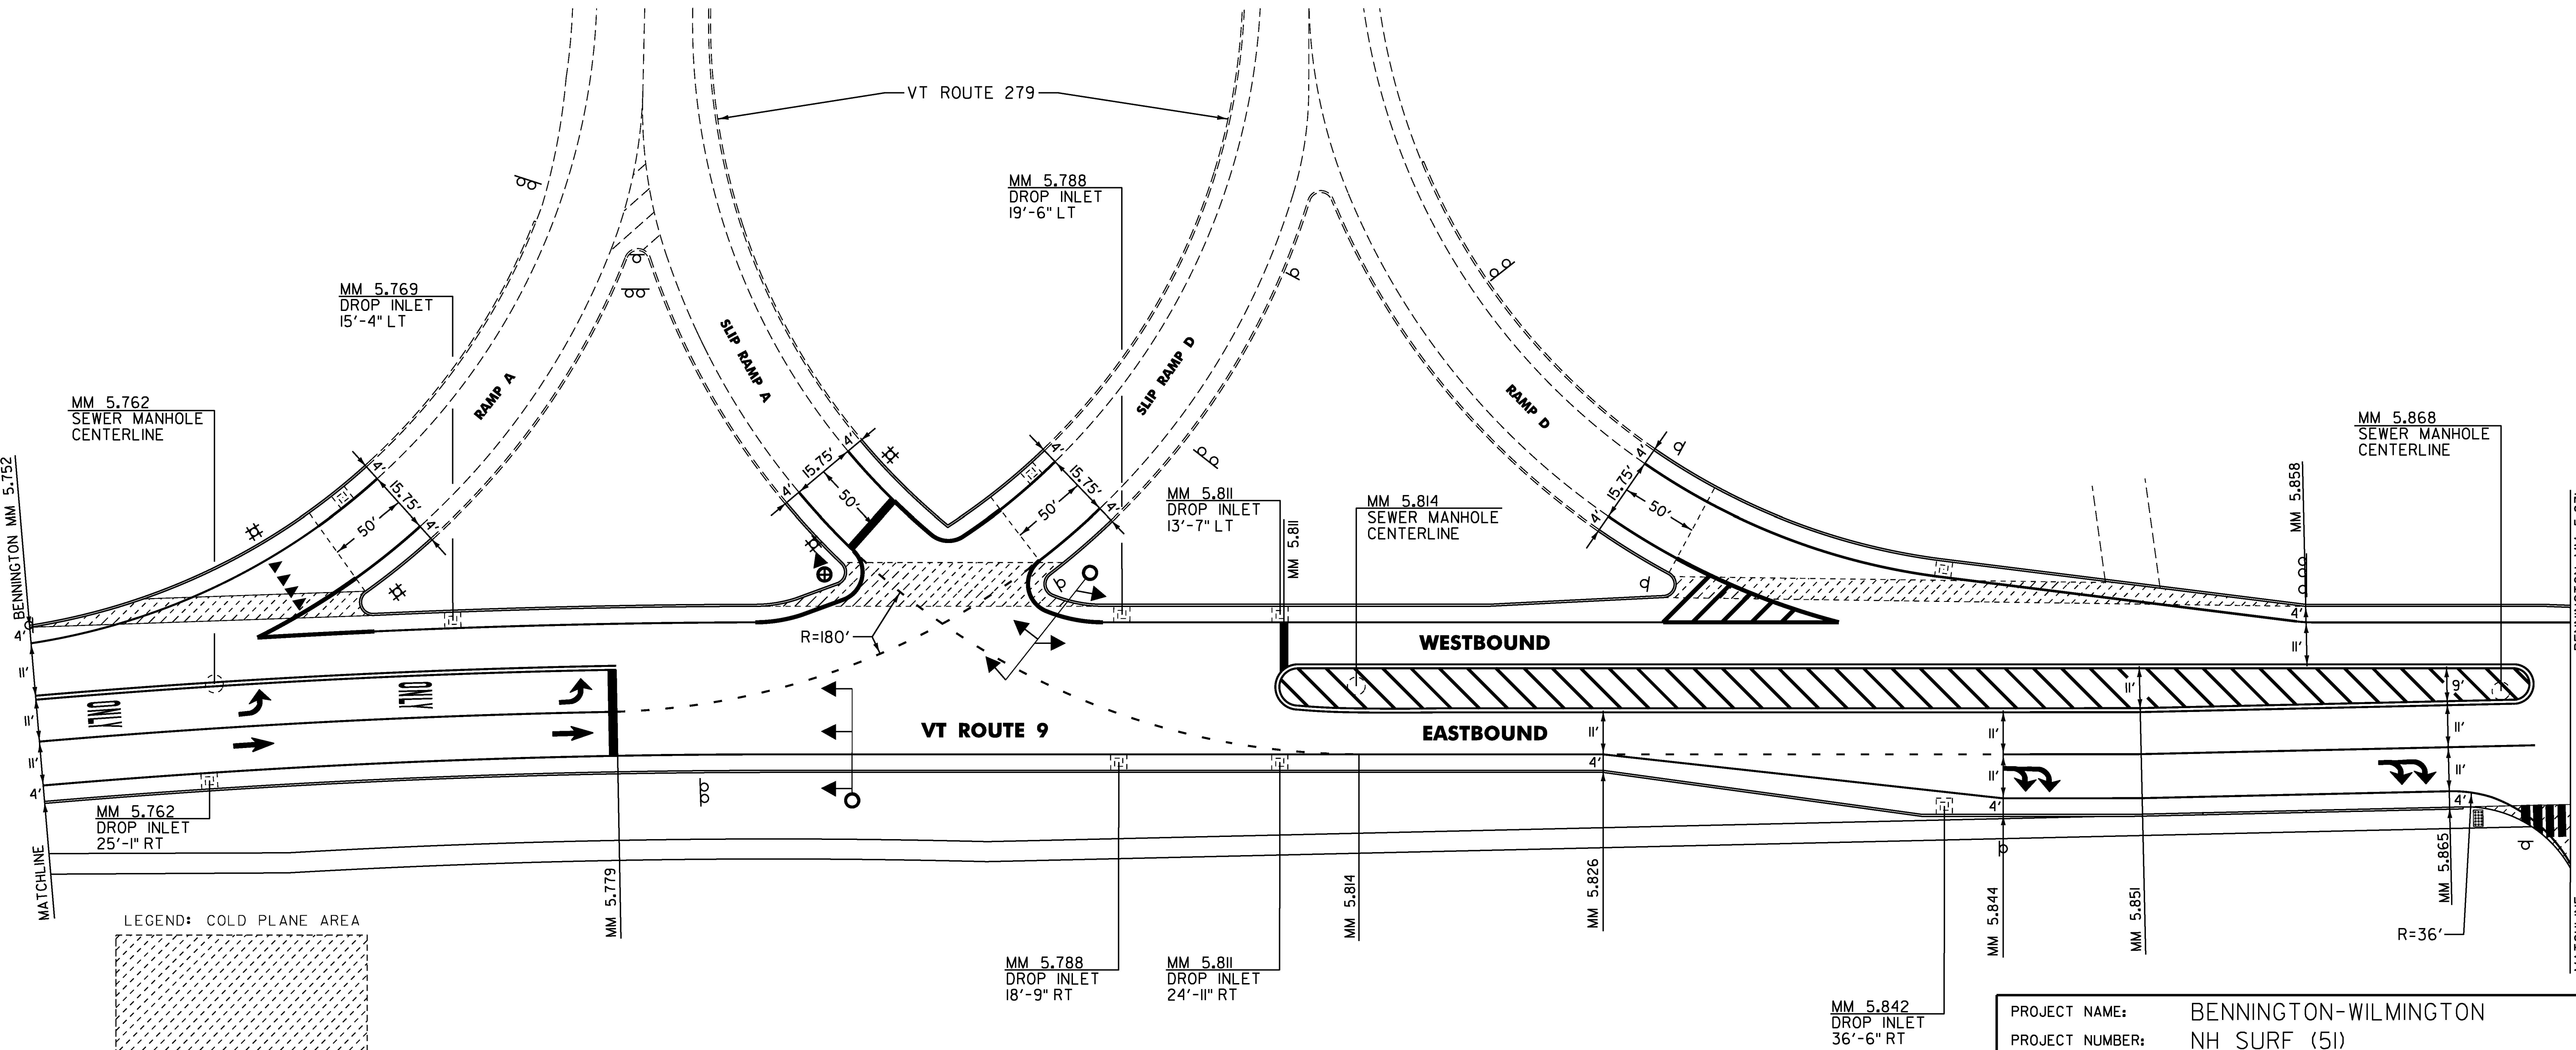

NOT TO SCALE

PROJECT NAME:	BENNINGTON-WILMINGTON
PROJECT NUMBER:	NH SURF (51)
FILE NAME:	p14v201Bennington-Wilmington.dgn
DATE:	28-MAR-2017
PROJECT LEADER:	M. FOWLER
DRAWN BY:	N. PAPPAS
DESIGNED BY:	N. PAPPAS
CHECKED BY:	M. FOWLER
LAYOUT SHEET 9	SHEET 28 OF 64
