


TEMPORARY 4 INCH WHITE LINE, PAINT  
 4 INCH WHITE LINE, WATERBORNE PAINT  
 (ALL LINES WILL INCLUDE EDGE LINE  
 BREAKS AND RADII FOR SIDE ROADS)  
 310+00 TO 338+00 LT & RT (SOL ID)

TEMPORARY 4 INCH YELLOW LINE, PAINT  
 4 INCH YELLOW LINE, WATERBORNE PAINT  
 (ALL LINES WILL INCLUDE  $\phi$   
 BREAKS FOR SIDE ROADS)  
 310+00 TO 338+00 LT & RT (SOL ID)

STEEL BEAM GUARDRAIL, GALVANIZED  
 330+82 TO 331+19.5 RT  
 336+52.5 TO 336+90 RT  
  
 ANCHOR FOR STEEL BEAM RAIL  
 330+94.5 RT  
 336+77.5 RT

ADJUST HEIGHT OF GUARDRAIL  
 331+19.5 TO 331+44.5 RT  
 331+94.5 TO 332+44.5 RT  
 332+92.5 TO 333+17.5 RT  
 333+42.5 TO 333+55 RT  
 333+92 TO 334+04.5 RT  
 334+54.5 TO 334+79.5 RT  
  
 REPLACE GUARDRAIL POST ASSEMBLY  
 REPLACE GUARDRAIL BEAM UNIT  
 333+17.5 TO 333+42.5 RT

REMOVAL AND DISPOSAL OF GUARDRAIL  
 330+82 TO 331+19.5 RT  
 336+52.5 TO 336+90 RT  
  
 DELINEATOR WITH STEEL POST  
 330+82 RT  
 333+55 RT  
 333+92 RT  
 336+90 RT

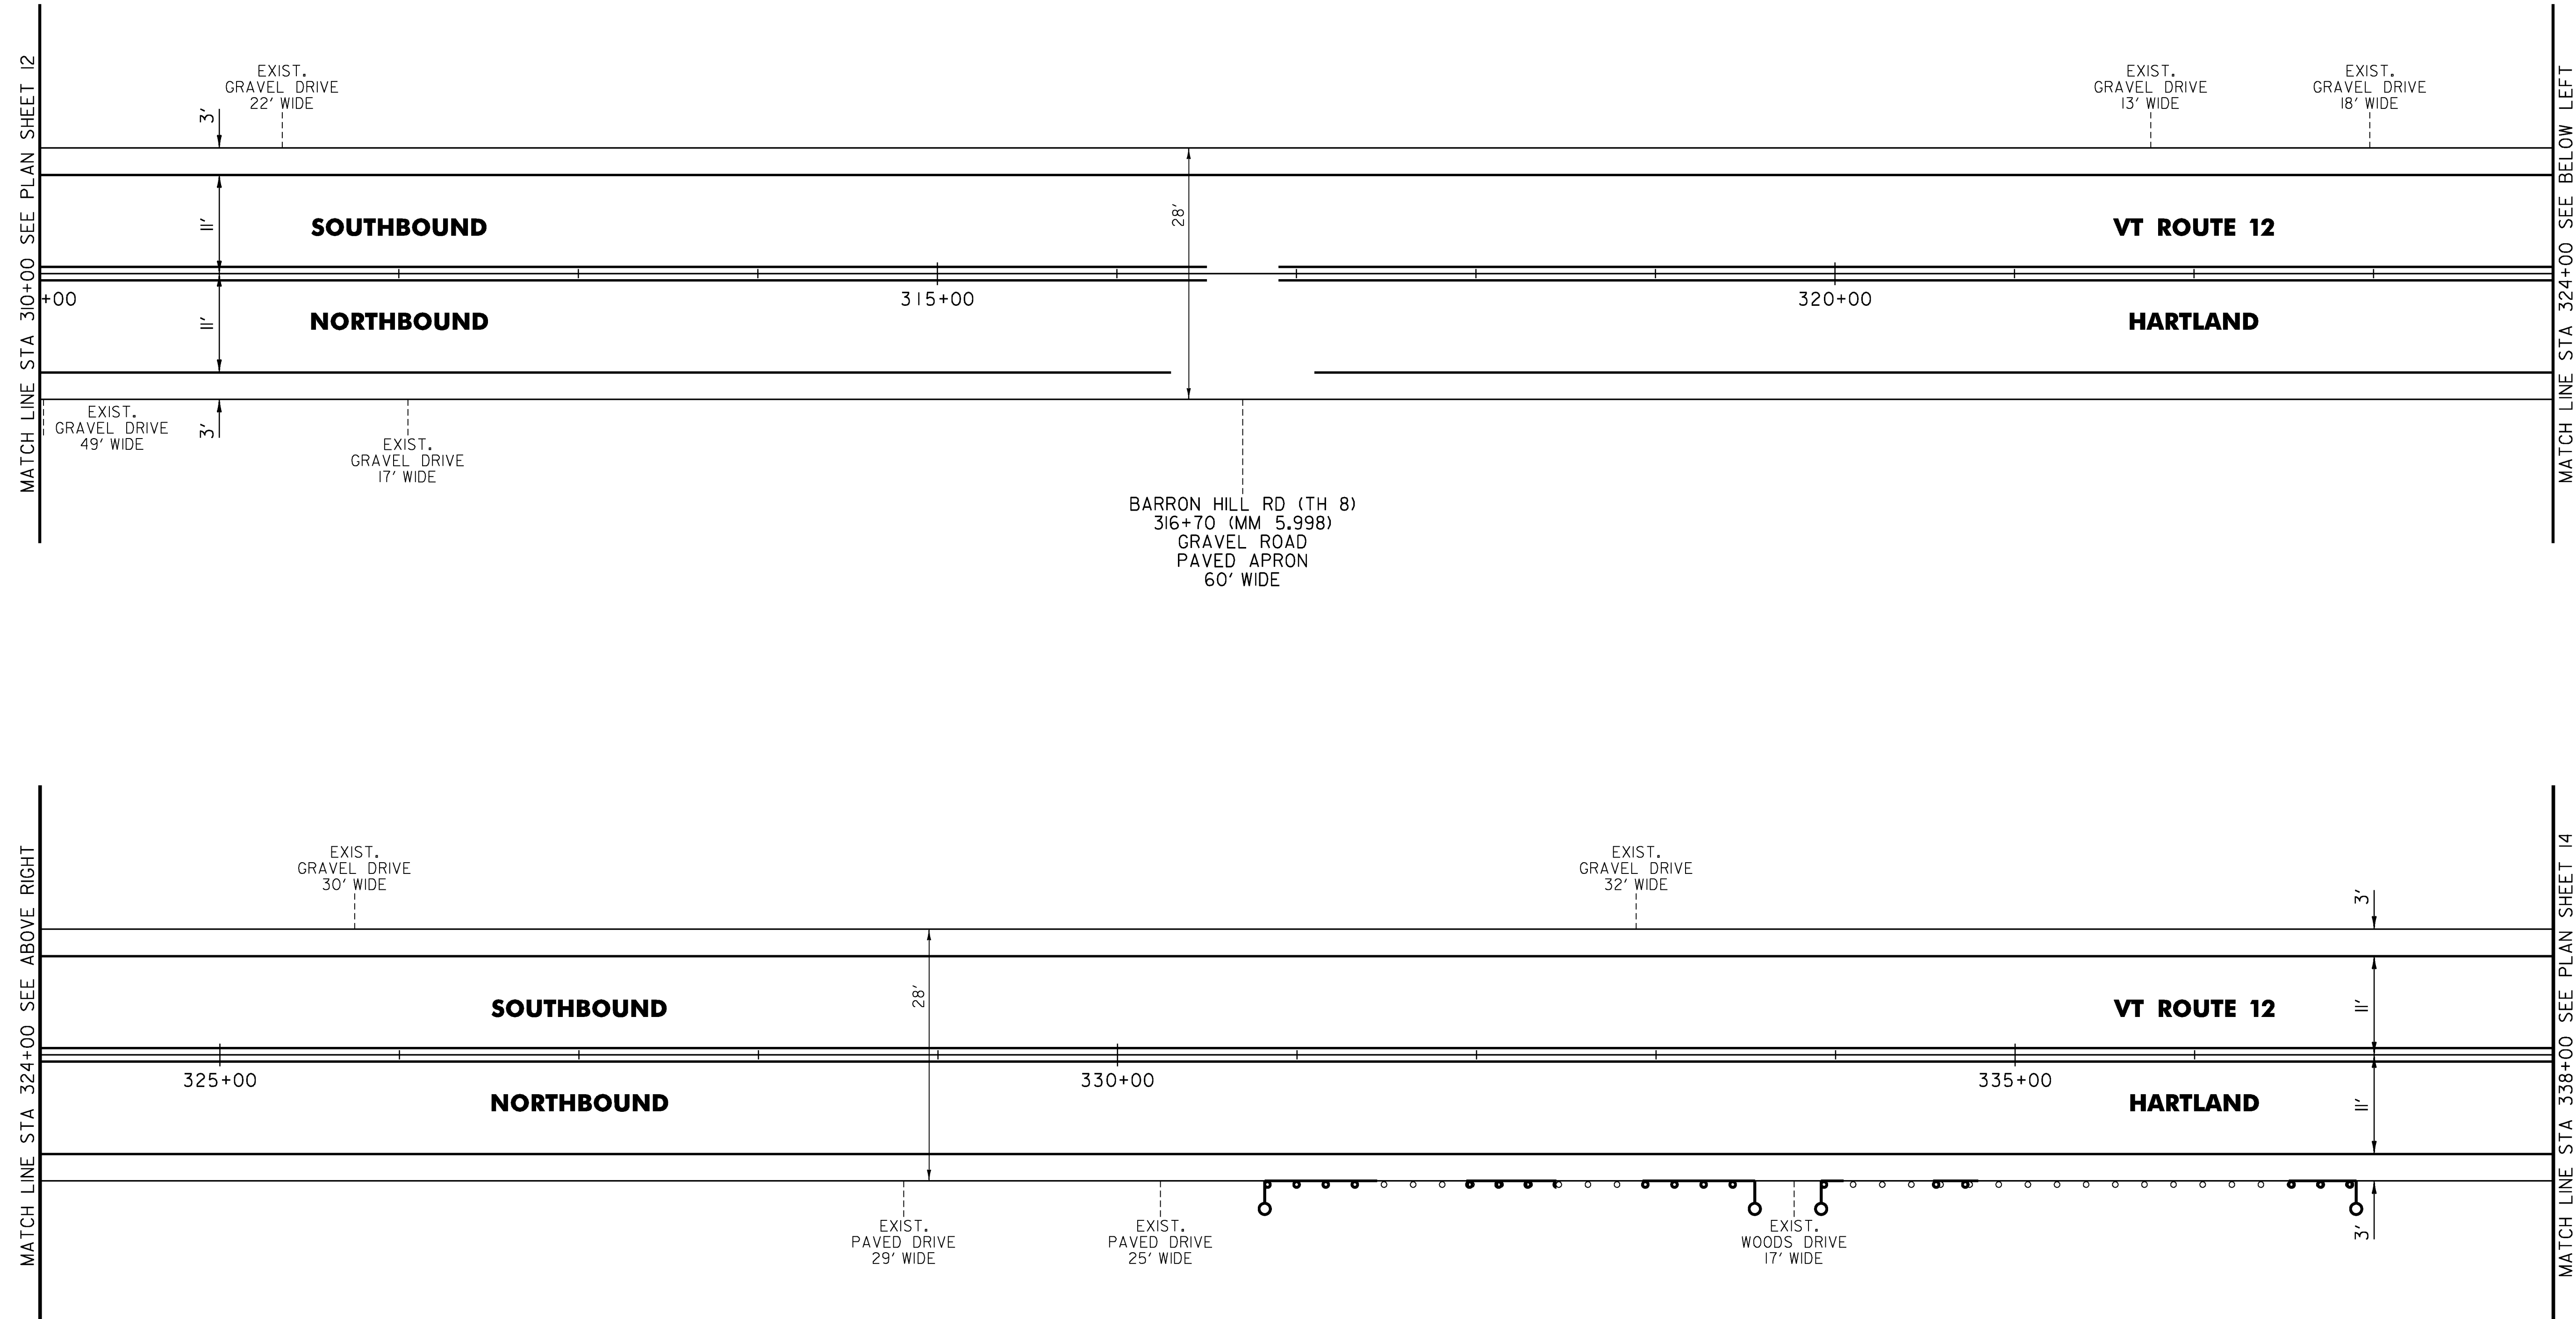

NOT TO SCALE

PROJECT NAME:	HARTLAND
PROJECT NUMBER:	STP FPAV(8)
FILE NAME:	z16vl47bdr.dgn
PROJECT LEADER:	P. SHEDD
DESIGNED BY:	N. LEMAY
PLAN SHEET 13	
PLOT DATE:	4/14/2017
DRAWN BY:	S. GOODWIN
CHECKED BY:	P. SHEDD
SHEET	28 OF 33
