VTrans *Working to Get You There* — Vermont Agency of Transportation

Route Log Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Unit with questions or concerns.

DISTRICT	TOWN	ROUTE
7	LUNENBURG	US-2

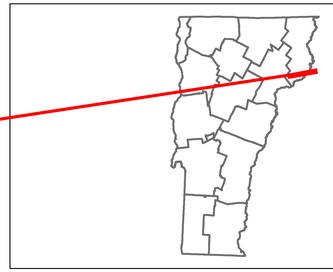

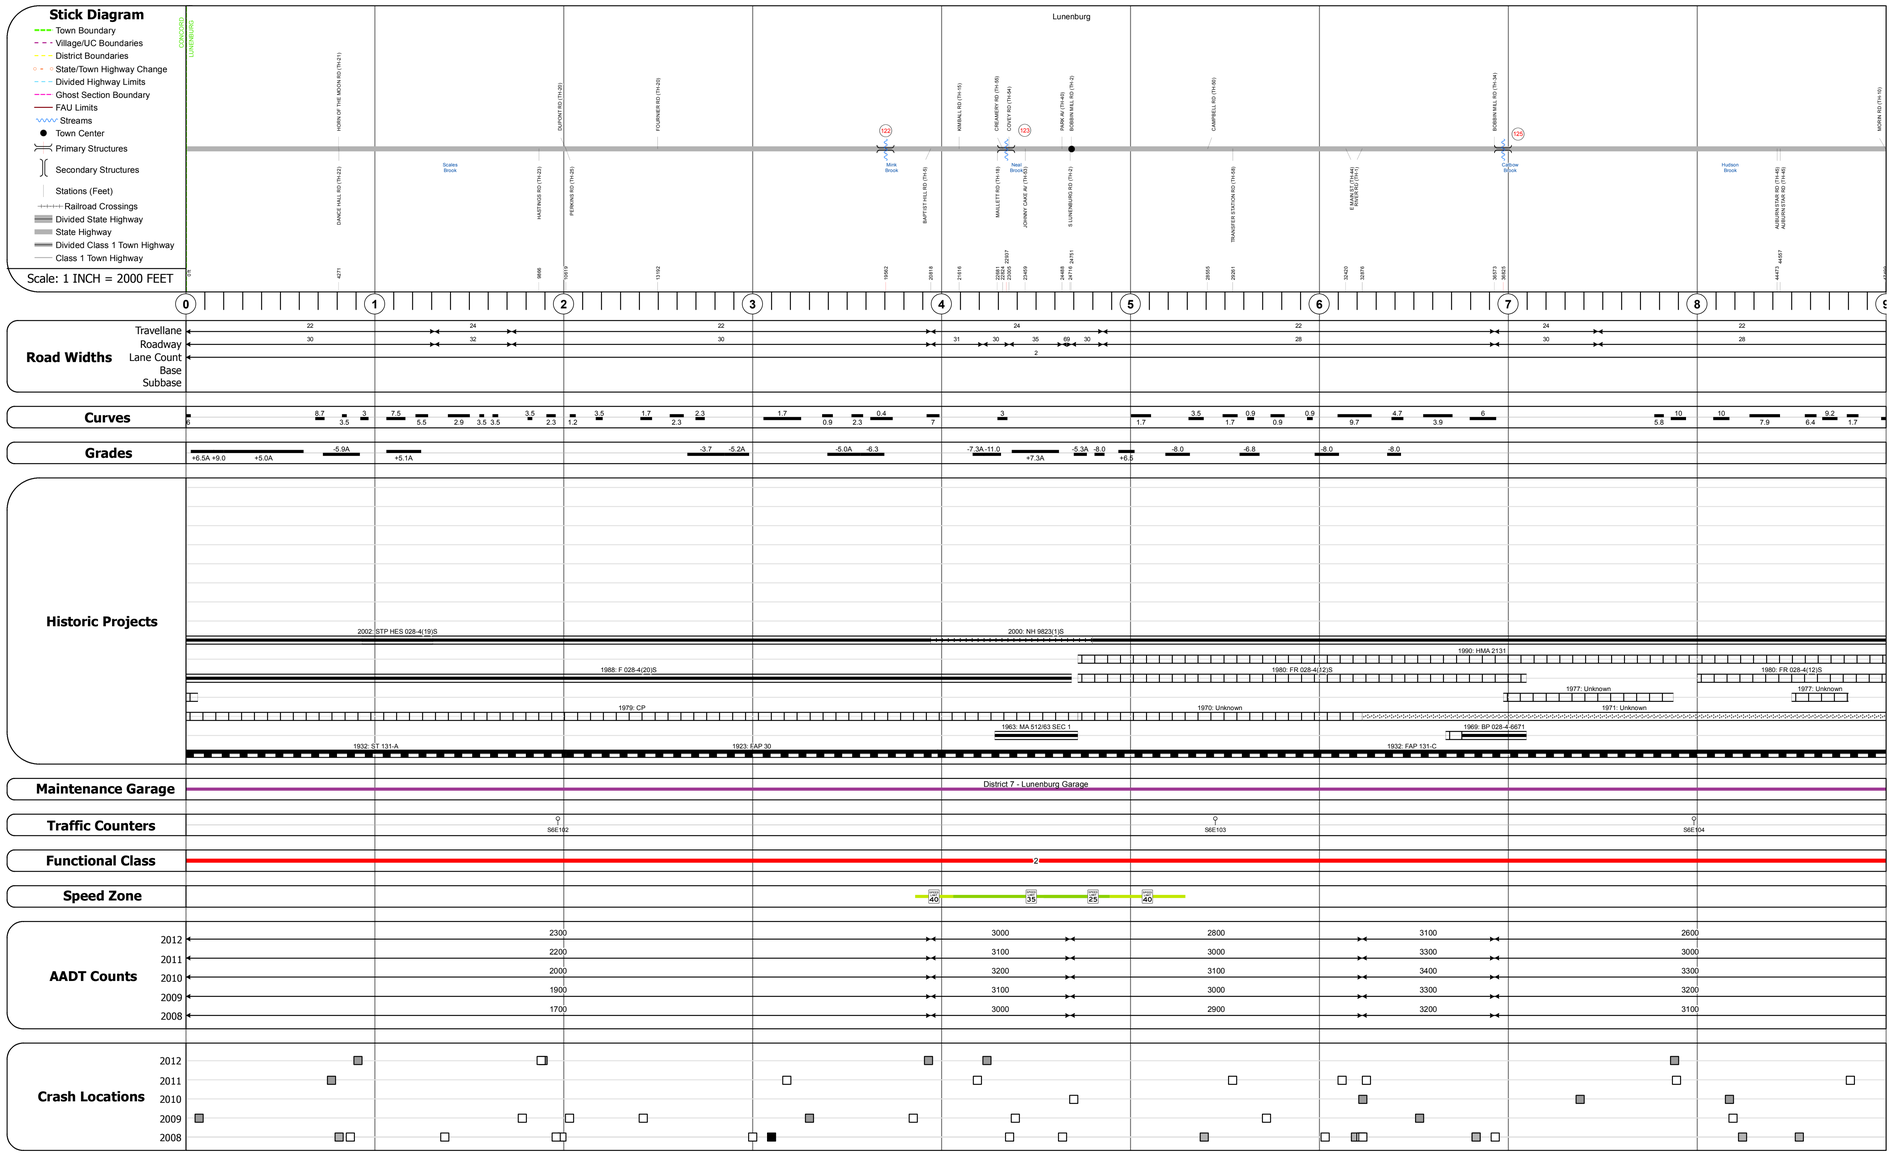

Road Widths

	0	1	2	3	4	5	6	7	8	9
Travellane		22	24	22	24	22		24	22	
Roadway		30	32	30	31 / 30 / 35 / 69 / 30	28		30	28	
Lane Count					2					
Base										
Subbase										

Curves

0	1	2	3	4	5	6	7	8	9
	8.7 3 3.5 7.5 5.5 2.9 3.5 3.5 3.5 2.3 1.2 3.5 1.7 2.3 2.3		1.7 0.9 2.3 0.4 7	3	1.7 3.5 1.7 0.9 0.9		9.7 4.7 3.9 6	5.8 10 10 7.9 6.4 9.2 1.7	

Grades

0	1	2	3	4	5	6	7	8	9
+6.5A +9.0 +5.0A -5.9A	+5.1A		-3.7 -5.2A	-5.0A -6.3	-7.3A -11.0 +7.3A -5.3A -8.0 +6.5	-8.0	-6.8	-8.0	-8.0

Historic Projects

	0	1	2	3	4	5	6	7	8	9
2002: STP HES 028-4(19)S										
2000: NH 9823(1)S										
1990: HMA 2131										
1988: F 028-4(20)S										
1980: FR 028-4(12)S										
1980: FR 028-4(12)S										
1979: CP										
1977: Unknown										
1977: Unknown										
1971: Unknown										
1970: Unknown										
1969: BP 028-4-6671										
1963: MA 512/63 SEC 1										
1932: ST 131-A										
1923: FAP 30										
1932: FAP 131-C										

Maintenance Garage

	0	1	2	3	4	5	6	7	8	9
District 7 - Lunenburg Garage										

Traffic Counters

	0	1	2	3	4	5	6	7	8	9
			S6E102		S6E103			S6E104		

Functional Class

	0	1	2	3	4	5	6	7	8	9
2										

Speed Zone

	0	1	2	3	4	5	6	7	8	9
					40	35	25	40		

AADT Counts

	0	1	2	3	4	5	6	7	8	9
2012		2300		3000		2800	3100		2600	
2011		2200		3100		3000	3300		3000	
2010		2000		3200		3100	3400		3300	
2009		1900		3100		3000	3300		3200	
2008		1700		3000		2900	3200		3100	

Crash Locations

	0	1	2	3	4	5	6	7	8	9
2012										
2011										
2010										
2009										
2008										

DESCRIPTION BLOCK

Bridge 122:
Slab - 1922
Structure No. 300028012205141
Length: 17'
Width: 26.1'
Under Clearance: 6.0'
Facility Carried: US2
Bridge Type: CONCRETE SLAB
Features Intersected: MINK BROOK
Surface: Bituminous
Maintenance: State

Bridge 123:
Arch - deck - 1917
Structure No. 300028012305141
Length: 16'
Under Clearance: 13.0'
Facility Carried: US2
Bridge Type: STONE ARCH
Features Intersected: NEAL BROOK
Maintenance: State

Culvert 125:
Culvert - 1915
Structure No. 300028012505141
Length: 11'
Under Clearance: 11.0'
Facility Carried: US2
Bridge Type: CGMPP
Features Intersected: CATSBOW BROOK
Maintenance: State

Historic Projects
Retreatment; Resurface; Unknown; Bituminous Mix; Skinny Mix; Bituminous Seal; Bituminous Concrete; Bituminous Macadam; Cold Plane and Bituminous Concrete; Concrete; Gravel; Surface Treated Gravel; Plant Mix; Reclaimed Base and Bituminous Concrete

Functional Class
1 Interstate; 2 Principal Arterial; 6 Minor Arterial; 7 Major Collector; 8 Minor Collector; 11 Local; 12 Principal Arterial - Interstate; 14 Minor Arterial - Interstate; 16 Major Collector - Interstate; 17 Minor Collector - Interstate; 19 Local - Interstate

Speed Zones
25 30 35 40 45 50 55 60 65

Curves: Left; Right

Grades: grade up; grade down

Road Widths (ft)

Traffic Counters (counter ID)

AADT (count)

Crash Locations: Fatal; Injury; Property Damage Only; Unknown Crash Type

Mileage by Functional Class By Sheet

028-4	2 - Rural - Principal Arterial	9.000

Total Mileage: 9.000 mi

Mileage by Town By Sheet

LUNENBURG - U002-0514		9.0 of 9.039

Total Mileage: 9.0 mi

DISTRICT	TOWN	Date: 05/22/14	ROUTE
7	LUNENBURG	1 of 2 TWN mileage: 0.0 to 9.0	US-2 ETE mileage: 130.729 to 139.729
