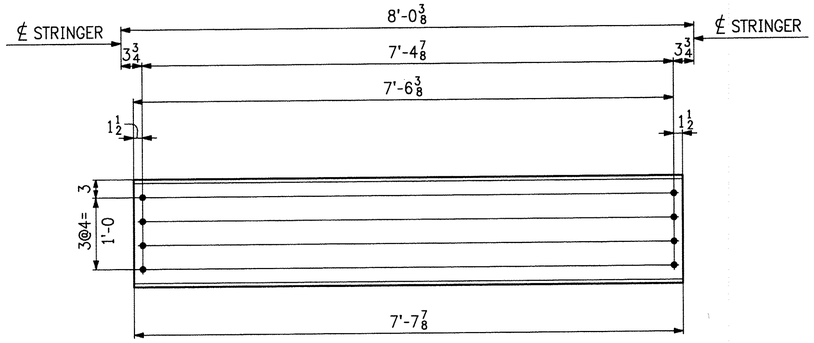

12 ~ DIAPHRAGMS ~ 4D1



8 ~ BLOCKOUT PLATES ~ 4MS1

ABM INFO		SHIP	BILL OF MATERIAL						JOB No.	REV.
PAGE	LINE	MARK	QTY.	MARK	MATERIAL	LENGTH FT.	LENGTH IN.	REMARKS	WEIGHT	PROCUREMENT NOTES
					DIAPHRAGMS					
1	17	4D1	12		MC18 42.7	7	7 7/8	M270-50W	326.9 lbs.	
					BLOCKOUT PLATES					
1	14	4MS1	8		PL 1/4 x 10	2	5	M270-50W	20.6 lbs.	

NOTES:

HOLES: 15/16 ø
BOLTS: NONE
MAT'L: M270-50W
PAINT: NONE
FOR GENERAL NOTES & TYPICAL DETAILS SEE SHT. GN1

REV.	DATE	DESCRIPTION

QTY.	DATE	ISSUED TO	FOR
8	3/9/06	F W Whitcomb	Approval

EASTERN BRIDGE LLC
RURAL RTE 2, BOX 302
CLAREMONT, NH 03743
603-542-5202

PROJECT:	T.H. NO. 1 OVER SAXTONS RIVER (BRIDGE NO. 16G)
LOCATION:	PROJ. NO. TH2-0104 GRAFTON, VERMONT
ENGINEER:	VANASSE HANGEN BRUSTLIN,INC.
CUSTOMER:	FRANK W. WHITCOMB CONST.
DRAWING TITLE:	STRINGER ~ 3S4A
DRAWN BY: CPM 3-3-06	JOB NUMBER: 6065
CHECKED BY: 3-6-06	SHEET NUMBER: 4

DPH-823

Sheet 4 - Plotted: 03/07/2006 @ 14:16 (HEATHER)
