File 5.1.2

Contractor:	Don Weston Exc.		
Job Name:	Bristol HES 021-1 (28)		
Location:	Bristol, VT		
Job #	025-15	Date:	3/4/2015

CAMP Precast Concrete Products, Inc.
78 Precast Road, Milton, VT 05468
Phone (802) 893-2401 Fax (802) 893-1542

Product I.D. D.I.

Size: **4' x 4'**

Invert: **No** Ladders: **No** Coating: **No** Access Size: **24" x 24"**

Cast Iron / Hatch: **24"x24"x6" High Neenah R-3405-A Frame & Type "D" Checkerboard Grate**

Rim:	568.82			Riser#1:		Riser#4:		
Inv. Out:	565.30	Cover:	8" Spec.	Riser#2:		Riser#5:		
Diff:	3.52	Base:	4'	Riser#3:		Riser#6:		
Sump:	2.00							
Gross V.F.:	5.52	Angle	0					
C.I. Height:	0.50	Boot:	S206-24L					
Net V.F.:	5.02	Dist. Up:	21"					
Brick Space:	0.35	Pipe Type:	HDPE					
Actual V.F.	4.67	Pipe Size:	18"					

Quality Control

Prepour

Form Cleaning: Form Release:
Rein. Steel: VT AOT Job Form Closure:
Block Out: Rein. Size:
Comments: Q.C. by/date:

Postpour

Finish: Bricking:
Invert: Ladders:
Coating: Boots:
Comments: Q.C. by/date:

Special Info. / Comments: VT AOT Job, 8" Thick Base Slab

Mold #: YDS³ Flat Top. No Tongue. 1@18" HDPE Adapter Wt.

FLIPPED **BASE**
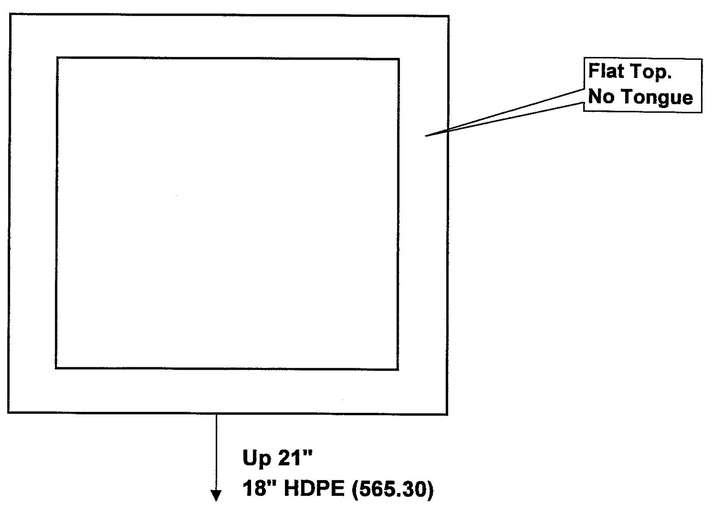
APPROVED
