ASSEMBLY
11

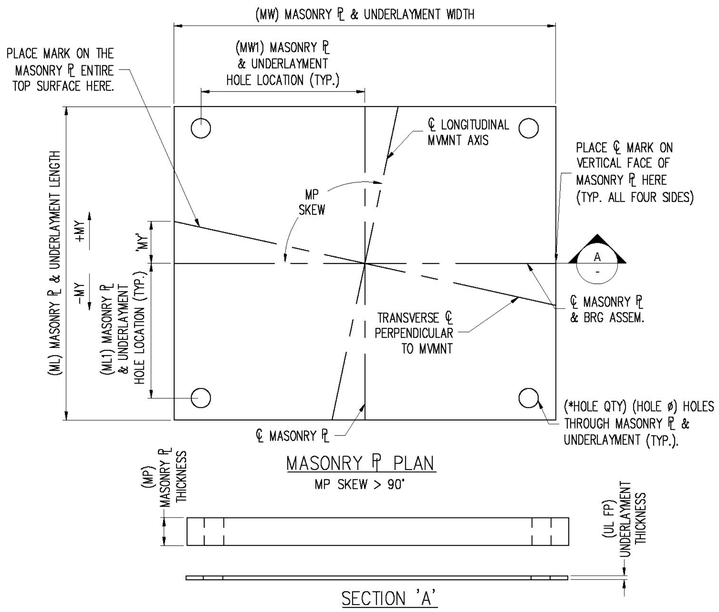

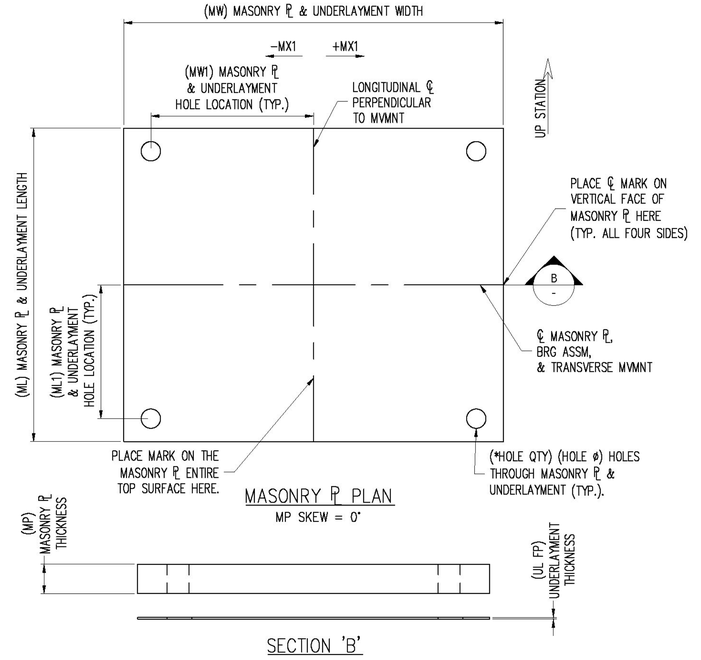

MASONRY PLATE SCHEDULE (DMG)

ASSEM MK	PIECE MK	QTY	MP	MW	ML	MW1	ML1	*HOLE QTY	HOLE ø	MP SKEW	MY	MX1	UL MK	UL FP	UL MATERIAL	MASONRY PL MATERIAL
11A	11mp1	3	1.000	31.750	14.500	13.000	4.375	4	1.875	+97.2°	+2.005		11FA (11fp1)	0.125	VT 731.02	A709 GR. 50 OR 50W
11B	11mp2	2	1.000	31.750	14.250	13.000	4.250	4	1.875	+0.0°		+0.000	11FB (11fp2)	0.125	VT 731.02	A709 GR. 50 OR 50W

* PER PLATE
SEE SHT. 11 FOR ASSEMBLY & DESIGN INFORMATION.
SEE SHT. 12, 13, & 15 FOR ADDITIONAL SUB-ASSEMBLY DETAILS.
ALL DIMENSIONS IN INCHES UNLESS OTHERWISE NOTED

Vermont Agency of Transportation
RECEIVED
Morristown BRS 0240(3)S Disc Bearing Submittal_Rev 2_Approved 12.8.17.pdf
CK'D BY CLC OK'D BY CWC
December 1, 2017
RESUBMIT NO Approved
BY C. CARLSON DATE 12/08/17

REV.	DESCRIPTION	DATE	DET.	CK'D.
1	REVISED ANCHOR HARDWARE DIAMETER FROM 1.25" TO 1.5"	12/1/17	DSB	KTG

D.S. BROWN
A GIBRALTAR INDUSTRIES COMPANY
THE D.S. BROWN COMPANY
300 E. CHERRY STREET
NORTH BALTIMORE, OHIO 45872
419.257.3561
FAX: 419.257.0332
WWW.DSBROWN.COM

	ITEM	QUANTITY
LOCATION — VT RTE 15A MAJOR COLLECTOR	–	–
BRIDGE — NO. 1	–	–
PROJECT — BRS 0240(3)S & STP HES 030-2(28)	–	–
PROJECT NAME — MORRISTOWN	–	–
P.O. NO. — K1619	–	–
DESIGNER — T.Y. LIN INTERNATIONAL	–	–
CUSTOMER — WINTERSET, INC.	–	–
	–	–
	–	–

DESCRIPTION: DMG UNI-DIRECTIONA HLMR SUB-ASSEMBLY DETAILS
LAMOILLE CO., VT

SCALE	DRAWN BY	CHECKED BY	DATE	
N.T.S.	DA	KTG	11/17	–

PROJECT NUMBER	PROJECT CODE	RELEASE	SHEET
53146	1114	1	14
