CONSTRUCTION OPERATIONS TRAFFIC PROTECTION PLAN

EXISTING GUARDRAIL INVENTORY								PROTECTION PLAN	
BEGIN STA.	END STA.	POS.	LENGTH (LF)	RETAIN/REPLACE (Y/N)	APPROX. OFFSET DISTANCE FROM PROPOSED CENTERLINE TO FACE OF EXISTING RAIL (LF)	EXISTING RAIL TYPE (POST AND BARRIER)	ASSESSED CONDITION (GOOD/FAIR/POOR)	CONSTRUCTION CONDITION	900.640 BARRIER FOR TEMPORARY TRAFFIC PROTECTION (LF)
SHARON - ROUTE 14									
323+00	333+03	LT	1003.0	Y	13-14	STEEL W-BEAM	GOOD	REMOVE AND RESET TO FACE OF RAIL 14 FEET OFF OF PROPOSED CENTERLINE, STA. 323+00 - STA. 333+00, BEFORE CONSTRUCTING SIDE SLOPES.	1000
333+50	343+00	LT	950.0	Y	13-14	STEEL W-BEAM	GOOD	REMOVE AND RESET TO FACE OF RAIL 14 FEET OFF OF PROPOSED CENTERLINE, STA. 334+00 - STA. 343+00, BEFORE CONSTRUCTING SIDE SLOPES.	950
								TOTAL =	1950

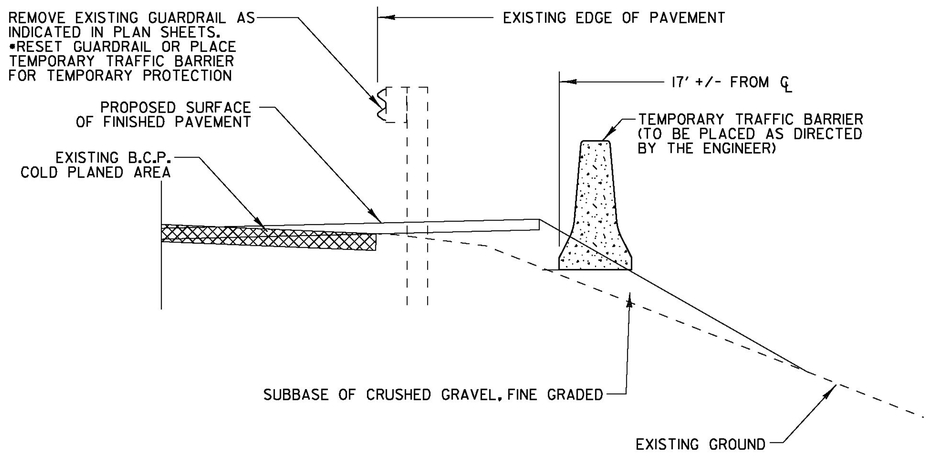

• PAYMENT FOR THIS WORK WILL BE MADE UNDER ITEM 900.640 SPECIAL PROVISION (BARRIER FOR TEMPORARY TRAFFIC PROTECTION)

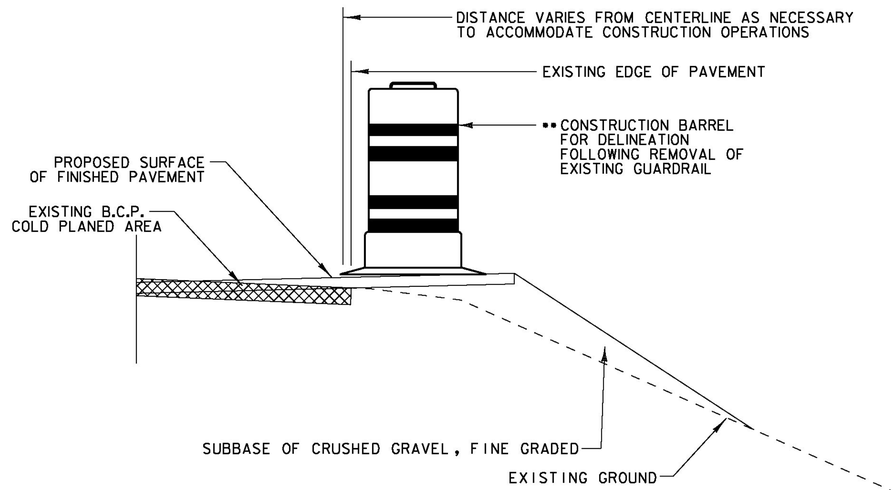

** PAYMENT FOR THIS WORK WILL BE INCLUDED IN THE UNIT PRICE BID FOR CONTRACT ITEM 641.10 "TRAFFIC CONTROL"

TEMPORARY PROTECTION AND DELINEATION DETAILS FOR ROADSIDE HAZARDS DURING CONSTRUCTION

NOT TO SCALE

PROJECT NAME:	SHARON
PROJECT NUMBER:	ER STP 0147(20)

FILE NAME: z12c410.dgn	PLOT DATE: 3/31/2015
PROJECT LEADER: J. TUCKER	DRAWN BY: B. MACK
DESIGNED BY: B. BRESLEND	CHECKED BY: A. SANZ
CONST. OPER. TRAFF. PROT. PLAN	SHEET 66 OF 66
