IDENTIFICATION NUMBER	SIZE OF SIGN WIDTH (IN)	SIZE OF SIGN HEIGHT (IN)	TEXT	NUMBER OF SIGNS REQ'D	REMARKS	COLOR
M1-5	30	24	VERMONT 100	43*	SEE NOTE 2	VTRANS STD E-136B
M3-1	24	12	NORTH	23*	SEE NOTE 2	VTRANS STD E-136B
M3-3	24	12	SOUTH	20*	SEE NOTE 2	VTRANS STD E-136B
G20-2	36	18	END ROAD WORK	3	MOUNT ON ONE POST	LEGEND BLACK BACKGROUND ORANGE ••
M4-8	24	12	DETOUR	42*	MOUNT ABOVE THE M3-1 OR M3-3	LEGEND BLACK BACKGROUND ORANGE ••
M4-8A	24	18	END DETOUR	2	MOUNT ON ONE POST	LEGEND BLACK BACKGROUND ORANGE ••
M5-1L	21	15		4	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M5-1R	21	15		2	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M5-2R	21	15		0	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M6-1L	21	15		1	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M6-2L	21	15		0	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M6-2R	21	15		1	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••
M6-3	21	15		34*	MOUNT BELOW THE M1-5	LEGEND BLACK BACKGROUND ORANGE•••

IDENTIFICATION NUMBER	SIZE OF SIGN WIDTH (IN)	SIZE OF SIGN HEIGHT (IN)	TEXT	NUMBER OF SIGNS REQ'D	REMARKS	COLOR
R11-2	48	30	ROAD CLOSED	3	MOUNT ON TYPE III BARRICADE (MOD.)	LEGEND BLACK BACKGROUND WHITE •••
SP-1	60	30	ROAD CLOSED 1 MILE AHEAD NO THRU TRAFFIC	2	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND WHITE •••
SP-2	60	30	ROAD CLOSED 3 MILES AHEAD NO THRU TRAFFIC	1	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND WHITE •••
W20-2	48	48	DETOUR AHEAD	2	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••
W20-3	48	48	ROAD CLOSED 1000FT	4	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••
W20-3	48	48	ROAD CLOSED 500 FT	2	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••
W20-3	48	48	ROAD WORK AHEAD	5	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••
SP-3	42	66	BRIDGE CLOSED VT 100 WESTON 2.4 MILES NORTH OF WESTON VILLAGE	11	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••
W20-3	48	48	ROAD CLOSED 200 FT	1	MOUNT ON TWO POSTS	LEGEND BLACK BACKGROUND ORANGE ••



SP-1 & SP-2
NOT TO SCALE

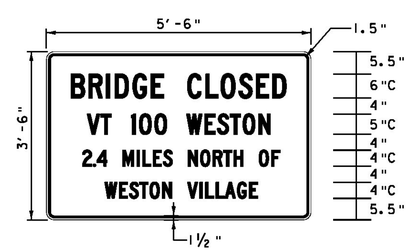

SP-3
NOT TO SCALE

NOTES:

1. PAYMENT OF ALL DETOUR SIGNS AND REQUIRED SIGN POSTS WILL BE MADE UNDER ITEM 641.10, "TRAFFIC CONTROL".
2. THE M1-5, M3-1, AND THE M3-3 SIGNS SHALL BECOME PROPERTY OF THE STATE AFTER THEY ARE REMOVED FROM THE DETOUR. THE CONTRACTOR SHALL DELIVER THE SIGNS TO THE STATE GARAGE IN THE TOWN OF LONDONDERRY. ALL COSTS ASSOCIATED WITH PROVIDING SIGNS TO THE STATE WILL BE CONSIDERED INCIDENTAL TO ITEM 641.10, "TRAFFIC CONTROL".
3. ONE WEEK PRIOR (7 DAYS) TO CONSTRUCTION ON THE BRIDGE, PORTABLE CHANGEABLE MESSAGE SIGNS (PCMS) MESSAGES 1 AND 2 WILL BE DISPLAYED AT THE BRIDGE AND PCMS MESSAGES 3, 4, AND 5 WILL BE DISPLAYED REGIONALLY.
4. DURING THE BRIDGE CLOSURE, PCMS SHALL READ MESSAGES 6 AND 7 REGIONALLY.

MESSAGES FOR PORTABLE CHANGEABLE MESSAGE SIGNS (PCMS) - AT BRIDGE

ONE WEEK PRIOR

	MESSAGE 1	MESSAGE 2	
(ROUTE) ***	VT 100	MMMM DD	(DATE) **
	BRIDGE	TO	
	CLOSED	MMMM DD	(DATE) **

MESSAGES FOR PORTABLE CHANGEABLE MESSAGE SIGNS (PCMS) - REGIONAL DETOUR

ONE WEEK PRIOR

	MESSAGE 3	MESSAGE 4	MESSAGE 5	
(ROUTE) ***	VT 100	NORTH OF	MMMM DD	(DATE) **
	BRIDGE	WESTON	TO	
	CLOSED	VILLAGE	MMMM DD	(DATE) **

DURING BRIDGE CLOSURE

	MESSAGE 6	MESSAGE 7
(ROUTE) ***	VT 100	NORTH OF
	BRIDGE	WESTON
	CLOSED	VILLAGE

** - MONTH SHALL BE SPELLED OUT - JUNE 10 NOT 06/10

*** - ROUTE VT 100 SHALL SPECIFY N (NORTH) OR S (SOUTH) AS APPROPRIATE FOR THE DETOUR.

* = NUMBER OF SIGNS REQ'D ASSUMING APPROXIMATELY 3 LOCATIONS OF CONFIRMATORY ROUTE MARKER ASSEMBLY DETAIL
** = SIGN BACKGROUND SHALL BE RETROREFLECTIVE FLUORESCENT
*** = SIGN BACKGROUNDS SHALL BE RETOREFLECTIVE

PROJECT NAME: WESTON
PROJECT NUMBER: BF 013-2(13)

FILE NAME: z13b076detour_dts.dgn
PROJECT LEADER: S.E. BURBANK
DESIGNED BY: J.J. WESTCOTT
TRAFFIC CONTROL PLAN (6 OF 6)

PLOT DATE: 10/2/2015
DRAWN BY: J.J. WESTCOTT
CHECKED BY: S.E. BURBANK
SHEET 24 OF 68

VHB 57673
