Route Log Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Unit with questions or concerns.

DISTRICT	TOWN	ROUTE
	[u'I093-0000']	I-93

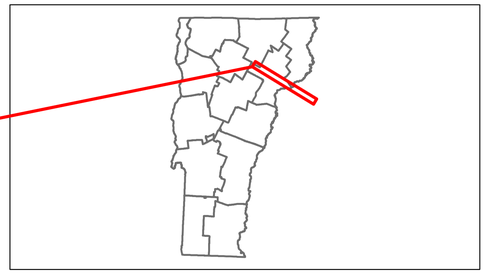

Base Map

1 in = 2 miles

Stick Diagram

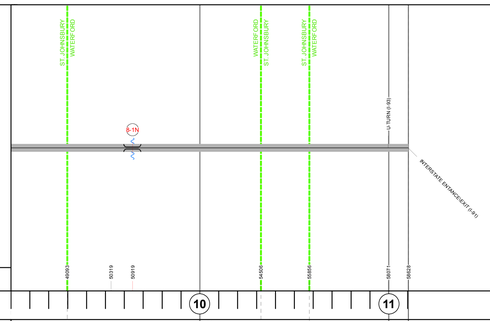

Road Widths

Travellane	24
Roadway	38
Lane Count	2
Base	Two 2 1/2" Plant Mix Base Courses
Subbase	24" Crushed Stone

Curves

Grades

Historic Projects

1999 IM 093-1(9)
1982 I 93-1(3) C/3

Maintenance Garage

District 7 - St Johnsbury Garage

Traffic Counters

Functional Class

1

Speed Zone

AADT Counts

2012	5900
2011	5900
2010	5900
2009	5700
2008	5400

Crash Locations

2012
2011
2010
2009
2008

DESCRIPTION BLOCK

Culvert 8-1N:
Culvert - 1982
Structure No. 3000938-1N03161
Length: 6'
Under Clearance: 4.0'
Facility Carried: I93
Bridge Type: ACCGMPPA
Features Intersected: BROOK
Maintenance: State

Historic Projects

Retreatment, Resurface, Unknown, Bituminous Mix, Skinny Mix, Bituminous Seal, Bituminous Concrete, Bituminous Macadam, Cold Plane and Bituminous Concrete, Concrete, Gravel, Surface Treated Gravel, Plant Mix, Reclaimed Base and Bituminous Concrete

Functional Class

1 - Rural - Principal Arterial - Interstate
7 - Rural - Principal Arterial - Other
12 - Rural - Minor Arterial
17 - Rural - Major Collector
2 - Urban - Principal Arterial - Interstate
8 - Urban - Principal Arterial - Other
14 - Urban - Minor Arterial
19 - Urban - Major Collector
6 - Rural - Minor Collector
11 - Urban - Local
16 - Rural - Local

Speed Zones

SPEED LIMIT 25, SPEED LIMIT 30, SPEED LIMIT 35, SPEED LIMIT 40, SPEED LIMIT 45, SPEED LIMIT 50, SPEED LIMIT 55, SPEED LIMIT 60, SPEED LIMIT 65

Curves

curve left
curve right

Grades

grade up
grade down

Road Widths

(ft)

Traffic Counters

(counter ID)

AADT

(count)

Crash Locations

Fatal
Injury
Property Damage Only
Unknown Crash Type

Mileage by Functional Class By Sheet

93-1	1 - Rural - Principal Arterial - Interstate	2.104

Total Mileage: 2.104 mi

Mileage by Town By Sheet

[u'I093-0000'] - I093-0000	2.104 of 11.104

Total Mileage: 2.104 mi

DISTRICT	TOWN	Date: 11/14/13	ROUTE
	[u'I093-0000']	2 of 2 TWN mileage: 9.0 to 11.104	I-93 ETE mileage: 0.0 to 11.104
