Route Log Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Unit with questions or concerns.

DISTRICT	TOWN	ROUTE
	ETE	I-91

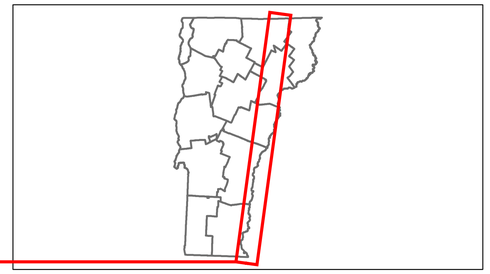

Base Map

1 in = 7 miles

Stick Diagram

- Town Boundary
- Village/UC Boundaries
- District Boundaries
- State/Town Highway Change
- Divided Highway Limits
- Ghost Section Boundary
- FAU Limits
- Streams
- Town Center
- Primary Structures
- Secondary Structures
- Stations (Feet)
- Railroad Crossings
- Divided State Highway
- State Highway
- Divided Class 1 Town Highway
- Class 1 Town Highway

Scale: 1 INCH = 2000 FEET

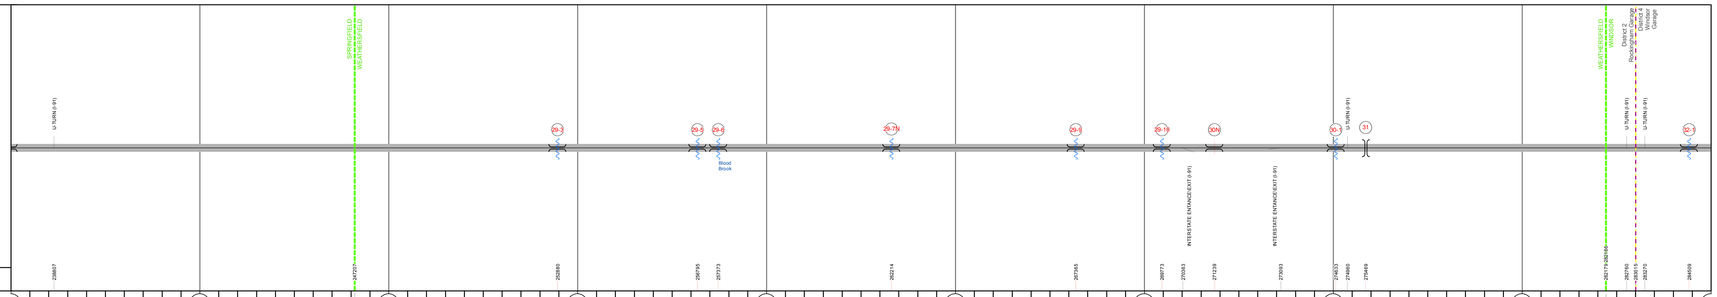

Road Widths

Travellane	24
Roadway	38
Lane Count	2
Base	Two 2 1/2" Cr. Stone Base Courses
Subbase	24" Crushed Rock

Curves

Grades

-3.2, +4.2, -5.3, +4, -2, +2.2, -5, -3, -4.8, +2.5, -6, +2, -3.8, +2.8, -3.7

Historic Projects

1989: IR 091-1(15)
2011: IM CULV(17)
1990: IR DECK(27)
1988: IR 091-1(19)
1979: IR F 91-1(4)
1981: IR 91-1(5)
1965: I 91-1(20) C/1
1965: I 91-1(20) C/2
1965: I 91-1(20) C/3
1965: I 91-1(21) C/1

Maintenance Garage

District 2 - Rockingham Garage

Traffic Counters

861075

Functional Class

1

Speed Zone

AADT Counts

	46	48	52
2012	10200	13000	
2011	11000	13700	
2010	11800	14300	
2009	11700	14400	
2008	11600	14400	

Crash Locations

2012, 2011, 2010, 2009, 2008

DESCRIPTION BLOCK

Culvert 29-3:
Culvert - 1965
Structure No. 30009129-314201
Length: 9'
Under Clearance: 10.0'
Facility Carried: I91
Bridge Type: MULTI PLATE PIPE
Features Intersected: BROOK
Maintenance: State

Culvert 29-5:
Culvert - 1965
Structure No. 30009129-514201
Length: 6'
Under Clearance: 6.5'
Facility Carried: I91
Bridge Type: CGMPP
Features Intersected: BROOK
Maintenance: State

Culvert 29-6:
Culvert - 1965
Structure No. 30009129-614201
Length: 9'
Under Clearance: 10.0'
Facility Carried: I91
Bridge Type: CGMPP
Features Intersected: BLOOD BROOK
Maintenance: State

Culvert 29-7N:
Culvert - 1965
Structure No. 300091297N14201
Length: 8'
Under Clearance: 8.0'
Facility Carried: I91
Bridge Type: CGMPP
Features Intersected: BROOK
Maintenance: State

Culvert 29-9:
Culvert - 1965
Structure No. 30009129-914201
Length: 6'
Under Clearance: 6.0'
Facility Carried: I91
Bridge Type: ACCGMP
Features Intersected: CATTLEPASS
Maintenance: State

Culvert 29-10:
Culvert - 1965
Structure No. 200091291014202
Length: 21'
Facility Carried: I 00091 ML
Bridge Type: TWIN CELL RC BOX
Features Intersected: MILL BROOK
Maintenance/Ownership: State

Bridge 30N:
Stringer/multi-beam or girder - 1965
Structure No. 200091030N14202
Length: 219'
Width: 30.0'
Under Clearance: 15.0'
Facility Carried: I 00091 ML
Bridge Type: 3 SP CONT ROLLED BM
Features Intersected: I 91 OVER VT 131
Surface: Bituminous
Maintenance/Ownership: State

Culvert 30-1:
Culvert - 1966
Structure No. 30009130-114201
Length: 8'
Under Clearance: 8.5'
Facility Carried: I91
Bridge Type: CGMPP
Features Intersected: BROOK
Maintenance: State

Bridge 31:
Stringer/multi-beam or girder - 1965
Structure No. 20142000D3114201
Length: 251'
Height: 0.0'
Weight Limit: 0
Facility Carried: TR 00037
Bridge Type: 4 SP ROLLED BEAM
Features Intersected: I 91 UNDER TH NO 37

Culvert 32-1:
Culvert - 1966
Structure No. 30009132-114231
Length: 6'
Under Clearance: 6.5'
Facility Carried: I91
Bridge Type: CGMPP
Features Intersected: BROOK
Maintenance: State

Historic Projects: Retreatment, Resurface, Unknown, Bituminous Mix, Skinny Mix, Bituminous Seal, Bituminous Concrete, Bituminous Macadam, Cold Plane and Bituminous Concrete, Concrete, Gravel, Surface Treated Gravel, Plant Mix, Reclaimed Base and Bituminous Concrete

Functional Class: 1, 7, 12, 17, 2, 8, 14, 19, 6, 11, 16

Speed Zones: 25, 30, 35, 40, 45, 50, 55, 60, 65

Curves: Left, Right

Grades: grade up, grade down

Road Widths (ft)

Traffic Counters (counter ID)

AADT (count)

Crash Locations: Fatal, Injury, Property Damage Only, Unknown Crash Type

Mileage by Functional Class By Sheet

91-1	1 - Rural - Principal Arterial - Interstate	9.000

Total Mileage: 9.000 mi

Mileage by Town By Sheet

ETE - I091-0000	9.0 of 177.432

Total Mileage: 9.0 mi

DISTRICT	TOWN	Date: 05/21/14	ROUTE
	ETE	6 of 20 TWN mileage: 45.0 to 54.0	I-91 ETE mileage: 45.0 to 54.0
