Route Log and Progress Chart

DRAFT

Please Note: Errors and Omissions May Exist.
Contact the VTrans Mapping Section with questions or concerns.

DISTRICT	TOWN	ROUTE
3	BRIDPORT	VT-125



VERMONT 125

Base Map

1 in = 0.8 miles



Stick Diagram

- Town Center
- Intersecting State Routes (excl. ramps/approaches)
- Other Intersecting Highways, Ramps, Approaches
- Railroad Crossings
- Primary Structures
- Secondary Structures
- Divided State Highway
- State Highway
- Divided Town Highway
- Town Highway
- Streams (Hydraulic Structure)
- Town Boundary
- District Boundaries
- State/Town Highway Change
- Divided Highway Limits
- Ghost Section Boundary
- Federal Urban Area Limits

Scale: 1 INCH = 2,000 FEET

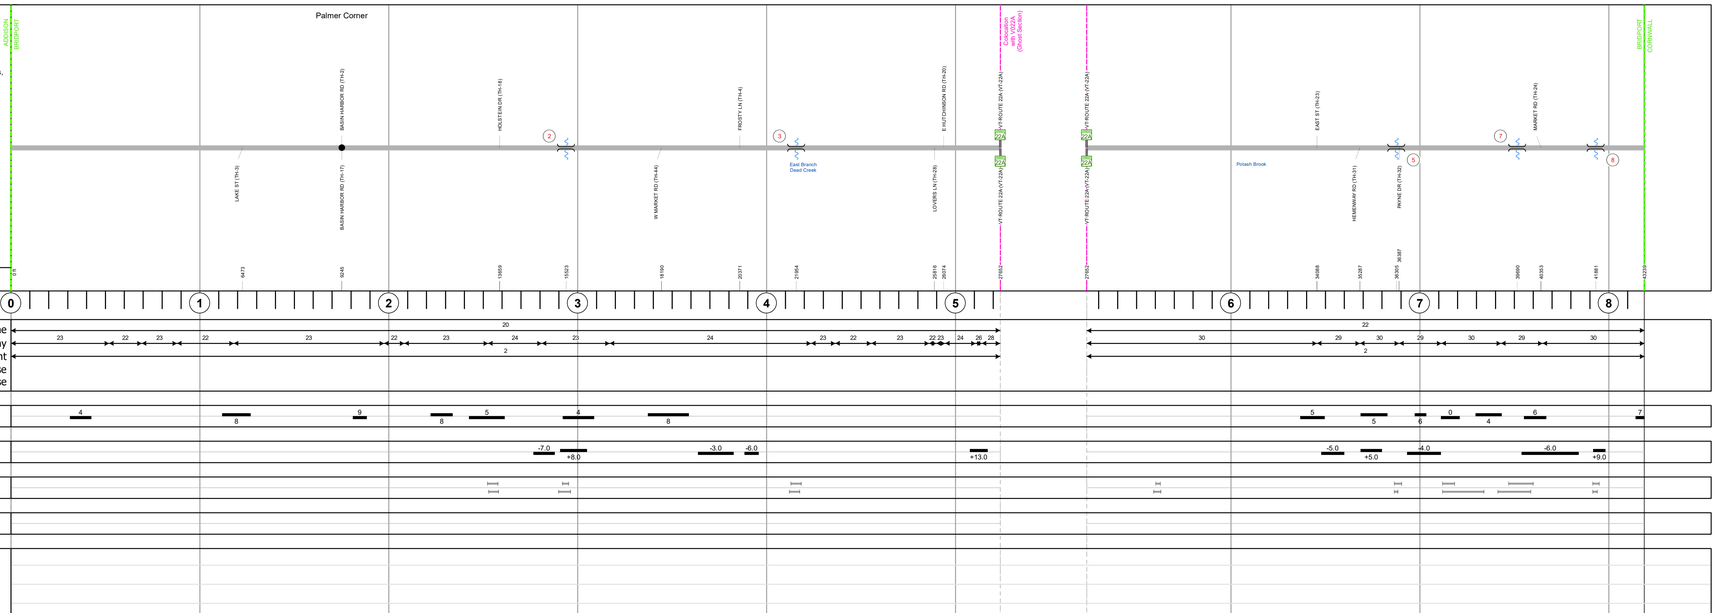

Road Widths

Travellane / Roadway / Lane Count / Base / Subbase

Curves

Grades

Guardrails

Rumblestrips

Historic Projects

- 2001: BHF 0172(7)S
- 1996: District
- 2015: STP CULV(29)
- 1977: RS 0172(2)
- 1996: STP 9471(1)S
- 1970: Unknown
- 1985: RS 0172(5)
- 1954: APP 130/54
- 1970: Unknown
- 1936: PWA 1020-P
- 1946: ST
- 1956: ST 69-L
- 1949: S 69(1)

Maintenance Garage

District 3 - DMF Maintenance Middlebury Garage

Speed Zone

Functional Class

5

National Highway System

Limited Access Highway

Customer Service Level

Local Connector

Traffic Counters

A144

AADT

2022	1226 / 1853
2021	1517 / 2051
2020	1339 / 1810
2019	1581 / 2137
2018	1600 / 1700 / 2100

Crash Locations

(Incomplete) 2023 / 2022 / 2021 / 2020 / 2019

STRUCTURE DESCRIPTIONS

Bridge 2:
Culvert - 2015
Structure No. 300172000201021
Length: 20'
Under Clearance: 10.0'
Weight Limit: 0
Facility Carried: VT125
Structure Type: SEGMENTAL RC BOX
Features Intersected: WEST BR DEAD CREEK
Inspection Date: 11/2018
Maintenance: State

Bridge 3:
Other - 1936
Structure No. 200172000301022
Length: 49'
Height: 100.0'
Width: 25.0'
Weight Limit: 0
Facility Carried: VT 00125 ML
Structure Type: T-BM WID W PS SLAB
Features Intersected: E. BR. DEAD CREEK
Surface: Bituminous
Inspection Date: 5/2023
Maintenance/Ownership: State

Bridge 5:
Culvert - 2015
Structure No. 300172000501021
Length: 22'
Under Clearance: 7.0'
Weight Limit: 0
Facility Carried: VT125
Structure Type: SEGMENTAL RC BOX
Features Intersected: DRAINAGE BROOK
Inspection Date: 11/2018
Maintenance: State

Bridge 7:
Culvert - 1945
Structure No. 300172000701021
Length: 12'
Under Clearance: 12.0'
Weight Limit: 0
Facility Carried: VT125
Structure Type: CGMPP
Features Intersected: BROOK
Inspection Date: 11/2018
Maintenance: State

Bridge 8:
Culvert - 1949
Structure No. 300172000801021
Length: 8'
Under Clearance: 7.0'
Weight Limit: 0
Facility Carried: VT125
Structure Type: CGMPP
Features Intersected: DRAINAGE BROOK
Inspection Date: 12/2018
Maintenance: State

Historic Projects

Unknown / Retreatment / Resurface / Bituminous Mix / Skinny Mix / Bituminous Seal / Bituminous Concrete / Bituminous Macadam / Cold Plane and Bituminous Concrete / Concrete / Gravel / Surface Treated / Gravel / Plant Mix / Reclaimed Base and Bituminous Concrete

Indicated plans available - http://vtransmap01.aot.state.vt.us/rp/dpr/Diwebstore/

Functional Class

1 - Interstate System / 2 - Other Freeways and Expressways / 3 - Principal Arterial / 4 - Minor Arterial / 5 - Major Collector / 6 - Minor Collector

Speed Zones

SPEED LIMIT 25 / 30 / 35 / 40 / 45 / 50 / 55 / 60 / 65

Curves (degrees) Left / Right

Grades (percent) grade up / grade down

Road Widths (ft)

Traffic Counters

Continuous (CTC) / Weigh-In-Motion (WIM) / Short-Term, Scheduled / Short-Term, Unscheduled (counter ID)

AADT (AADT)

Crash Locations

Fatal / Injury / Property Damage Only / Unknown Crash Type

High Crash Locations (HCL's)

Sections (& Intersections)

HCL No.
1 - 100 (1 - 10) / 101 - 200 (11 - 20) / 201 - 300 (21 - 30) / 301 - 400 (31 - 40) / 401 - 800 (41 - 113)

Mileage by Functional Class By Sheet

0172	5 - Major Collector	8.189

Page Total Mileage: 8.189 mi

Mileage by Town By Sheet

BRIDPORT - V125-0102 Ghost Section - (VT-22A, MM 3.788 to 3.330)		8.189 of 8.189

Page Total Mileage: 8.189 mi

DISTRICT	TOWN	Date: 09/23/23	ROUTE
3	BRIDPORT	1 of 1 TWN mileage: 0.0 to 8.189	VT-125 ETE mileage: 1.854 to 10.043
