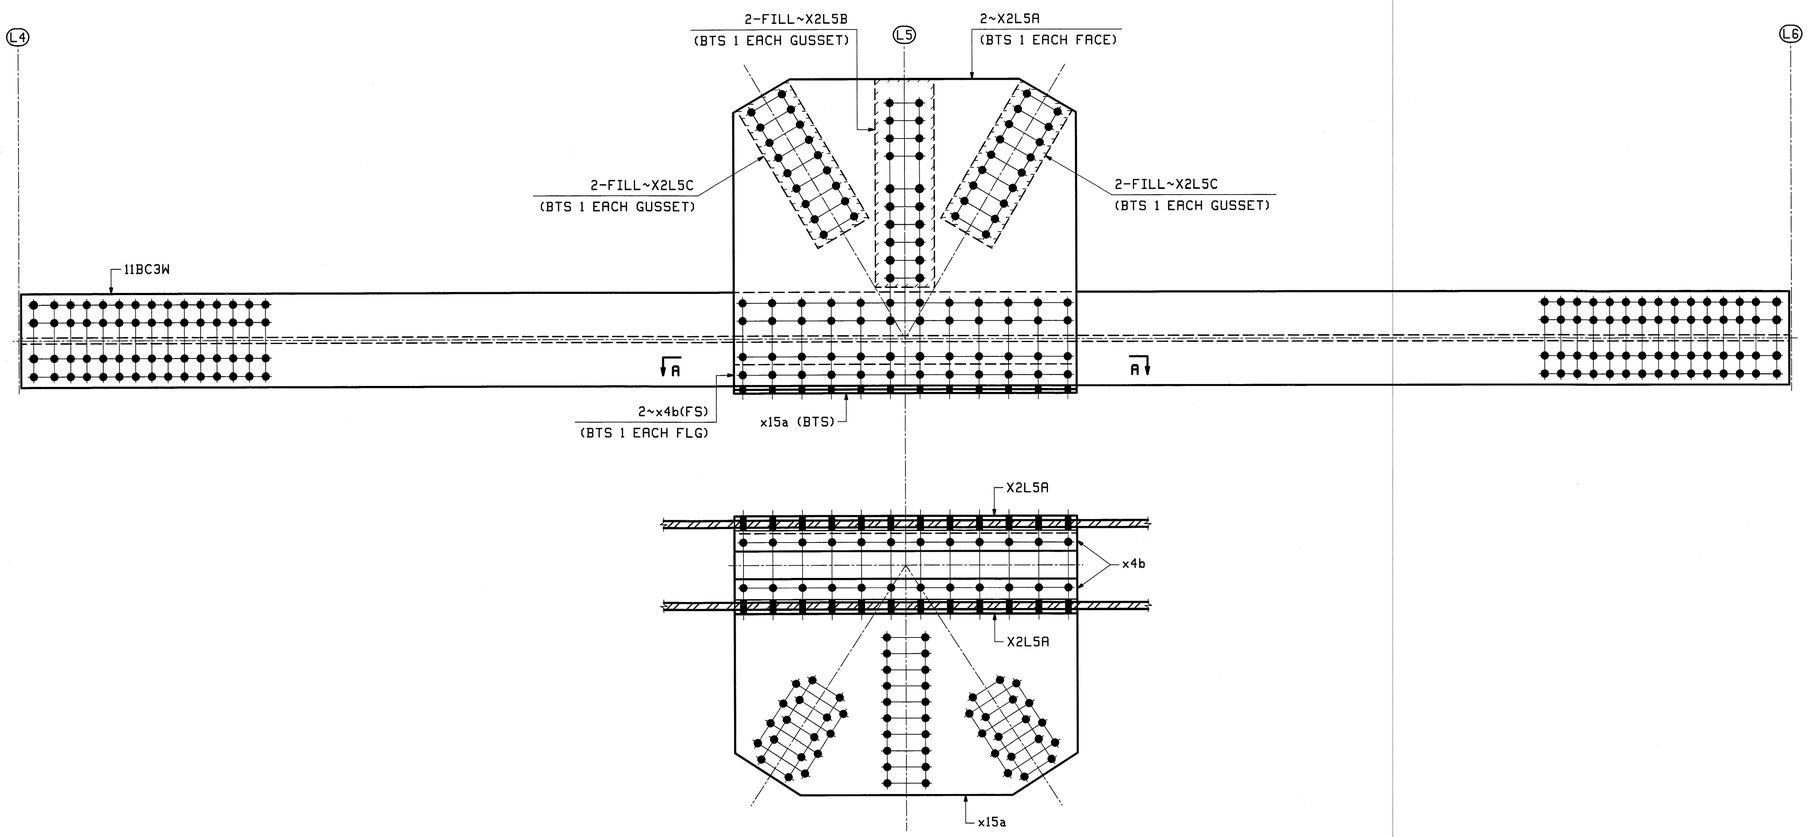

SECTION A-A

ONE ~ SHIPPING ASSEMBLY ~ 41L4L6W

(BOTTOM CHORD) (L4 - L6 WEST TRUSS, LOOKING WEST)

ABM INFO PAGE	ABM INFO LINE	SHIP MARK	QTY	MARK	MATERIAL	LENGTH FT	LENGTH INCHES	REMARKS	WT	PROCUREMENT NOTES
		41L4L6W	1		BTM CHORD SHIPPING ASS'Y				10076	
			1	11BC3W	BOTTOM CHORD					
1	R		2	X2L5A	PL $\frac{3}{4}$x51$\frac{1}{2}$	4	10	M270-50F2 (FCM)		
3	L		2	X2L5B	PL $\frac{9}{16}$x10	2	11$\frac{1}{16}$	FILL M270-50		
3	P		4	X2L5C	PL $\frac{9}{16}$x10	2	3	FILL M270-50		
3	C		2	x4b	L 4x4x$\frac{1}{2}$	4	10	M270-36		
2	K		1	x15a	PL $\frac{5}{8}$x44$\frac{5}{16}$	4	10	M270-50		

JOB NO. 498 | DRAWING NO. 41 | REV.

REV.	DATE	REMARKS	DWN	CHK	APVL	SHOP
0					NOV 30 2011	
					JAN 9 2012	

MATERIAL:	SURFACE PREP. & PAINT:	HOLES:	SHOP BOLTS:
M270-50 (UN)	HOT-DIP GALV.	$\frac{15}{16}$Ø (UN)	NONE

DESCRIPTION: SHIPPING ASSEMBLY (L4-L6 WEST)

CASCO BAY STEEL STRUCTURES, INC.
1 WALLACE AVE. PHONE (207) 780-6722
SOUTH PORTLAND, ME 04106 FAX. (207) 780-6726
TENSOR 3073

STRUCTURE: VT RTE 107 OVER WHITE RIVER	DRAWN: EEO	DATE: 11/21	
	CHK'D: PCP	DATE: 11/23	
LOCATION: BETHEL, VT.	JOB NO. 498	DWG NO. 41	
PROJ NO. BRF 022-1(14)		REV. △	
CUSTOMER: BECK & BELLUCCI			

Vermont Agency of Transportation
RECEIVED
CK'D BY M.C.L. OK'D BY S.S.S.
January 10 2012
RESUBMIT APPROVED ✓
BY J. LACROIX DATE 01-12-2012

EEO Tue, Nov 29, 2011 03:13:13 PM /users/jobs/3073.41.dwg
